
SOUTH TERRACE – SCHEDULE UPDATE

TO: WACO HOUSING AUTHORITY
FROM: BRINSHORE DEVELOPMENT - TEXAS
SUBJECT: CONSTRUCTION UPDATE
DATE: 10/27/2021

Attached is a schedule update from J4 dated October 19. Brinshore reviewed and has provided a summary of the expected completion dates. This list does not include units already accepted or pending final acceptance. 5 units are pending final acceptance this week.


An updated schedule has been provided but under review by Brinshore.

South Terrace


Completion Schedule Summary

		Keys Received	Completion Dates as of 10/19/21	Bldg Status	Notes
COMMUNITY CENTER			10/29/2021		
LAUNDRY BLDG					
1228 CARTER	J	N/A	11/11/2021	VACANT	
1230 CARTER		N/A			
221 LYNDON	J	N/A	11/29/2021	VACANT	
223 LYNDON		N/A			
217 LYNDON	J	N/A	11/18/2021	VACANT	
219 LYNDON		N/A			
1101 GURLEY	H	N/A	11/23/2021	VACANT	
1103 GURLEY		N/A			
303 KENNEDY	H	N/A	12/3/2021	VACANT	
305 KENNEDY		N/A			
309 KENNEDY	H	N/A	12/1/2021	VACANT	
311 KENNEDY		N/A			
2713 S 12TH ST	J	N/A	12/23/2021	VACANT	
2715 S 12TH ST		N/A			
301 KENNEDY	F	N/A	12/2/2021	VACANT	
308 KENNEDY	E	N/A	11/29/2021	VACANT	
1200 CARTER	J	N/A	12/7/2021	VACANT	
1202 CARTER		N/A			
121 LYNDON	J	N/A	12/6/2021	VACANT	
123 LYNDON		N/A			
1105 GURLEY	H	N/A	12/17/2021	VACANT	
1107 GURLEY		N/A			
1109 GURLEY		N/A		VACANT	
1111 GURLEY		N/A			
317 KENNEDY	F	8/10/2021	12/10/2021	VACANT	
2700 S 14TH ST	A	N/A	12/16/2021	VACANT	
2702 S 14TH ST		N/A			
2634 S 14TH ST	B	N/A	12/22/2021	VACANT	
2636 S 14TH ST		N/A			
2612 S 14TH ST	C	N/A	12/22/2021	VACANT	
2614 S 14TH ST		N/A			
204 KENNEDY	H	N/A	12/17/2021	VACANT	
206 KENNEDY		N/A			

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
1	South Terrace	95 days?	Mon 8/16/21	Fri 12/24/21			52%
2	Building 173	64 days	Mon 8/16/21	Thu 11/11/21			71%
3	Unit 1228/1230 Carter Type J	64 days	Mon 8/16/21	Thu 11/11/21			71%
4	Receive possession of Unit	1 day	Mon 8/16/21	Mon 8/16/21		J4 Development	100%
5	Walk unit to verify existing conditions & MEP systems are working	3 days	Tue 8/17/21	Thu 8/19/21	4	J4 Development	100%
6	Submit 10 day abatement notice	10 days	Tue 8/17/21	Mon 8/30/21	4	ARC	100%
7	Electrical Demo	1 day	Fri 8/20/21	Fri 8/20/21	5	DPE	100%
8	HVAC Demo	1 day	Fri 8/20/21	Fri 8/20/21	5	3 C Mechanical	100%
9	Plumbing Demo	1 day	Fri 8/20/21	Fri 8/20/21	5	Streamline	100%
10	Fascia Demo & Install New	2 days	Tue 8/17/21	Wed 8/18/21	4	Sekresa	100%
11	New Roof Demo & Install New	2 days	Thu 8/19/21	Fri 8/20/21	10	Texas Built Roofing	100%
12	Interior Soft Demo	2 days	Fri 8/20/21	Mon 8/23/21	5	ARC	100%
13	Abatement	2 days	Tue 8/31/21	Wed 9/1/21	6	ARC	100%
14	Air Test	1 day	Thu 9/2/21	Thu 9/2/21	13	Choice Consulting	100%
15	Remaining Demo Walls & Ceilings	3 days	Fri 9/3/21	Tue 9/7/21	14	ARC	100%
16	Point up Existing Brick	2 days	Tue 8/17/21	Wed 8/18/21	4	Alamo Masonry	100%
17	Install Exterior Stone	3 days	Thu 8/19/21	Mon 8/23/21	16	Alamo Masonry	100%
18	Install new front door with construction lock	1 day	Tue 8/24/21	Tue 8/24/21	17	Rich Craft Doors	100%
19	Cedar Demo and/or building wrap install	2 days	Tue 8/24/21	Wed 8/25/21	17	Sherman	100%
20	Building Wrap Inspection	1 day	Thu 8/26/21	Thu 8/26/21	19	J4 Development	100%
21	Install Hardie Shake Siding	2 days	Fri 8/27/21	Mon 8/30/21	20	Sherman	100%
22	Install Hardie Soffit Board	1 day	Tue 8/31/21	Tue 8/31/21	21	Sekresa	100%
23	Prime Paint Building Exterior	1 day	Wed 9/1/21	Wed 9/1/21	22	Sekresa	100%
24	Finish Paint Building Exterior	1 day	Thu 9/2/21	Thu 9/2/21	23	Sekresa	100%
25	Pressure Wash Interior Existing CMU	1 day	Fri 9/3/21	Fri 9/3/21	24	Sekresa	100%
26	Install Vapor Barrier	2 days	Mon 9/6/21	Tue 9/7/21	25	Sekresa	100%
27	Install Foam Insulation	1 day	Wed 9/8/21	Wed 9/8/21	26	Sekresa	100%
28	Install Metal Strapping	1 day	Wed 9/8/21	Wed 9/8/21	26	Sekresa	100%
29	Install Ceiling Hat Channel	1 day	Wed 9/8/21	Wed 9/8/21	15	Sekresa	100%
30	Install Smoke Barrier	1 day	Wed 9/8/21	Wed 9/8/21	15	Sekresa	100%
31	Smoke Barrier Inspection	1 day	Thu 9/9/21	Thu 9/9/21	30	J4 Development	100%
32	Install Interior Wall Framing	1 day	Wed 9/8/21	Wed 9/8/21	15	Sekresa	100%
33	Install in Wall Blocking	1 day	Thu 9/9/21	Thu 9/9/21	32	Sekresa	100%
34	Install Plumbing R/I	1 day	Thu 9/9/21	Thu 9/9/21	32	Streamline	100%
35	Install HVAC R/I	2 days	Fri 9/10/21	Fri 9/10/21	29	3 C Mechanical	100%
36	Install Electrical R/I	2 days	Thu 9/9/21	Fri 9/10/21	32	DPE	100%
37	Install Data R/I	1 day	Thu 9/9/21	Thu 9/9/21	32	Entry Tech.	100%
38	Plumbing R/I Inspection	1 day	Fri 9/10/21	Fri 9/10/21	34	Streamline	100%
39	HVAC R/I Inspection	1 day	Mon 9/13/21	Mon 9/13/21	35	3 C Mechanical	100%
40	Electrical R/I Inspection	1 day	Mon 9/13/21	Mon 9/13/21	36	DPE	100%
41	J4 Frame Punch	2 days	Fri 9/10/21	Mon 9/13/21	33	J4 Development	100%
42	Wall Framing Inspection	1 day	Fri 9/10/21	Fri 9/10/21	33	J4 Development	100%
43	Install Batt Insulation	1 day	Mon 9/13/21	Mon 9/13/21	42	Sekresa	100%
44	Insulation Inspection	1 day	Tue 9/14/21	Tue 9/14/21	43	J4 Development	100%
45	Hang Drywall	3 days	Wed 9/15/21	Fri 9/17/21	44	Sekresa	100%
46	Skim Coat and/or T&T	3 days	Mon 9/20/21	Wed 9/22/21	45	Sekresa	100%
47	J4 Drywall Punch	2 days	Thu 9/23/21	Fri 9/24/21	46	J4 Development	100%
48	Install Interior Doors	2 days	Thu 9/23/21	Fri 9/24/21	46	Rich Craft Doors	100%
49	Install Closet Shelving	1 day	Thu 9/23/21	Thu 9/23/21	46	AZGS	100%
50	Interior Prime Paint	2 days	Thu 10/7/21	Fri 10/8/21	49	Sekresa	100%
51	Interior Finish Paint	3 days	Mon 10/11/21	Wed 10/13/21	50	Sekresa	100%
52	Install Cabinets	1 day	Fri 10/15/21	Fri 10/15/21	51FS+1 day	AZGS	100%
53	Field measure & cut Countertops	2 days	Mon 10/18/21	Tue 10/19/21	52	Authentic Granite	100%
54	Install Countertop	1 day	Wed 10/20/21	Wed 10/20/21	53	Authentic Granite	0%
55	Install Backplash Tile	3 days	Thu 10/21/21	Mon 10/25/21	54	Centex	0%
56	Install Bathroom Floor Tile	2 days	Thu 10/21/21	Fri 10/22/21	51FS+5 days	Centex	0%
57	Trim out Electrical	3 days	Tue 10/26/21	Thu 10/28/21	55	DPE	0%
58	Trim out HVAC	1 day	Fri 10/29/21	Fri 10/29/21	57	3 C Mechanical	0%
59	Trim out Plumbing	2 days	Thu 10/21/21	Fri 10/22/21	54	Streamline	0%
60	Trim out Data	1 day	Tue 10/26/21	Tue 10/26/21	55	Entry Tech.	0%
61	Electrical Final Inspection	1 day	Fri 10/29/21	Fri 10/29/21	57	DPE	0%
62	HVAC Final Inspection	1 day	Mon 11/1/21	Mon 11/1/21	58	3 C Mechanical	0%
63	Plumbing Final Inspection	1 day	Mon 10/25/21	Mon 10/25/21	59	Streamline	0%

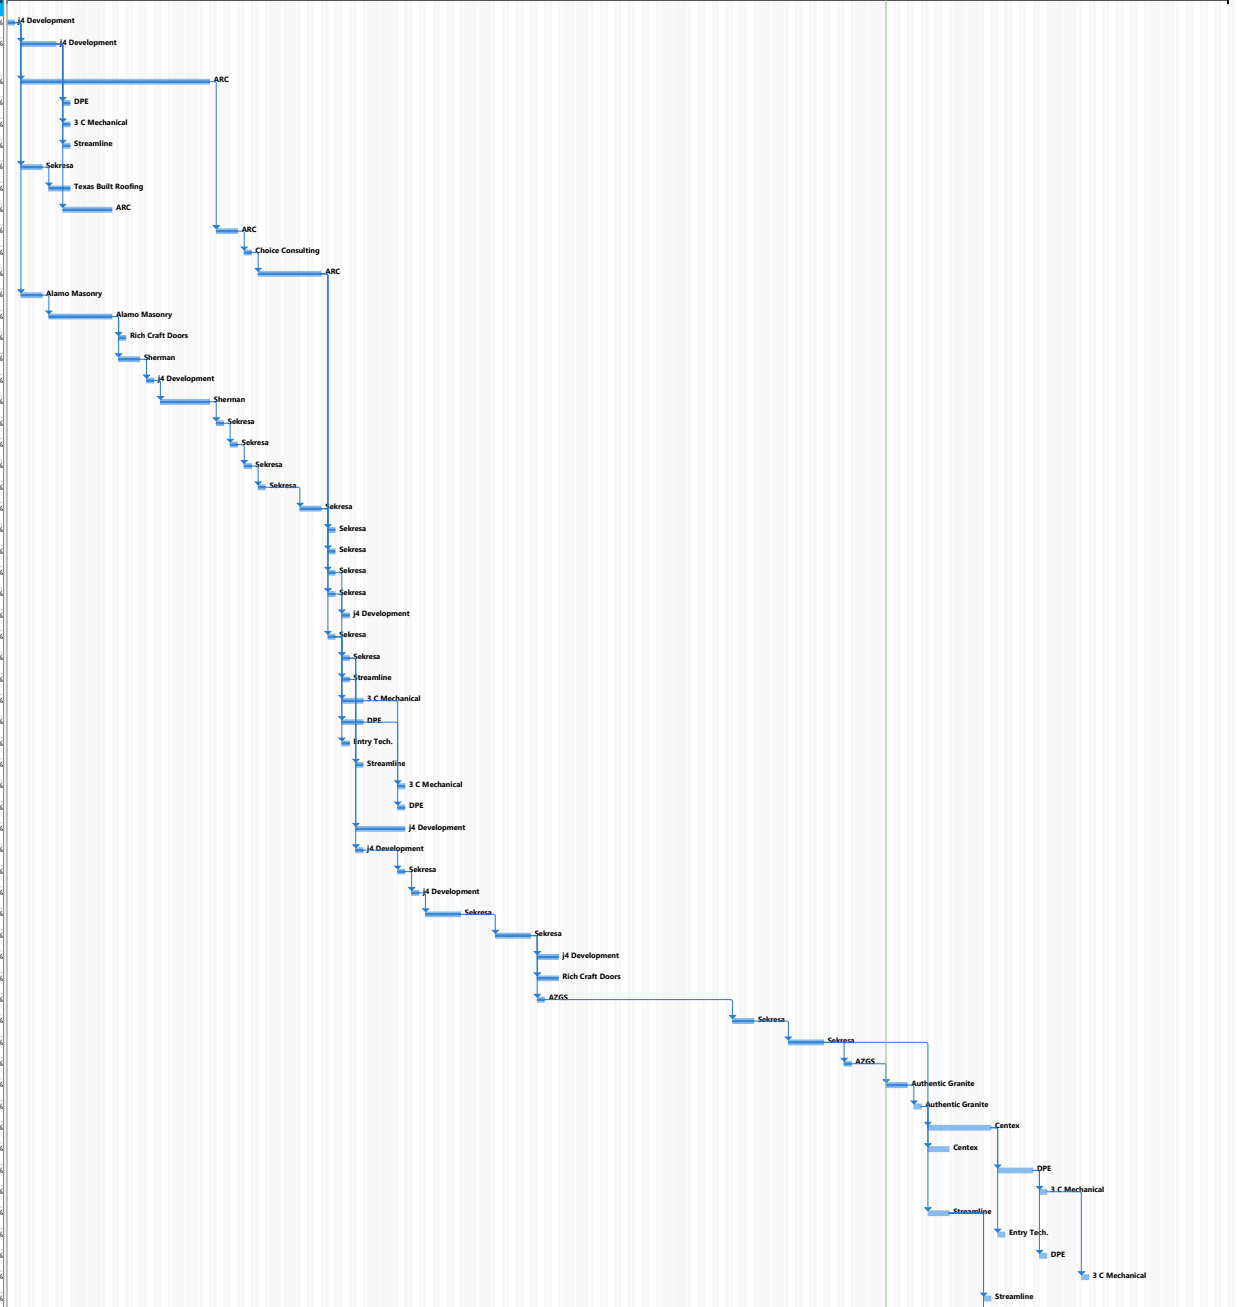



ID	Task	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
64	Install Bath Acc.	1 day	Mon 10/25/21	Mon 10/25/21	59	Sekresa	0%	
65	Install Blinds	1 day	Mon 10/25/21	Mon 10/25/21	59	AZGS	0%	
66	Install interior Door Hardware	1 day	Mon 10/25/21	Mon 10/25/21	59	Rich Craft Doors	0%	
67	Install Exterior Door Hardware	1 day	Mon 10/25/21	Mon 10/25/21	59	Rich Craft Doors	0%	
68	Blow Insulation in Attic	1 day	Mon 10/25/21	Mon 10/25/21	59	Think Home	0%	
69	Prep floors for LVT	2 days	Mon 10/25/21	Tue 10/26/21	59	Centex	0%	
70	Install LVT	2 days	Wed 10/27/21	Thu 10/28/21	69	Centex	0%	
71	Install Rubber Base	1 day	Fri 10/29/21	Fri 10/29/21	70	Centex	0%	
72	Install Door Stops	1 day	Mon 11/1/21	Mon 11/1/21	71	Sekresa	0%	
73	Install Appliances	1 day	Tue 11/2/21	Tue 11/2/21	72	AZGS	0%	
74	Construction Clean Unit	1 day	Wed 11/3/21	Wed 11/3/21	73	Sekresa	0%	
75	j4 Punch Walk	1 day	Thu 11/4/21	Thu 11/4/21	74	j4 Development	0%	
76	j4 Punch Unit	2 days	Fri 11/5/21	Mon 11/8/21	75	j4 Development	0%	
77	Building City Final Inspection	1 day	Tue 11/9/21	Tue 11/9/21	76	j4 Development	0%	
78	Final Clean Unit	1 day	Wed 11/10/21	Wed 11/10/21	77	Sekresa	0%	
79	Architect/Owner Turn Over Walk	1 day	Thu 11/11/21	Thu 11/11/21	78	RDDR/Allied Orion	0%	
81	Building 169	69 days	Mon 8/16/21	Thu 11/18/21			0%	
82	Unit 217/219 Lyndon Type J	68 days	Tue 8/17/21	Thu 11/18/21			65%	
83	Receive possession of Unit	68 days	Tue 8/17/21	Thu 11/18/21		j4 Development	65%	
84	Walk unit to verify existing conditions & MEP systems are working	3 days	Tue 8/17/21	Thu 8/19/21		j4 Development	100%	
85	Submit 10 day abatement notice	10 days	Tue 8/17/21	Mon 8/30/21		ARC	100%	
86	Electrical Demo	1 day	Fri 8/20/21	Fri 8/20/21	84	DPE	100%	
87	HVAC Demo	1 day	Fri 8/20/21	Fri 8/20/21	84	3 C Mechanical	100%	
88	Plumbing Demo	1 day	Fri 8/20/21	Fri 8/20/21	84	Streamline	100%	
89	Fascia Demo & install New	2 days	Tue 8/17/21	Wed 8/18/21	84	Sekresa	100%	
90	New Roof Demo & install New	2 days	Thu 8/19/21	Fri 8/20/21	89	Texas Built Roofing	100%	
91	Interior Soft Demo	2 days	Fri 8/20/21	Mon 8/23/21	84	ARC	100%	
92	Abatement	2 days	Tue 8/31/21	Wed 9/1/21	85	ARC	100%	
93	Air Test	1 day	Thu 9/2/21	Thu 9/2/21	92	Choice Consulting	100%	
94	Remaining Demo Walls & Ceilings	3 days	Fri 9/3/21	Tue 9/7/21	93	ARC	100%	
95	Point up Existing Brick	2 days	Tue 8/17/21	Wed 8/18/21	84	Alamo Masonry	100%	
96	Install Exterior Stone	3 days	Thu 8/19/21	Mon 8/23/21	95	Alamo Masonry	100%	
97	Install new front door with construction lock	1 day	Tue 8/24/21	Tue 8/24/21	96	Rich Craft Doors	100%	
98	Cedar Demo and/or building wrap install	2 days	Tue 8/24/21	Wed 8/25/21	96	Sherman	100%	
99	Building Wrap Inspection	1 day	Thu 8/26/21	Thu 8/26/21	98	j4 Development	100%	
100	Install Hardie Shake Siding	2 days	Fri 8/27/21	Mon 8/30/21	99	Sherman	100%	
101	Install Hardie Soffit Board	1 day	Tue 8/31/21	Tue 8/31/21	100	Sekresa	100%	
102	Prime Paint Building Exterior	1 day	Wed 9/1/21	Wed 9/1/21	101	Sekresa	100%	
103	Finish Paint Building Exterior	1 day	Thu 9/2/21	Thu 9/2/21	102	Sekresa	100%	
104	Pressure Wash Interior Existing CMU	1 day	Fri 9/3/21	Fri 9/3/21	93	Sekresa	100%	
105	Install Vapor Barrier	2 days	Mon 9/6/21	Tue 9/7/21	104	Sekresa	100%	
106	Install Foam Insulation	1 day	Wed 9/8/21	Wed 9/8/21	105	Sekresa	100%	
107	Install Metal Strapping	1 day	Wed 9/8/21	Wed 9/8/21	105	Sekresa	100%	
108	Install Ceiling Hat Channel	1 day	Fri 9/3/21	Fri 9/3/21	93	Sekresa	100%	
109	Install Smoke Barrier	1 day	Fri 9/3/21	Fri 9/3/21	93	Sekresa	100%	
110	Smoke Barrier Inspection	1 day	Mon 9/6/21	Mon 9/6/21	109	j4 Development	100%	
111	Install Interior Wall Framing	1 day	Fri 9/3/21	Fri 9/3/21	93	Sekresa	100%	
112	Install in Wall Blocking	1 day	Mon 9/6/21	Mon 9/6/21	111	Sekresa	100%	
113	Install Plumbing R/I	1 day	Mon 9/6/21	Mon 9/6/21	111	Streamline	100%	
114	Install HVAC R/I	2 days	Mon 9/6/21	Tue 9/7/21	108	3 C Mechanical	100%	
115	Install Electrical R/I	2 days	Mon 9/6/21	Tue 9/7/21	111	DPE	100%	
116	Install Gata R/I	1 day	Mon 9/6/21	Mon 9/6/21	111	Entry Tech.	100%	
117	Plumbing R/I Inspection	1 day	Tue 9/7/21	Tue 9/7/21	113	Streamline	100%	
118	HVAC R/I Inspection	1 day	Wed 9/8/21	Wed 9/8/21	114	3 C Mechanical	100%	
119	Electrical R/I Inspection	1 day	Wed 9/8/21	Wed 9/8/21	115	DPE	100%	
120	j4 Frame Punch	2 days	Tue 9/7/21	Wed 9/8/21	112	j4 Development	100%	
121	Wall Framing Inspection	1 day	Tue 9/7/21	Tue 9/7/21	112	j4 Development	100%	
122	Install Batt Insulation	1 day	Wed 9/8/21	Wed 9/8/21	121	Sekresa	100%	
123	Insulation inspection	1 day	Thu 10/7/21	Thu 10/7/21	122	j4 Development	100%	
124	Hang Drywall	3 days	Fri 10/8/21	Tue 10/12/21	123	Sekresa	100%	
125	Skim Coat and/or T&T	3 days	Wed 10/13/21	Fri 10/15/21	124	Sekresa	100%	
126	j4 Drywall Punch	2 days	Mon 10/18/21	Tue 10/19/21	125	j4 Development	100%	

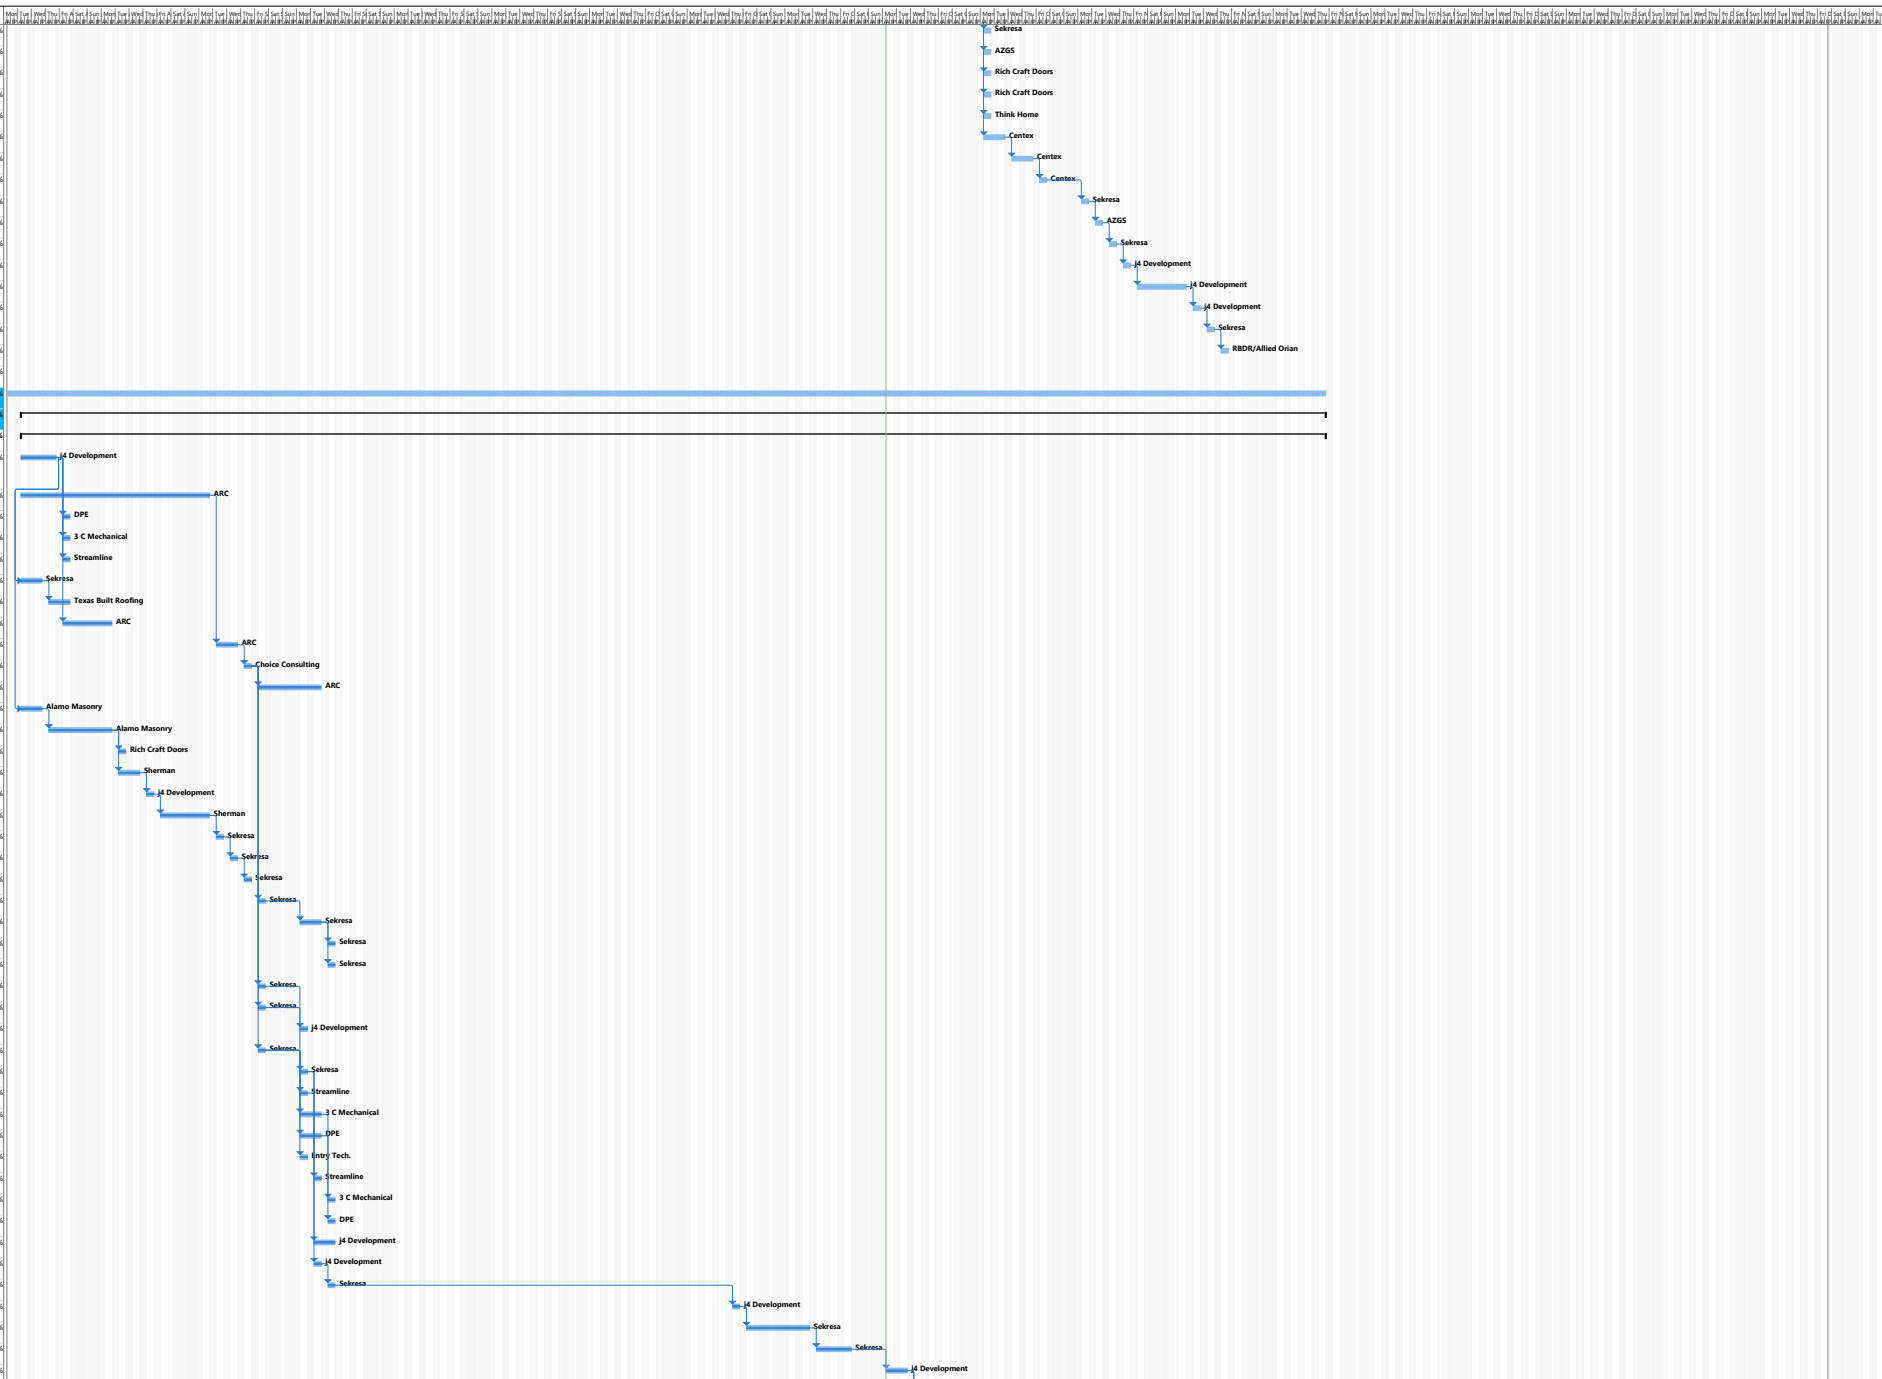



Project: 10.11.2021 South Terra
 Date: Mon 10/18/21

■ Milestone
■ Project Summary
■ Inactive Milestone
■ Manual Task
■ Manual Summary Rollup
■ Start-only
■ External Tasks
■ Deadline
■ Manual Progress
■ Inactive Summary
■ Inactive Summary
■ Duration-only
■ Manual Summary
■ Finish-only
■ External Milestone
■ Progress

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
127	Install Interior Doors	1 day	Wed 10/20/21	Wed 10/20/21	126	Rich Craft Doors	100%
128	Install Closet Shelving	1 day	Wed 10/20/21	Wed 10/20/21	126	AZGS	100%
129	Interior Prime Paint	2 days	Thu 10/21/21	Fri 10/22/21	128	Sekresa	0%
130	Interior Finish Paint	3 days	Mon 10/25/21	Wed 10/27/21	129	Sekresa	0%
131	Install Cabinets	1 day	Thu 10/28/21	Thu 10/28/21	130	AZGS	0%
132	Field measure & cut Countertops	2 days	Fri 10/29/21	Mon 11/1/21	131	Authentic Granite	0%
133	Install Countertop	1 day	Tue 11/2/21	Tue 11/2/21	132	Authentic Granite	0%
134	Install Backsplash Tile	2 days	Wed 11/3/21	Thu 11/4/21	133	Centex	0%
135	Install Bathroom Floor Tile	2 days	Thu 10/28/21	Fri 10/29/21	130	Centex	0%
136	Trim out Electrical	3 days	Fri 11/5/21	Tue 11/9/21	134	DPE	0%
137	Trim out HVAC	1 day	Wed 11/10/21	Wed 11/10/21	136	3 C Mechanical	0%
138	Trim out Plumbing	2 days	Fri 11/5/21	Mon 11/8/21	134	Streamline	0%
139	Trim out Data	1 day	Wed 11/10/21	Wed 11/10/21	136	Entry Tech.	0%
140	Electrical Final Inspection	1 day	Wed 11/10/21	Wed 11/10/21	136	DPE	0%
141	HVAC Final Inspection	1 day	Thu 11/11/21	Thu 11/11/21	137	3 C Mechanical	0%
142	Plumbing Final Inspection	1 day	Tue 11/9/21	Tue 11/9/21	138	Streamline	0%
143	Install Bath Acc.	1 day	Tue 11/9/21	Tue 11/9/21	138	Sekresa	0%
144	Install Blinds	1 day	Tue 11/9/21	Tue 11/9/21	138	AZGS	0%
145	Install Interior Door Hardware	1 day	Tue 11/9/21	Tue 11/9/21	138	Rich Craft Doors	0%
146	Install Exterior Door Hardware	1 day	Tue 11/9/21	Tue 11/9/21	138	Rich Craft Doors	0%
147	Blow Insulation in Attic	1 day	Tue 11/9/21	Tue 11/9/21	138	Think Home	0%
148	Prep floors for LVT	1 day	Tue 11/9/21	Tue 11/9/21	138	Centex	0%
149	Install LVT	2 days	Wed 11/10/21	Thu 11/11/21	148	Centex	0%
150	Install Rubber Base	1 day	Fri 11/12/21	Fri 11/12/21	149	Centex	0%
151	Install Door Stops	1 day	Mon 11/15/21	Mon 11/15/21	150	Sekresa	0%
152	Install Appliances	1 day	Mon 11/15/21	Mon 11/15/21	150	AZGS	0%
153	Construction Clean Unit	1 day	Mon 11/15/21	Mon 11/15/21	150	Sekresa	0%
154	j4 Punch Walk	1 day	Mon 11/15/21	Mon 11/15/21	150	j4 Development	0%
155	j4 Punch Unit	2 days	Tue 11/16/21	Wed 11/17/21	154	j4 Development	0%
156	Building City Final Inspection	1 day	Tue 11/16/21	Tue 11/16/21	152	j4 Development	0%
157	Final Clean Unit	1 day	Wed 11/17/21	Wed 11/17/21	156	Sekresa	0%
158	Architect/Owner Turn Over Walk	1 day	Thu 11/18/21	Thu 11/18/21	157	RBDR/Allied Orion	0%
159							0%
160	Building L70	70 days	Tue 8/24/21	Mon 11/29/21			0%
161	221/223 Lyndon Type I	70 days	Tue 8/24/21	Mon 11/29/21			56%
162	Receive possession of Unit	70 days	Tue 8/24/21	Mon 11/29/21		j4 Development	56%
163	Walk unit to verify existing conditions & MEP systems are working	3 days	Tue 8/24/21	Thu 8/26/21		j4 Development	100%
164	Submit 10 day abatement notice	10 days	Fri 8/27/21	Thu 9/9/21	163	ARC	100%
165	Electrical Demo	1 day	Fri 8/27/21	Fri 8/27/21	163	DPE	100%
166	HVAC Demo	1 day	Fri 8/27/21	Fri 8/27/21	163	3 C Mechanical	100%
167	Plumbing Demo	1 day	Fri 8/27/21	Fri 8/27/21	163	Streamline	100%
168	Fascia Demo & Install New	2 days	Tue 8/24/21	Wed 8/25/21	163	Sekresa	100%
169	New Roof Demo & Install New	2 days	Thu 8/26/21	Fri 8/27/21	168	Texas Built Roofing	100%
170	Interior Soft Demo	2 days	Tue 8/24/21	Wed 8/25/21	163	ARC	100%
171	Abatement	2 days	Fri 9/10/21	Mon 9/13/21	164	ARC	100%
172	Air Test	1 day	Tue 9/14/21	Tue 9/14/21	171	Choice Consulting	100%
173	Remaining Demo Walls & Ceilings	3 days	Wed 9/15/21	Fri 9/17/21	172	ARC	100%
174	Point up Existing Brick	2 days	Tue 8/24/21	Wed 8/25/21	163	Alamo Masonry	100%
175	Install Exterior Stone	3 days	Thu 8/26/21	Mon 8/30/21	174	Alamo Masonry	100%
176	Install new front door with construction lock	1 day	Tue 8/31/21	Tue 8/31/21	175	Rich Craft Doors	100%
177	Cedar Demo and/or building wrap install	2 days	Tue 8/31/21	Wed 9/1/21	175	Sherman	100%
178	Building Wrap Inspection	1 day	Thu 9/2/21	Thu 9/2/21	177	j4 Development	100%
179	Install Hardie Shake Siding	2 days	Fri 9/3/21	Mon 9/6/21	178	Sherman	100%
180	Install Hardie Soffit Board	1 day	Tue 9/7/21	Tue 9/7/21	179	Sekresa	100%
181	Prime Paint Building Exterior	1 day	Wed 9/8/21	Wed 9/8/21	180	Sekresa	100%
182	Finish Paint Building Exterior	1 day	Thu 9/9/21	Thu 9/9/21	181	Sekresa	100%
183	Pressure Wash Existing CMU	1 day	Wed 9/15/21	Wed 9/15/21	172	Sekresa	100%
184	Install Vapor Barrier	2 days	Thu 9/16/21	Fri 9/17/21	183	Sekresa	100%
185	Install Foam Insulation	1 day	Mon 9/20/21	Mon 9/20/21	184	Sekresa	100%
186	Install Metal Strapping	1 day	Mon 9/20/21	Mon 9/20/21	184	Sekresa	100%
187	Install Ceiling Hat Channel	1 day	Wed 9/15/21	Wed 9/15/21	172	Sekresa	100%
188	Install Smoke Barrier	1 day	Wed 9/15/21	Wed 9/15/21	172	Sekresa	100%
189	Smoke Barrier Inspection	1 day	Thu 9/16/21	Thu 9/16/21	188	j4 Development	100%

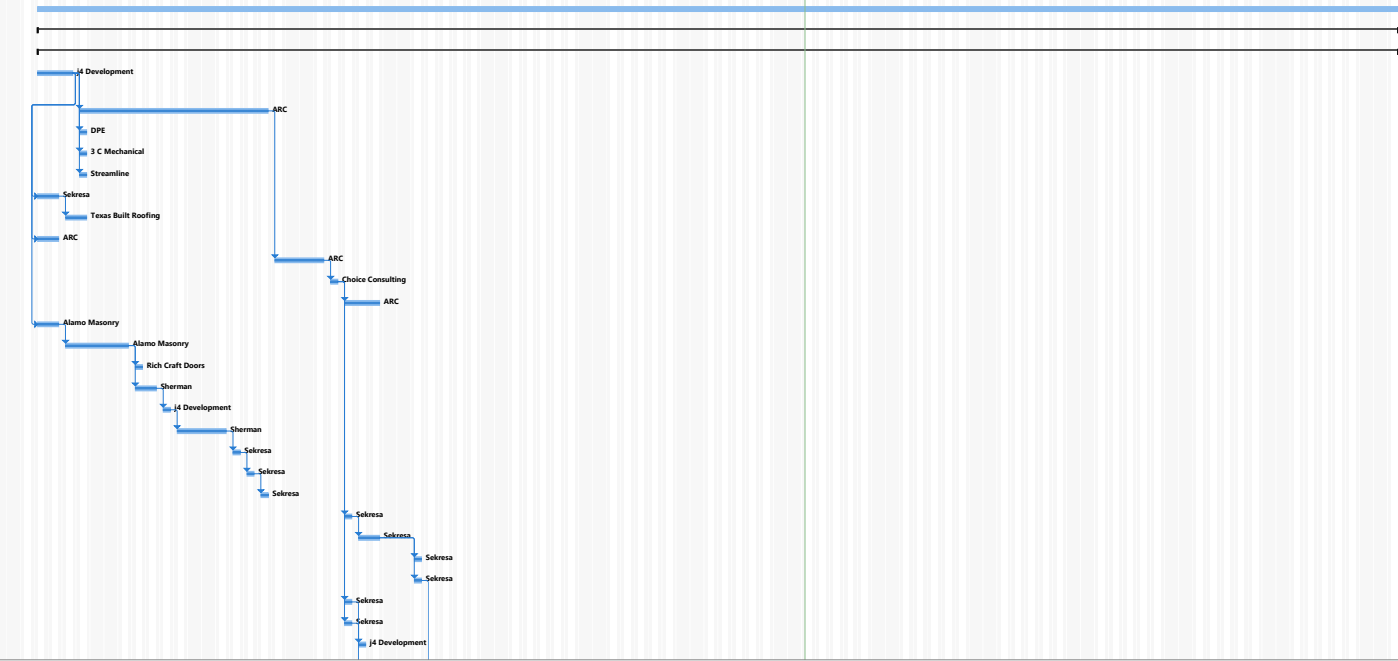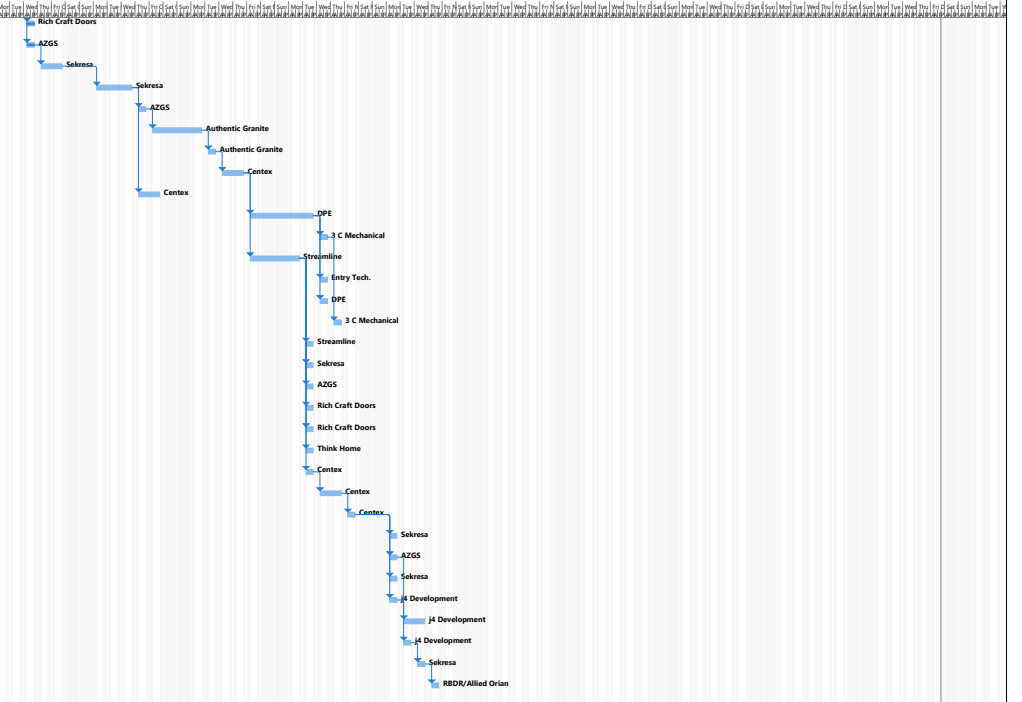

ID	Task	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
190	✓	Install Interior Wall Framing	1 day	Tue 9/21/21	Tue 9/22/21	186	Sekresa	100%
191	✓	Install in Wall Blocking	1 day	Wed 9/22/21	Wed 9/22/21	190	Sekresa	100%
192	✓	J4 Frame Punch	2 days	Thu 9/23/21	Fri 9/24/21	191	J4 Development	100%
193	✓	Install Plumbing R/I	1 day	Wed 9/22/21	Wed 9/22/21	190	Streamline	100%
194	✓	Install HVAC R/I	2 days	Thu 9/16/21	Fri 9/17/21	187	3 C Mechanical	100%
195	✓	Install Electrical R/I	2 days	Wed 9/22/21	Thu 9/23/21	190	DPE	100%
196	✓	Install Data R/I	1 day	Mon 10/11/21	Mon 10/11/21	190	Entry Tech.	100%
197	✓	Plumbing R/I Inspection	1 day	Thu 9/23/21	Thu 9/23/21	193	Streamline	100%
198	✓	HVAC R/I Inspection	1 day	Mon 9/20/21	Mon 9/20/21	194	3 C Mechanical	100%
199	✓	Electrical R/I Inspection	1 day	Thu 10/7/21	Thu 10/7/21	195	DPE	100%
200	✓	Wall Framing Inspection	1 day	Mon 10/11/21	Mon 10/11/21	1975+2 days	J4 Development	100%
201	✓	Install Batt Insulation	1 day	Tue 10/12/21	Tue 10/12/21	200	Sekresa	100%
202	✓	Insulation Inspection	1 day	Fri 10/15/21	Fri 10/15/21	2015+2 days	J4 Development	100%
203	✗	Hang Drywall	3 days	Wed 10/20/21	Fri 10/22/21	2025+2 days	Sekresa	0%
204	✗	Skim Coat and/or TBT	3 days	Mon 10/25/21	Wed 10/27/21	203	Sekresa	0%
205	✗	J4 Drywall Punch	2 days	Thu 10/28/21	Fri 10/29/21	204	J4 Development	0%
206	✗	Install Interior Doors	1 day	Thu 10/28/21	Thu 10/28/21	204	Rich Craft Doors	0%
207	✗	Install Closet Shelving	1 day	Thu 10/28/21	Thu 10/28/21	204	AZGS	0%
208	✗	Interior Prime Paint	2 days	Fri 10/29/21	Mon 11/1/21	207	Sekresa	0%
209	✗	Interior Finish Paint	3 days	Tue 11/2/21	Thu 11/4/21	208	Sekresa	0%
210	✗	Install Cabinets	1 day	Fri 11/5/21	Fri 11/5/21	209	AZGS	0%
211	✗	Field measure & cut Countertops	2 days	Mon 11/8/21	Tue 11/9/21	210	Authentic Granite	0%
212	✗	Install Countertop	1 day	Wed 11/10/21	Wed 11/10/21	211	Authentic Granite	0%
213	✗	Install Backsplash Tile	2 days	Thu 11/11/21	Fri 11/12/21	212	Centex	0%
214	✗	Install Bathroom Floor Tile	2 days	Fri 11/5/21	Mon 11/8/21	209	Centex	0%
215	✗	Trim out Electrical	3 days	Mon 11/15/21	Wed 11/17/21	213	DPE	0%
216	✗	Trim out HVAC	1 day	Thu 11/18/21	Thu 11/18/21	215	3 C Mechanical	0%
217	✗	Trim out Plumbing	2 days	Mon 11/15/21	Tue 11/16/21	213	Streamline	0%
218	✗	Trim out Data	1 day	Thu 11/18/21	Thu 11/18/21	215	Entry Tech.	0%
219	✗	Electrical Final Inspection	1 day	Thu 11/18/21	Thu 11/18/21	215	DPE	0%
220	✗	HVAC Final Inspection	1 day	Fri 11/19/21	Fri 11/19/21	216	3 C Mechanical	0%
221	✗	Plumbing Final Inspection	1 day	Wed 11/17/21	Wed 11/17/21	217	Streamline	0%
222	✗	Install Bath Acc.	1 day	Wed 11/17/21	Wed 11/17/21	217	Sekresa	0%
223	✗	Install Blinds	1 day	Wed 11/17/21	Wed 11/17/21	217	AZGS	0%
224	✗	Install Interior Door Hardware	1 day	Wed 11/17/21	Wed 11/17/21	217	Rich Craft Doors	0%
225	✗	Install Exterior Door Hardware	1 day	Wed 11/17/21	Wed 11/17/21	217	Rich Craft Doors	0%
226	✗	Blow Insulation in Attic	1 day	Wed 11/17/21	Wed 11/17/21	217	Think Home	0%
227	✗	Prep floors for LVT	1 day	Thu 11/18/21	Thu 11/18/21	221	Centex	0%
228	✗	Install LVT	2 days	Fri 11/19/21	Mon 11/22/21	227	Centex	0%
229	✗	Install Rubber Base	1 day	Tue 11/23/21	Tue 11/23/21	228	Centex	0%
230	✗	Install Door Stops	1 day	Wed 11/24/21	Wed 11/24/21	229	Sekresa	0%
231	✗	Install Appliances	1 day	Wed 11/24/21	Wed 11/24/21	229	AZGS	0%
232	✗	Construction Clean Unit	1 day	Wed 11/24/21	Wed 11/24/21	229	Sekresa	0%
233	✗	J4 Punch Walk	1 day	Wed 11/24/21	Wed 11/24/21	229	J4 Development	0%
234	✗	J4 Punch Unit	2 days	Thu 11/25/21	Fri 11/26/21	233	J4 Development	0%
235	✗	Building City Final Inspection	1 day	Thu 11/25/21	Thu 11/25/21	231	J4 Development	0%
236	✗	Final Clean Unit	1 day	Fri 11/26/21	Fri 11/26/21	235	Sekresa	0%
237	✗	Architect/Owner Turn Over Walk	1 day	Mon 11/29/21	Mon 11/29/21	236	RBD/Allied Orion	0%
238	✗							0%
239	✗	Building 203	66 days	Tue 8/24/21	Tue 11/23/21			56%
240	✗	1001/1103 Gurley Type H	66 days	Tue 8/24/21	Tue 11/23/21			56%
241	✗	Receive possession of Unit	66 days	Tue 8/24/21	Tue 11/23/21		J4 Development	56%
242	✓	Walk unit to verify existing conditions & MEP systems are working	3 days	Tue 8/24/21	Thu 8/26/21		J4 Development	100%
243	✓	Submit 10 day abatement notice	10 days	Tue 8/24/21	Mon 9/6/21		ARC	100%
244	✓	Electrical Demo	1 day	Fri 8/27/21	Fri 8/27/21	242	DPE	100%
245	✓	HVAC Demo	1 day	Fri 8/27/21	Fri 8/27/21	242	3 C Mechanical	100%
246	✓	Plumbing Demo	1 day	Fri 8/27/21	Fri 8/27/21	242	Streamline	100%
247	✓	Fascia Demo & Install New	2 days	Tue 8/24/21	Wed 8/25/21	242	Sekresa	100%
248	✓	New Roof Demo & Install New	2 days	Thu 8/26/21	Fri 8/27/21	247	Texas Built Roofing	100%
249	✓	Interior Soft Demo	2 days	Tue 8/24/21	Wed 8/25/21	242	ARC	100%
250	✓	Abatement	2 days	Tue 9/7/21	Wed 9/8/21	243	ARC	100%
251	✓	Air Test	1 day	Thu 9/9/21	Thu 9/9/21	250	Choice Consulting	100%
252	✓	Remaining Demo Walls & Ceilings	3 days	Fri 9/10/21	Tue 9/14/21	251	ARC	100%

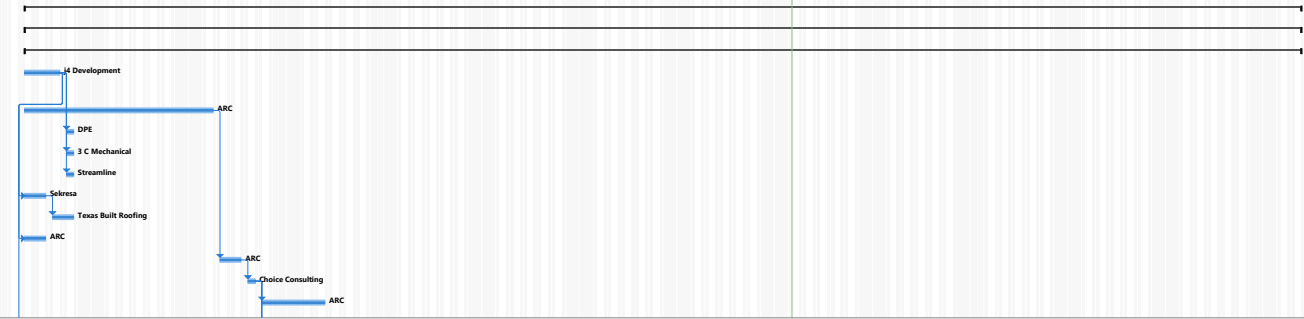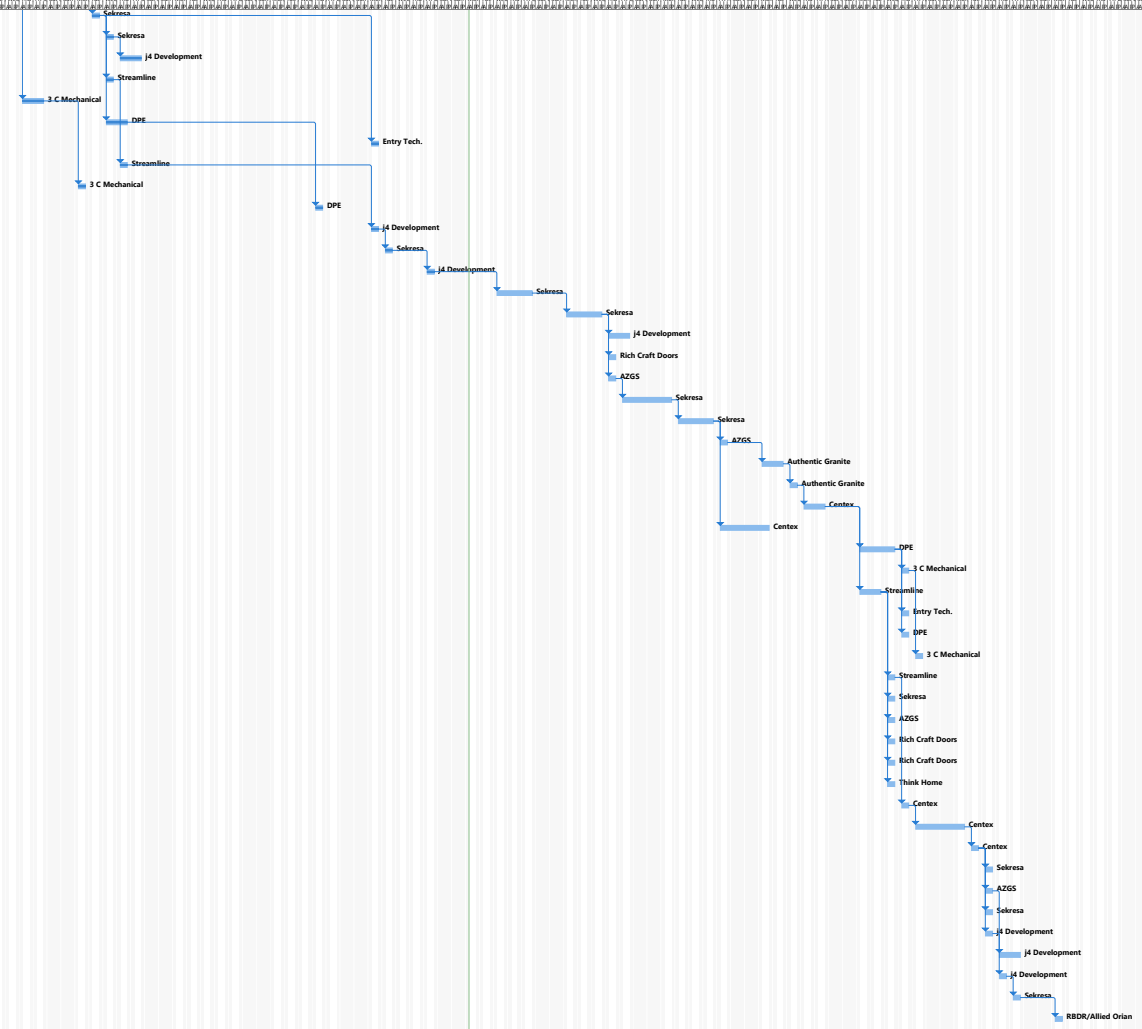


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
253	Point up Existing Brick	2 days	Tue 8/24/21	Wed 8/25/21	242	Alamo Masonry	100%
254	Install Exterior Stone	3 days	Thu 8/26/21	Mon 8/30/21	253	Alamo Masonry	100%
255	Install new front door with construction	1 day	Tue 8/31/21	Tue 8/31/21	254	Rich Craft Doors	100%
256	Cedar Demo and/or building wrap install	2 days	Tue 8/31/21	Wed 9/1/21	254	Sherman	100%
257	Building Wrap Inspection	1 day	Thu 9/2/21	Thu 9/2/21	256	J4 Development	100%
258	Install Hardie Shake Siding	2 days	Fri 9/3/21	Mon 9/6/21	257	Sherman	100%
259	Install Hardie Soffit Board	1 day	Tue 9/7/21	Tue 9/7/21	258	Sekresa	100%
260	Prime Paint Building Exterior	1 day	Wed 9/8/21	Wed 9/8/21	259	Sekresa	100%
261	Finish Paint Building Exterior	1 day	Thu 9/9/21	Thu 9/9/21	260	Sekresa	100%
262	Pressure Wash Existing CMU	1 day	Fri 9/10/21	Fri 9/10/21	261	Sekresa	100%
263	Install Vapor Barrier	2 days	Mon 9/13/21	Tue 9/14/21	262	Sekresa	100%
264	Install Foam insulation	1 day	Wed 9/15/21	Wed 9/15/21	263	Sekresa	100%
265	Install Metal Strapping	1 day	Wed 9/15/21	Wed 9/15/21	263	Sekresa	100%
266	Install Ceiling Hat Channel	1 day	Fri 9/10/21	Fri 9/10/21	251	Sekresa	100%
267	Install Smoke Barrier	1 day	Fri 9/10/21	Fri 9/10/21	251	Sekresa	100%
268	Smoke Barrier Inspection	1 day	Mon 9/13/21	Mon 9/13/21	267	J4 Development	100%
269	Install Interior Wall Framing	1 day	Thu 9/16/21	Thu 9/16/21	265	Sekresa	100%
270	Install in Wall Blocking	1 day	Fri 9/17/21	Fri 9/17/21	269	Sekresa	100%
271	J4 Frame Punch	2 days	Mon 9/20/21	Tue 9/21/21	270	Streamline	100%
272	Install Plumbing R/I	1 day	Fri 9/17/21	Fri 9/17/21	269	3 C Mechanical	100%
273	Install HVAC R/I	2 days	Mon 9/13/21	Tue 9/14/21	266	DPE	100%
274	Install Electrical R/I	2 days	Fri 9/17/21	Mon 9/20/21	269	Entry Tech.	100%
275	Install Data R/I	1 day	Fri 9/17/21	Fri 9/17/21	269	Streamline	100%
276	Plumbing R/I Inspection	1 day	Mon 9/20/21	Mon 9/20/21	272	3 C Mechanical	100%
277	HVAC R/I Inspection	1 day	Wed 9/15/21	Wed 9/15/21	273	DPE	100%
278	Electrical R/I Inspection	1 day	Fri 10/8/21	Fri 10/8/21	274	J4 Development	100%
279	Wall Framing Inspection	1 day	Wed 10/13/21	Wed 10/13/21	278	J4 Development	100%
280	Install Batt Insulation	1 day	Thu 10/14/21	Thu 10/14/21	279	Sekresa	100%
281	Insulation Inspection	1 day	Fri 10/15/21	Fri 10/15/21	280	J4 Development	100%
282	Hang Drywall	3 days	Mon 10/18/21	Wed 10/20/21	281	Sekresa	0%
283	Skim Coat and/or T&T	3 days	Thu 10/21/21	Mon 10/25/21	282	Sekresa	0%
284	J4 Drywall Punch	2 days	Tue 10/26/21	Wed 10/27/21	283	J4 Development	0%
285	Install Interior Doors	1 day	Thu 10/28/21	Thu 10/28/21	284	Rich Craft Doors	0%
286	Install Closet Shelving	1 day	Thu 10/28/21	Thu 10/28/21	284	AZGS	0%
287	Interior Prime Paint	2 days	Fri 10/29/21	Mon 11/1/21	285	Sekresa	0%
288	Interior Finish Paint	3 days	Tue 11/2/21	Thu 11/4/21	287	Sekresa	0%
289	Install Cabinets	1 day	Fri 11/5/21	Fri 11/5/21	288	AZGS	0%
290	Field measure & cut Countertops	2 days	Mon 11/8/21	Tue 11/9/21	289	Authentic Granite	0%
291	Install Countertop	1 day	Wed 11/10/21	Wed 11/10/21	290	Authentic Granite	0%
292	Install Backsplash Tile	2 days	Thu 11/11/21	Fri 11/12/21	291	Centex	0%
293	Install Bathroom Floor Tile	2 days	Fri 11/5/21	Mon 11/8/21	288	Centex	0%
294	Trim out Electrical	3 days	Mon 11/15/21	Wed 11/17/21	292	DPE	0%
295	Trim out HVAC	1 day	Thu 11/18/21	Thu 11/18/21	294	3 C Mechanical	0%
296	Trim out Plumbing	2 days	Tue 11/9/21	Wed 11/10/21	293	Streamline	0%
297	Trim out Data	1 day	Thu 11/18/21	Thu 11/18/21	294	Entry Tech.	0%
298	Electrical Final Inspection	1 day	Thu 11/18/21	Thu 11/18/21	294	DPE	0%
299	HVAC Final Inspection	1 day	Fri 11/19/21	Fri 11/19/21	295	3 C Mechanical	0%
300	Plumbing Final Inspection	1 day	Thu 11/11/21	Thu 11/11/21	296	Streamline	0%
301	Install Bath Acc.	1 day	Thu 11/11/21	Thu 11/11/21	296	Sekresa	0%
302	Install Blinds	1 day	Thu 11/11/21	Thu 11/11/21	296	AZGS	0%
303	Install Interior Door Hardware	1 day	Thu 11/11/21	Thu 11/11/21	296	Rich Craft Doors	0%
304	Install Exterior Door Hardware	1 day	Thu 11/11/21	Thu 11/11/21	296	Rich Craft Doors	0%
305	Blow Insulation in Attic	1 day	Thu 11/11/21	Thu 11/11/21	296	Think Home	0%
306	Prep floors for LVT	1 day	Thu 11/11/21	Thu 11/11/21	296	Centex	0%
307	Install LVT	2 days	Fri 11/12/21	Mon 11/15/21	306	Centex	0%
308	Install Rubber Base	1 day	Tue 11/16/21	Tue 11/16/21	307	Centex	0%
309	Install Door Stops	1 day	Wed 11/17/21	Wed 11/17/21	308	Sekresa	0%
310	Install Appliances	1 day	Wed 11/17/21	Wed 11/17/21	308	AZGS	0%
311	Construction Clean Unit	1 day	Thu 11/18/21	Thu 11/18/21	310	Sekresa	0%
312	J4 Punch Walk	1 day	Thu 11/18/21	Thu 11/18/21	310	J4 Development	0%
313	J4 Punch Unit	2 days	Fri 11/19/21	Mon 11/22/21	312	J4 Development	0%
314	Building City Final Inspection	1 day	Fri 11/19/21	Fri 11/19/21	311	J4 Development	0%
315	Final Clean Unit	1 day	Mon 11/22/21	Mon 11/22/21	314	Sekresa	0%
316	Architect/Owner Turn Over Walk	1 day	Tue 11/23/21	Tue 11/23/21	315	RBD/Allied Orion	0%

Project: 10.11.2021 South Terra Date: Mon 10/18/21


■ Milestone ◆ Project Summary ▬ Inactive Milestone ○ Manual Task ▬ Manual Summary Rollup ▬ Start-only ▬ External Tasks ▬ Deadline ▬ Manual Progress ▬ Progress
▬ Split ◆ Summary ▬ Inactive Task ▬ Inactive Summary ▬ Duration-only ▬ Manual Summary ▬ Finish-only ▬ External Milestone ▬ Progress

Page 5



ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
317							0%
318	Building 217	72 days?	Thu 8/26/21	Fri 12/3/21			53%
319	309/305 Kennedy Type H	72 days?	Thu 8/26/21	Fri 12/3/21			53%
320	Receive possession of Unit	72 days?	Thu 8/26/21	Fri 12/3/21	J4 Development		53%
397	Building 215	70 days	Thu 8/26/21	Wed 12/1/21			53%
398	309/311 Kennedy Type H	70 days	Thu 8/26/21	Wed 12/1/21			53%
399	Receive possession of Unit	70 days	Thu 8/26/21	Wed 12/1/21	J4 Development		53%
400	Walk unit to verify existing conditions & MEP systems are working	3 days	Thu 8/26/21	Mon 8/30/21	J4 Development		100%
401	Submit 10 day abatement notice	10 days	Thu 8/26/21	Wed 9/8/21	ARC		100%
402	Electrical Demo	1 day	Tue 8/31/21	Tue 8/31/21	400 DPE		100%
403	HVAC Demo	1 day	Tue 8/31/21	Tue 8/31/21	400 3 C Mechanical		100%
404	Plumbing Demo	1 day	Tue 8/31/21	Tue 8/31/21	400 Streamline		100%
405	Fascia Demo & Install New	2 days	Thu 8/26/21	Fri 8/27/21	400 Sekresa		100%
406	New Roof Demo & Install New	2 days	Mon 8/30/21	Tue 8/31/21	405 Texas Built Roofing		100%
407	Interior Soft Demo	2 days	Thu 8/26/21	Fri 8/27/21	400 ARC		100%
408	Abatement	2 days	Thu 9/9/21	Fri 9/10/21	401 ARC		100%
409	Air Test	1 day	Mon 9/13/21	Mon 9/13/21	408 Choice Consulting		100%
410	Remaining Demo Walls & Ceilings	3 days	Tue 9/14/21	Thu 9/16/21	409 ARC		100%
411	Paint up Existing Brick	2 days	Thu 8/26/21	Fri 8/27/21	400 Alamo Masonry		100%
412	Install Exterior Stone	3 days	Mon 8/30/21	Wed 9/1/21	411 Alamo Masonry		100%
413	Install new front door with construction	1 day	Thu 9/2/21	Thu 9/2/21	412 Rich Craft Doors		100%
414	Cedar Demo and/or building wrap install	2 days	Thu 9/2/21	Fri 9/3/21	412 Sherman		100%
415	Building Wrap Inspection	1 day	Mon 9/6/21	Mon 9/6/21	414 J4 Development		100%
416	Install Hardie Shake Siding	2 days	Tue 9/7/21	Wed 9/8/21	415 Sherman		100%
417	Install Hardie Soffit Board	1 day	Thu 9/9/21	Thu 9/9/21	416 Sekresa		100%
418	Prime Paint Building Exterior	1 day	Fri 9/10/21	Fri 9/10/21	417 Sekresa		100%
419	Finish Paint Building Exterior	1 day	Mon 9/13/21	Mon 9/13/21	418 Sekresa		100%
420	Pressure Wash Existing CMU	1 day	Tue 9/14/21	Tue 9/14/21	409 Sekresa		100%
421	Install Vapor Barrier	2 days	Wed 9/29/21	Thu 9/30/21	420S+10 days Sekresa		100%
422	Install Foam Insulation	1 day	Fri 10/1/21	Fri 10/1/21	421 Sekresa		100%
423	Install Metal Strapping	1 day	Fri 10/1/21	Fri 10/1/21	421 Sekresa		100%
424	Install Ceiling Hat Channel	1 day	Tue 9/14/21	Tue 9/14/21	409 Sekresa		100%
425	Install Smoke Barrier	1 day	Tue 9/14/21	Tue 9/14/21	409 Sekresa		100%
426	Smoke Barrier Inspection	1 day	Wed 9/15/21	Wed 9/15/21	425 J4 Development		100%
427	Install Interior Wall Framing	1 day	Mon 10/4/21	Mon 10/4/21	423 Sekresa		100%
428	Install in Wall Blocking	1 day	Tue 10/5/21	Tue 10/5/21	427 Sekresa		100%
429	J4 Frame Punch	2 days	Wed 10/6/21	Thu 10/7/21	428 Streamline		100%
430	Install Plumbing R/	1 day	Tue 10/5/21	Tue 10/5/21	427 3 C Mechanical		100%
431	Install HVAC R/	1 day	Wed 9/15/21	Wed 9/15/21	424 DPE		100%
432	Install Electrical R/	1 day	Tue 10/5/21	Tue 10/5/21	427 Entry Tech.		100%
433	Install Data R/	1 day	Tue 10/5/21	Tue 10/5/21	427 Streamline		100%
434	Plumbing R/ Inspection	1 day	Wed 10/6/21	Wed 10/6/21	430 3 C Mechanical		100%
435	HVAC R/ Inspection	1 day	Thu 9/16/21	Thu 9/16/21	431 DPE		100%
436	Electrical R/ Inspection	1 day	Mon 10/18/21	Mon 10/18/21	432PS+8 days J4 Development		100%
437	Wall Framing Inspection	1 day	Tue 10/19/21	Tue 10/19/21	436 J4 Development		0%
438	Install Batt Insulation	1 day	Wed 10/20/21	Wed 10/20/21	437 Sekresa		0%
439	Insulation Inspection	1 day	Thu 10/21/21	Thu 10/21/21	438 J4 Development		0%
440	Hang Drywall	3 days	Fri 10/22/21	Tue 10/26/21	439 Sekresa		0%
441	Skim Coat and/or TBT	3 days	Wed 10/27/21	Fri 10/29/21	440 Sekresa		0%
442	J4 Drywall Punch	2 days	Mon 11/1/21	Tue 11/2/21	441 J4 Development		0%
443	Install Interior Doors	1 day	Mon 11/1/21	Mon 11/1/21	441 Rich Craft Doors		0%
444	Install Closet Shelving	1 day	Mon 11/1/21	Mon 11/1/21	441 AZGS		0%
445	Interior Prime Paint	2 days	Tue 11/2/21	Wed 11/3/21	443 Sekresa		0%
446	Interior Finish Paint	3 days	Thu 11/4/21	Mon 11/8/21	445 Sekresa		0%
447	Install Cabinets	1 day	Tue 11/9/21	Tue 11/9/21	446 AZGS		0%
448	Field measure & cut Countertops	2 days	Wed 11/10/21	Thu 11/11/21	447 Authentic Granite		0%
449	Install Countertop	1 day	Fri 11/12/21	Fri 11/12/21	448 Authentic Granite		0%
450	Install Backsplash Tile	2 days	Mon 11/15/21	Tue 11/16/21	449 Centex		0%
451	Install Bathroom Floor Tile	2 days	Tue 11/9/21	Wed 11/10/21	446 Centex		0%
452	Trim out Electrical	3 days	Wed 11/17/21	Fri 11/19/21	450 DPE		0%
453	Trim out HVAC	1 day	Mon 11/22/21	Mon 11/22/21	452 3 C Mechanical		0%
454	Trim out Plumbing	2 days	Wed 11/17/21	Thu 11/18/21	450 Streamline		0%
455	Trim out Data	1 day	Tue 11/9/21	Tue 11/9/21	446 Entry Tech.		0%

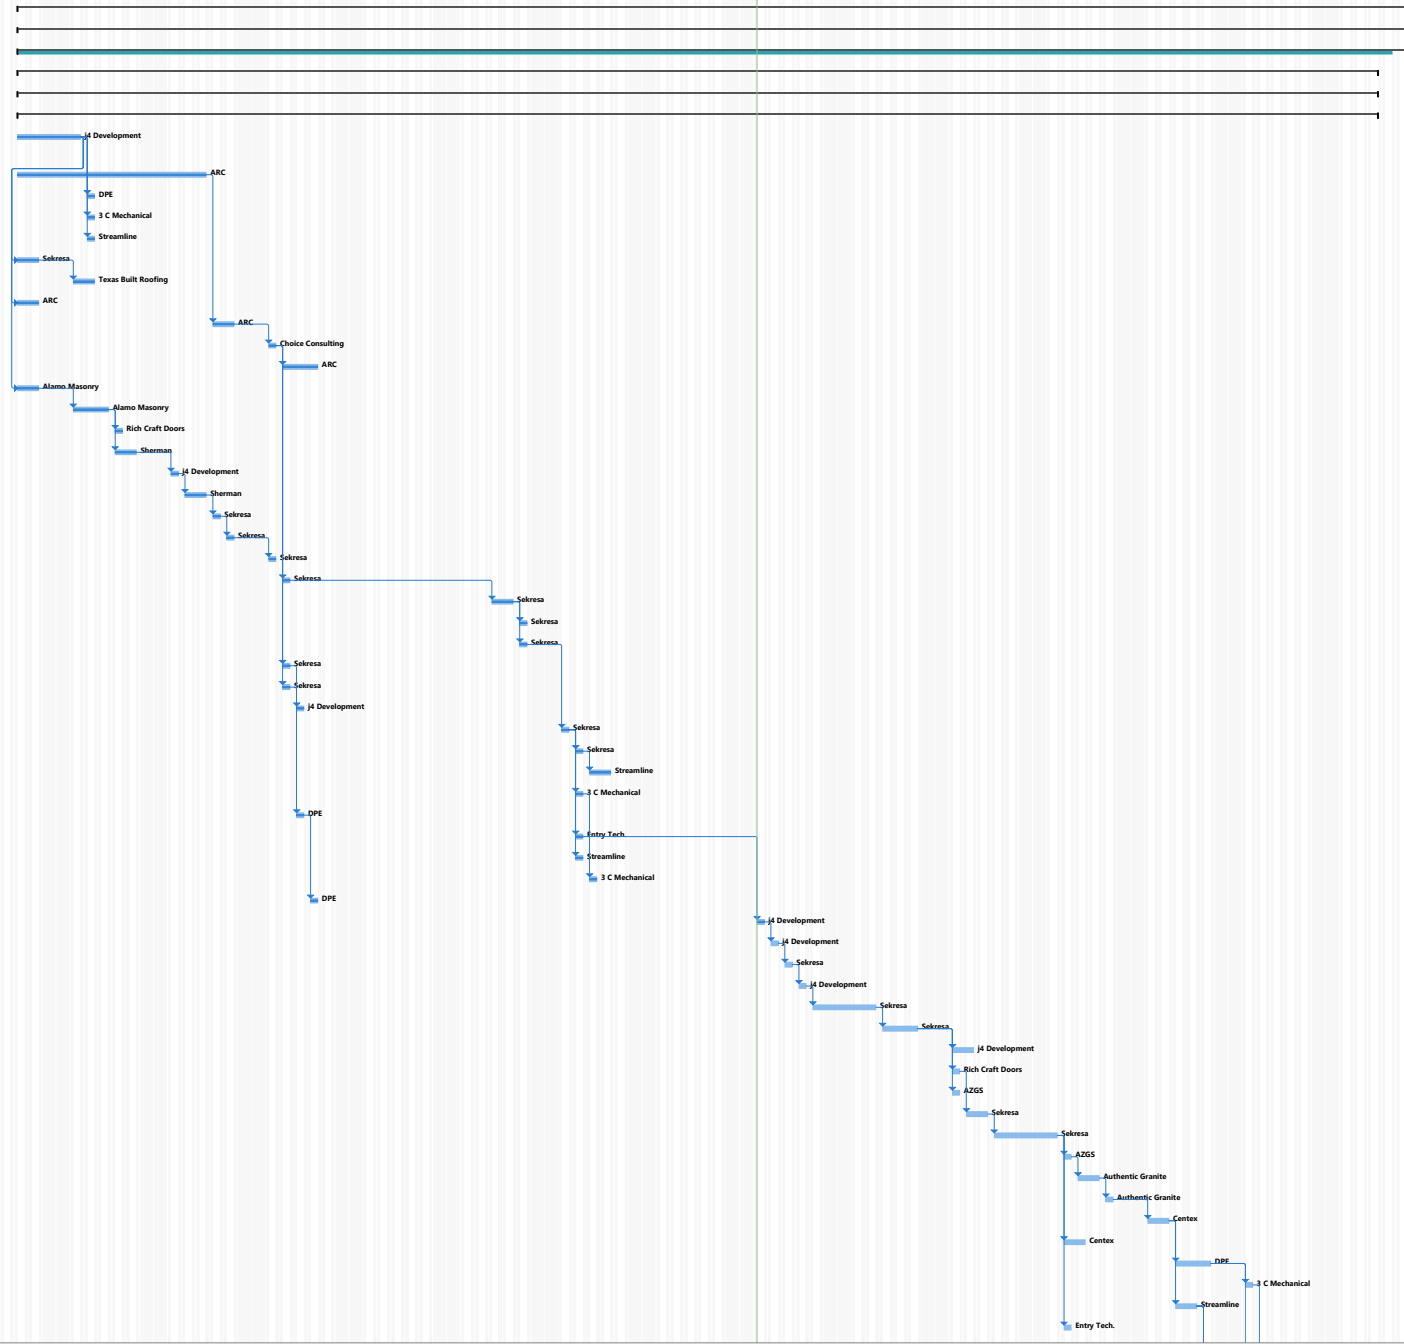



ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
456	Electrical Final Inspection	1 day	Mon 11/22/21	Mon 11/22/21	452	DPE	0%
457	HVAC Final Inspection	1 day	Tue 11/23/21	Tue 11/23/21	453	3 C Mechanical	0%
458	Plumbing Final Inspection	1 day	Fri 11/19/21	Fri 11/19/21	454	Streamline	0%
459	Install Bath Acc.	1 day	Fri 11/19/21	Fri 11/19/21	454	Sekresa	0%
460	Install Blinds	1 day	Fri 11/19/21	Fri 11/19/21	454	AZGS	0%
461	Install Interior Door Hardware	1 day	Fri 11/19/21	Fri 11/19/21	454	Rich Craft Doors	0%
462	Install Exterior Door Hardware	1 day	Fri 11/19/21	Fri 11/19/21	454	Rich Craft Doors	0%
463	Blow Insulation in Attic	1 day	Fri 11/19/21	Fri 11/19/21	454	Think Home	0%
464	Prep floors for LVT	1 day	Fri 11/19/21	Fri 11/19/21	454	Centex	0%
465	Install LVT	3 days	Mon 11/22/21	Wed 11/24/21	464	Centex	0%
466	Install Rubber Base	1 day	Thu 11/25/21	Thu 11/25/21	465	Centex	0%
467	Install Door Stops	1 day	Fri 11/26/21	Fri 11/26/21	466	Sekresa	0%
468	Install Appliances	1 day	Fri 11/26/21	Fri 11/26/21	466	AZGS	0%
469	Construction Clean Unit	1 day	Mon 11/29/21	Mon 11/29/21	468	Sekresa	0%
470	J4 Punch Walk	1 day	Mon 11/29/21	Mon 11/29/21	468	J4 Development	0%
471	J4 Punch Unit	2 days	Tue 11/30/21	Wed 12/1/21	470	J4 Development	0%
472	Building City Final Inspection	1 day	Mon 11/29/21	Mon 11/29/21	468	J4 Development	0%
473	Final Clean Unit	1 day	Tue 11/30/21	Tue 11/30/21	472	Sekresa	0%
474	Architect/Owner Turn Over Walk	1 day	Wed 12/1/21	Wed 12/1/21	473	RBD/Allied Orion	0%
475							0%
476	Building 216	67 days	Wed 9/1/21	Thu 12/2/21			55%
477	301 Kennedy Type F	67 days	Wed 9/1/21	Thu 12/2/21			55%
478	Receive possession of Unit	67 days	Wed 9/1/21	Thu 12/2/21		J4 Development	55%
479	Walk unit to verify existing conditions & MEP systems are working	3 days	Wed 9/2/21	Fri 9/3/21		J4 Development	100%
480	Submit 10 day abatement notice	10 days	Wed 9/2/21	Tue 9/14/21		ARC	100%
481	Electrical Demo	1 day	Mon 9/6/21	Mon 9/6/21	479	DPE	100%
482	HVAC Demo	1 day	Mon 9/6/21	Mon 9/6/21	479	3 C Mechanical	100%
483	Plumbing Demo	1 day	Mon 9/6/21	Mon 9/6/21	479	Streamline	100%
484	Fascia Demo & Install New	2 days	Wed 9/7/21	Thu 9/2/21	479	Sekresa	100%
485	New Roof Demo & Install New	2 days	Fri 9/3/21	Mon 9/6/21	484	Texas Built Roofing	100%
486	Interior Soft Demo	1 day	Wed 9/2/21	Wed 9/2/21	479	ARC	100%
487	Abatement	2 days	Wed 9/15/21	Thu 9/16/21	480	ARC	100%
488	Air Test	1 day	Fri 9/17/21	Fri 9/17/21	487	Choice Consulting	100%
489	Remaining Demo Walls & Ceilings	3 days	Mon 9/20/21	Wed 9/22/21	488	ARC	100%
490	Point up Existing Brick	2 days	Wed 9/1/21	Thu 9/2/21	479	Alamo Masonry	100%
491	Install Exterior Stone	3 days	Fri 9/3/21	Tue 9/7/21	490	Alamo Masonry	100%
492	Install new front door with construction	1 day	Wed 9/8/21	Wed 9/8/21	491	Rich Craft Doors	100%
493	Cedar Demo and/or building wrap install	2 days	Wed 9/8/21	Thu 9/9/21	491	Sherman	100%
494	Building Wrap Inspection	1 day	Fri 9/10/21	Fri 9/10/21	493	J4 Development	100%
495	Install Hardie Shake Siding	2 days	Mon 9/13/21	Tue 9/14/21	494	Sherman	100%
496	Install Hardie Soffit Board	1 day	Wed 9/15/21	Wed 9/15/21	495	Sekresa	100%
497	Prime Paint Building Exterior	1 day	Thu 9/16/21	Thu 9/16/21	496	Sekresa	100%
498	Finish Paint Building Exterior	1 day	Fri 9/17/21	Fri 9/17/21	497	Sekresa	100%
499	Pressure Wash Existing CMU	1 day	Mon 9/20/21	Mon 9/20/21	488	Sekresa	100%
500	Install Vapor Barrier	2 days	Thu 10/7/21	Fri 10/8/21	499S+12 days	Sekresa	100%
501	Install Foam Insulation	1 day	Mon 10/11/21	Mon 10/11/21	500	Sekresa	100%
502	Install Metal Strapping	1 day	Mon 10/11/21	Mon 10/11/21	500	Sekresa	100%
503	Install Ceiling Hat Channel	1 day	Mon 9/20/21	Mon 9/20/21	488	Sekresa	100%
504	Install Smoke Barrier	1 day	Mon 9/20/21	Mon 9/20/21	488	Sekresa	100%
505	Install Interior Wall Framing	1 day	Tue 10/12/21	Tue 10/12/21	502	J4 Development	100%
506	Install in Wall Blocking	1 day	Wed 10/13/21	Wed 10/13/21	505	Sekresa	100%
507	J4 Frame Punch	2 days	Thu 10/14/21	Fri 10/15/21	506	Sekresa	100%
508	Install Plumbing R/	1 day	Wed 10/13/21	Wed 10/13/21	505	Streamline	100%
509	Install HVAC R/	2 days	Tue 9/21/21	Wed 9/22/21	503	3 C Mechanical	100%
510	Install Electrical R/	2 days	Wed 10/13/21	Thu 10/14/21	505	DPE	100%
511	Install Data R/	1 day	Wed 10/13/21	Wed 10/13/21	505	Entry Tech.	100%
512	Plumbing R/ Inspection	1 day	Wed 10/13/21	Wed 10/13/21	505	Streamline	100%
513	HVAC R/ Inspection	1 day	Thu 9/23/21	Thu 9/23/21	509	3 C Mechanical	100%
514	Electrical R/ Inspection	1 day	Tue 10/12/21	Tue 10/12/21	510S-3 days	DPE	100%
515	Smoke Barrier Inspection	1 day	Wed 10/13/21	Wed 10/13/21	514	J4 Development	100%
516	Wall Framing Inspection	1 day	Mon 10/18/21	Mon 10/18/21	515S+2 days	J4 Development	0%
517	Install Batt Insulation	1 day	Tue 10/19/21	Tue 10/19/21	516	Sekresa	0%
518	Insulation Inspection	1 day	Wed 10/20/21	Wed 10/20/21	517	J4 Development	0%

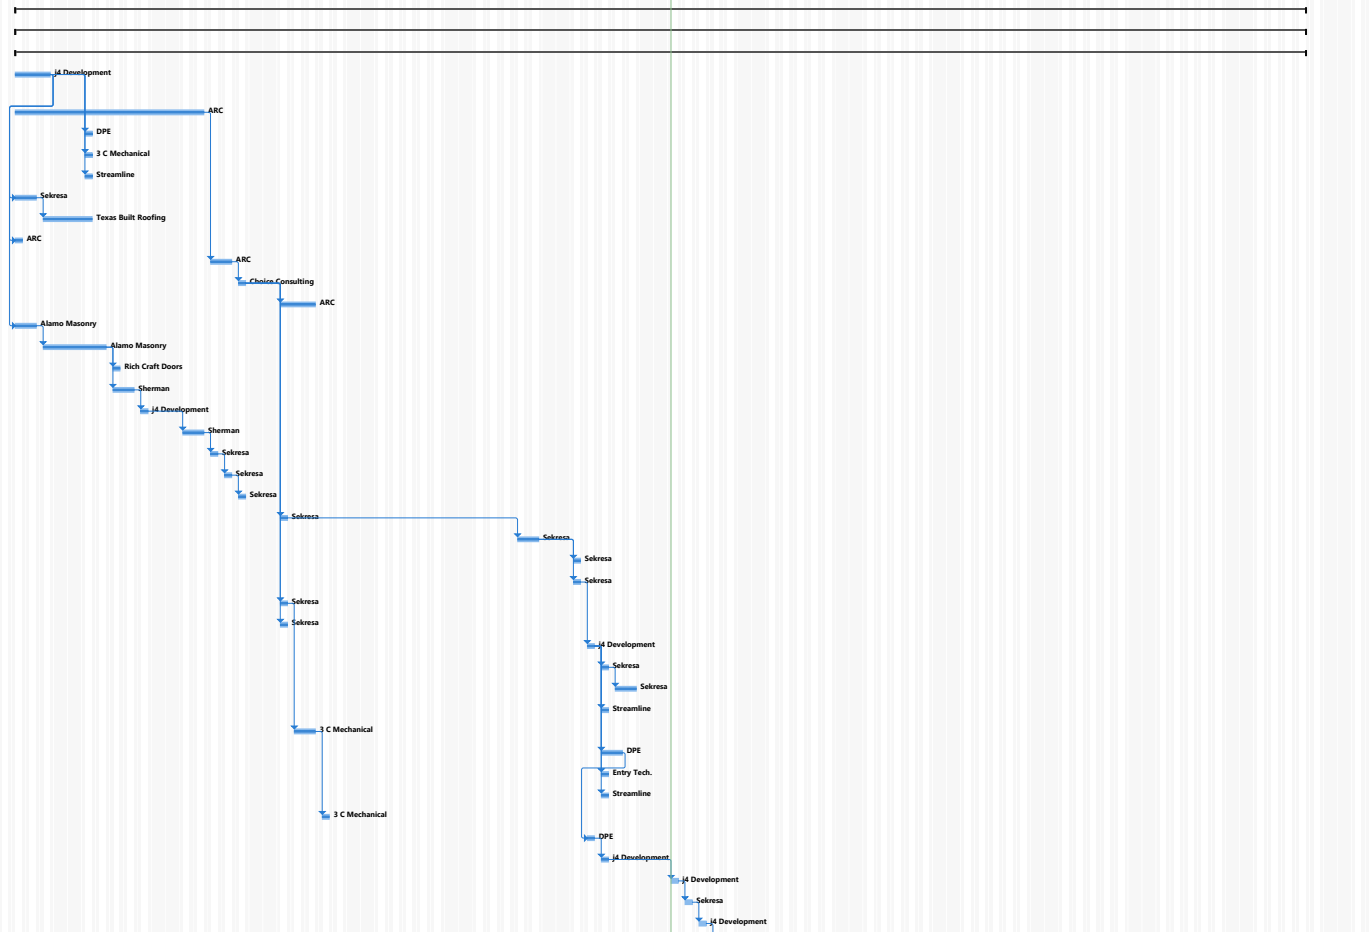


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
515	Hang Drywall	4 days	Thu 10/21/21	Tue 10/26/21	518	Sekresa	0%
520	Skim Coat and/or T&T	3 days	Wed 10/27/21	Fri 10/29/21	519	Sekresa	0%
521	J4 Drywall Punch	2 days	Mon 11/1/21	Tue 11/2/21	520	J4 Development	0%
522	Install Interior Doors	1 day	Mon 11/1/21	Mon 11/1/21	520	Rich Craft Doors	0%
523	Install Closet Shelving	1 day	Mon 11/1/21	Mon 11/1/21	520	AZGS	0%
524	Interior Prime Paint	1 day	Tue 11/2/21	Tue 11/2/21	523	Sekresa	0%
525	Interior Finish Paint	2 days	Wed 11/3/21	Thu 11/4/21	524	Sekresa	0%
526	Install Cabinets	1 day	Fri 11/5/21	Fri 11/5/21	525	AZGS	0%
527	Field measure & cut Countertops	2 days	Mon 11/8/21	Tue 11/9/21	526	Authentic Granite	0%
528	Install Countertop	1 day	Wed 11/10/21	Wed 11/10/21	527	Authentic Granite	0%
529	Install Backsplash Tile	2 days	Thu 11/11/21	Fri 11/12/21	528	Centex	0%
530	Install Bathroom Floor Tile	2 days	Wed 11/3/21	Thu 11/4/21	524	Centex	0%
531	Trim out Electrical	2 days	Mon 11/15/21	Tue 11/16/21	529	DPE	0%
532	Trim out HVAC	1 day	Wed 11/17/21	Wed 11/17/21	531	3 C Mechanical	0%
533	Trim out Plumbing	1 day	Mon 11/15/21	Mon 11/15/21	529	Streamline	0%
534	Trim out Data	1 day	Wed 11/17/21	Wed 11/17/21	531	Entry Tech.	0%
535	Electrical Final Inspection	1 day	Wed 11/17/21	Wed 11/17/21	531	DPE	0%
536	HVAC Final Inspection	1 day	Thu 11/18/21	Thu 11/18/21	532	3 C Mechanical	0%
537	Plumbing Final Inspection	1 day	Tue 11/16/21	Tue 11/16/21	533	Streamline	0%
538	Install Bath Acc.	1 day	Tue 11/16/21	Tue 11/16/21	533	Sekresa	0%
539	Install Blinds	1 day	Tue 11/16/21	Tue 11/16/21	533	AZGS	0%
540	Install Interior Door Hardware	1 day	Tue 11/16/21	Tue 11/16/21	533	Rich Craft Doors	0%
541	Install Exterior Door Hardware	1 day	Tue 11/16/21	Tue 11/16/21	533	Rich Craft Doors	0%
542	Blow Insulation in Attic	1 day	Tue 11/16/21	Tue 11/16/21	533	Think Home	0%
543	Prep Floors for LVT	1 day	Tue 11/16/21	Tue 11/16/21	533	Centex	0%
544	Install LVT	2 days	Wed 11/17/21	Thu 11/18/21	543	Centex	0%
545	Install Rubber Base	1 day	Fri 11/19/21	Fri 11/19/21	544	Centex	0%
546	Install Door Steps	1 day	Mon 11/22/21	Mon 11/22/21	545	Sekresa	0%
547	Install Appliances	1 day	Tue 11/23/21	Tue 11/23/21	546	AZGS	0%
548	Construction Clean Unit	1 day	Wed 11/24/21	Wed 11/24/21	547	Sekresa	0%
549	J4 Punch Walk	1 day	Thu 11/25/21	Thu 11/25/21	548	J4 Development	0%
550	J4 Punch Unit	2 days	Fri 11/26/21	Mon 11/29/21	549	J4 Development	0%
551	Building City Final Inspection	1 day	Tue 11/30/21	Tue 11/30/21	550	J4 Development	0%
552	Final Clean Unit	1 day	Wed 12/1/21	Wed 12/1/21	551	Sekresa	0%
553	Architect/Owner Turn Over Walk	1 day	Thu 12/2/21	Thu 12/2/21	552	RDDR/Allied Orion	0%
554							0%
555	Building 213	64 days	Wed 9/1/21	Mon 11/29/21			58%
556	Unit 308 Kennedy Type E	64 days	Wed 9/1/21	Mon 11/29/21			58%
557	Receive possession of Unit	64 days	Wed 9/1/21	Mon 11/29/21		J4 Development	58%
558	Walk unit to verify existing conditions & MEP systems are working	3 days	Wed 9/1/21	Fri 9/3/21		J4 Development	100%
559	Submit 10 day abatement notice	10 days	Wed 9/1/21	Tue 9/14/21		ARC	100%
560	Electrical Demo	1 day	Mon 9/6/21	Mon 9/6/21	558	DPE	100%
561	HVAC Demo	1 day	Mon 9/6/21	Mon 9/6/21	558	3 C Mechanical	100%
562	Plumbing Demo	1 day	Mon 9/6/21	Mon 9/6/21	558	Streamline	100%
563	Fascia Demo & Install New	2 days	Wed 9/1/21	Thu 9/2/21	558	Sekresa	100%
564	New Roof Demo & Install New	2 days	Wed 9/1/21	Thu 9/2/21	558	Texas Built Roofing	100%
565	Interior Soft Demo	1 day	Wed 9/1/21	Wed 9/1/21	558	ARC	100%
566	Abatement	2 days	Wed 9/15/21	Thu 9/16/21	559	ARC	100%
567	Air Test	1 day	Fri 9/17/21	Fri 9/17/21	566	Choice Consulting	100%
568	Remaining Demo Walls & Ceilings	3 days	Mon 9/20/21	Wed 9/22/21	567	ARC	100%
569	Point up Existing Brick	2 days	Wed 9/1/21	Thu 9/2/21	558	Alamo Masonry	100%
570	Install Exterior Stone	3 days	Fri 9/3/21	Tue 9/7/21	569	Alamo Masonry	100%
571	Install new front door with construction	1 day	Wed 9/8/21	Wed 9/8/21	570	Rich Craft Doors	100%
572	Cedar Demo and/or building wrap install	2 days	Wed 9/8/21	Thu 9/9/21	570	Sherman	100%
573	Building Wrap Inspection	1 day	Fri 9/10/21	Fri 9/10/21	572	J4 Development	100%
574	Install Hardie Shake Siding	2 days	Mon 9/13/21	Tue 9/14/21	573	Sherman	100%
575	Install Hardie Soffit Board	1 day	Wed 9/15/21	Wed 9/15/21	574	Sekresa	100%
576	Prime Paint Building Exterior	1 day	Thu 9/16/21	Thu 9/16/21	575	Sekresa	100%
577	Finish Paint Building Exterior	1 day	Fri 9/17/21	Fri 9/17/21	576	Sekresa	100%
578	Pressure Wash Existing CMU	1 day	Thu 9/23/21	Thu 9/23/21	568	Sekresa	100%
579	Install Vapor Barrier	2 days	Tue 9/28/21	Wed 9/29/21	578	Sekresa	100%
580	Install Foam Insulation	1 day	Thu 9/30/21	Thu 9/30/21	579	Sekresa	100%
581	Install Metal Strapping	1 day	Fri 10/1/21	Fri 10/1/21	580	Sekresa	100%

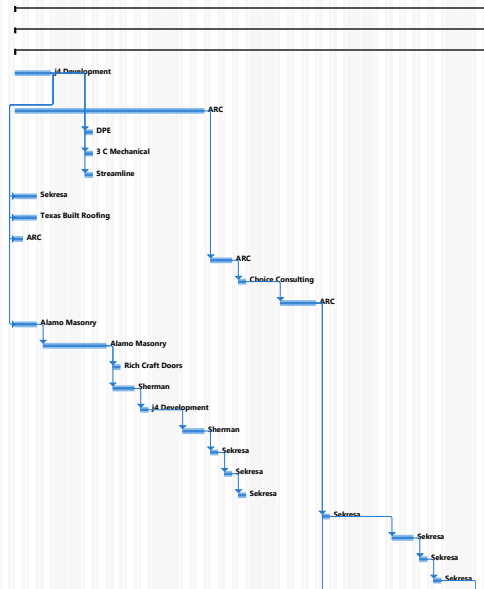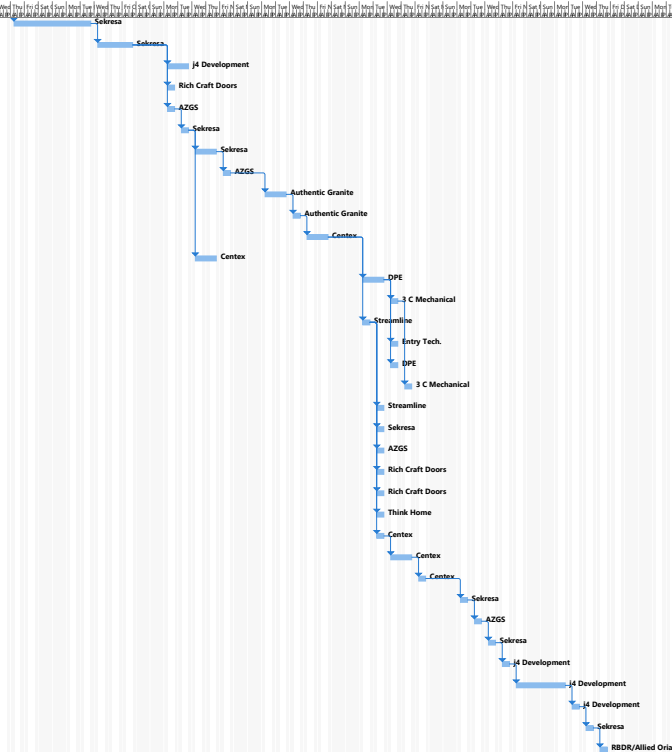

ID	Task	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
582	✓	Install Ceiling Hat Channel	1 day	Thu 9/23/21	Thu 9/23/21	568	Sekresa	100%
583	✓	Install Smoke Barrier	1 day	Thu 9/23/21	Thu 9/23/21	568	Sekresa	100%
584	✓	Install Interior Wall Framing	1 day	Mon 10/4/21	Mon 10/4/21	581	J4 Development	100%
585	✓	Install in Wall Blocking	1 day	Tue 10/5/21	Tue 10/5/21	584	Sekresa	100%
586	✓	J4 Frame Punch	1 day	Tue 10/5/21	Tue 10/5/21	584	Sekresa	100%
587	✓	Install Plumbing R/I	2 days	Wed 10/6/21	Thu 10/7/21	585	Streamline	100%
588	✓	Install HVAC R/I	2 days	Tue 10/5/21	Wed 10/6/21	584	3 C Mechanical	100%
589	✓	Install Electrical R/I	1 day	Tue 10/5/21	Tue 10/5/21	584	DPE	100%
590	✓	Install Data R/I	1 day	Tue 10/5/21	Tue 10/5/21	584	Entry Tech.	100%
591	✓	Plumbing R/I Inspection	1 day	Fri 10/8/21	Fri 10/8/21	587	Streamline	100%
592	✓	HVAC R/I Inspection	1 day	Thu 10/7/21	Thu 10/7/21	588	3 C Mechanical	100%
593	✓	Electrical R/I Inspection	1 day	Tue 10/12/21	Tue 10/12/21	5895+4 days	DPE	100%
594	✓	Smoke Barrier Inspection	1 day	Wed 10/13/21	Wed 10/13/21	593	J4 Development	100%
595	✓	Wall Framing Inspection	1 day	Thu 10/14/21	Thu 10/14/21	594	J4 Development	100%
596	✓	Install Batt Insulation	1 day	Fri 10/15/21	Fri 10/15/21	595	Sekresa	100%
597	✓	Insulation Inspection	1 day	Mon 10/18/21	Mon 10/18/21	596	J4 Development	100%
598	✗	Hang Drywall	3 days	Tue 10/19/21	Thu 10/21/21	597	Sekresa	0%
599	✗	Skim Coat and/or T&T	3 days	Fri 10/22/21	Tue 10/26/21	598	Sekresa	0%
600	✗	J4 Drywall Punch	2 days	Wed 10/27/21	Thu 10/28/21	599	J4 Development	0%
601	✗	Install Interior Doors	1 day	Fri 10/29/21	Fri 10/29/21	600	Rich Craft Doors	0%
602	✗	Install Closet Shelving	1 day	Mon 11/1/21	Mon 11/1/21	601	AZGS	0%
603	✗	Interior Prime Paint	1 day	Tue 11/2/21	Tue 11/2/21	602	Sekresa	0%
604	✗	Interior Finish Paint	2 days	Wed 11/3/21	Thu 11/4/21	603	Sekresa	0%
605	✗	Install Cabinets	1 day	Fri 11/5/21	Fri 11/5/21	604	AZGS	0%
606	✗	Field measure & cut Countertops	2 days	Mon 11/8/21	Tue 11/9/21	605	Authentic Granite	0%
607	✗	Install Countertop	1 day	Wed 11/10/21	Wed 11/10/21	606	Authentic Granite	0%
608	✗	Install Backsplash Tile	2 days	Thu 11/11/21	Fri 11/12/21	607	Centex	0%
609	✗	Install Bathroom Floor Tile	2 days	Fri 11/5/21	Mon 11/8/21	604	Centex	0%
610	✗	Trim out Electrical	2 days	Mon 11/15/21	Tue 11/16/21	608	DPE	0%
611	✗	Trim out HVAC	1 day	Wed 11/17/21	Wed 11/17/21	610	3 C Mechanical	0%
612	✗	Trim out Plumbing	1 day	Mon 11/15/21	Mon 11/15/21	608	Streamline	0%
613	✗	Trim out Data	1 day	Wed 11/17/21	Wed 11/17/21	610	Entry Tech.	0%
614	✗	Electrical Final Inspection	1 day	Wed 11/17/21	Wed 11/17/21	610	DPE	0%
615	✗	HVAC Final Inspection	1 day	Thu 11/18/21	Thu 11/18/21	611	3 C Mechanical	0%
616	✗	Plumbing Final Inspection	1 day	Tue 11/16/21	Tue 11/16/21	612	Streamline	0%
617	✗	Install Bath Acc.	1 day	Tue 11/16/21	Tue 11/16/21	612	Sekresa	0%
618	✗	Install Blinds	1 day	Tue 11/16/21	Tue 11/16/21	612	AZGS	0%
619	✗	Install Interior Door Hardware	1 day	Tue 11/16/21	Tue 11/16/21	612	Rich Craft Doors	0%
620	✗	Install Exterior Door Hardware	1 day	Tue 11/16/21	Tue 11/16/21	612	Rich Craft Doors	0%
621	✗	Blow Insulation in Attic	1 day	Tue 11/16/21	Tue 11/16/21	612	Think Home	0%
622	✗	Prep floors for LVT	1 day	Tue 11/16/21	Tue 11/16/21	612	Centex	0%
623	✗	Install LVT	1 day	Wed 11/17/21	Wed 11/17/21	622	Centex	0%
624	✗	Install Rubber Base	1 day	Thu 11/18/21	Thu 11/18/21	623	Centex	0%
625	✗	Install Door Stops	1 day	Fri 11/19/21	Fri 11/19/21	624	Sekresa	0%
626	✗	Install Appliances	1 day	Thu 11/18/21	Thu 11/18/21	623	AZGS	0%
627	✗	Construction Clean Unit	1 day	Fri 11/19/21	Fri 11/19/21	626	Sekresa	0%
628	✗	J4 Punch Walk	1 day	Mon 11/22/21	Mon 11/22/21	627	J4 Development	0%
629	✗	J4 Punch Unit	2 days	Tue 11/23/21	Wed 11/24/21	628	J4 Development	0%
630	✗	Building City Final Inspection	1 day	Thu 11/25/21	Thu 11/25/21	629	J4 Development	0%
631	✗	Final Clean Unit	1 day	Fri 11/26/21	Fri 11/26/21	630	Sekresa	0%
632	✗	Architect/Owner Turn Over Walk	1 day	Mon 11/29/21	Mon 11/29/21	631	RBD/Allied Orion	0%
633	✗	<New Task>						0%
634	✗	Building 104	77 days	Mon 8/23/21	Tue 12/7/21			54%
635	✗	1000/1202 Carter Type 1	77 days	Mon 8/23/21	Tue 12/7/21			54%
636	✗	Receive possession of Unit	77 days	Mon 8/23/21	Tue 12/7/21		J4 Development	54%
637	✓	Walk unit to verify existing conditions & MEP systems are working	3 days	Mon 8/23/21	Wed 8/25/21		J4 Development	100%
638	✓	Submit 10 day abatement notice	10 days	Mon 8/23/21	Fri 9/3/21		ARC	100%
639	✓	Electrical Demo	1 day	Thu 8/26/21	Thu 8/26/21	637	DPE	100%
640	✓	HVAC Demo	1 day	Thu 8/26/21	Thu 8/26/21	637	3 C Mechanical	100%
641	✓	Plumbing Demo	1 day	Thu 8/26/21	Thu 8/26/21	637	Streamline	100%
642	✓	Fascia Demo & Install New	2 days	Mon 8/23/21	Tue 8/24/21	637	Sekresa	100%
643	✓	New Roof Demo & Install New	2 days	Wed 8/25/21	Thu 8/26/21	642	Texas Built Roofing	100%
644	✓	Interior Soft Demo	1 day	Mon 8/23/21	Mon 8/23/21	637	ARC	100%

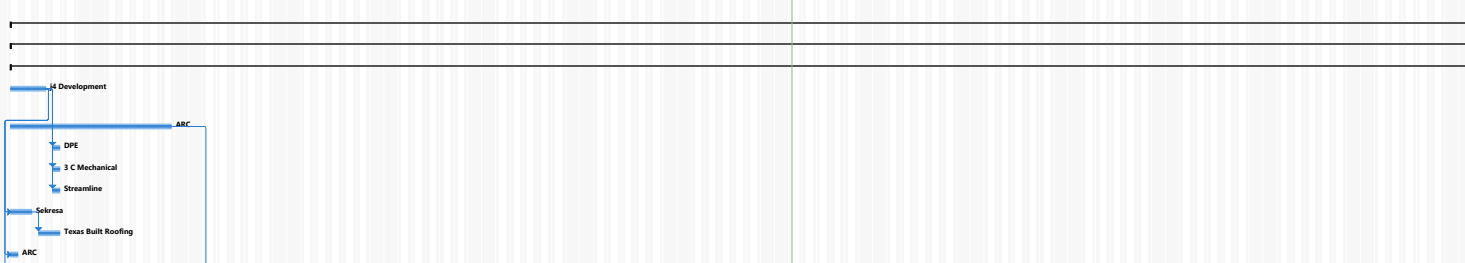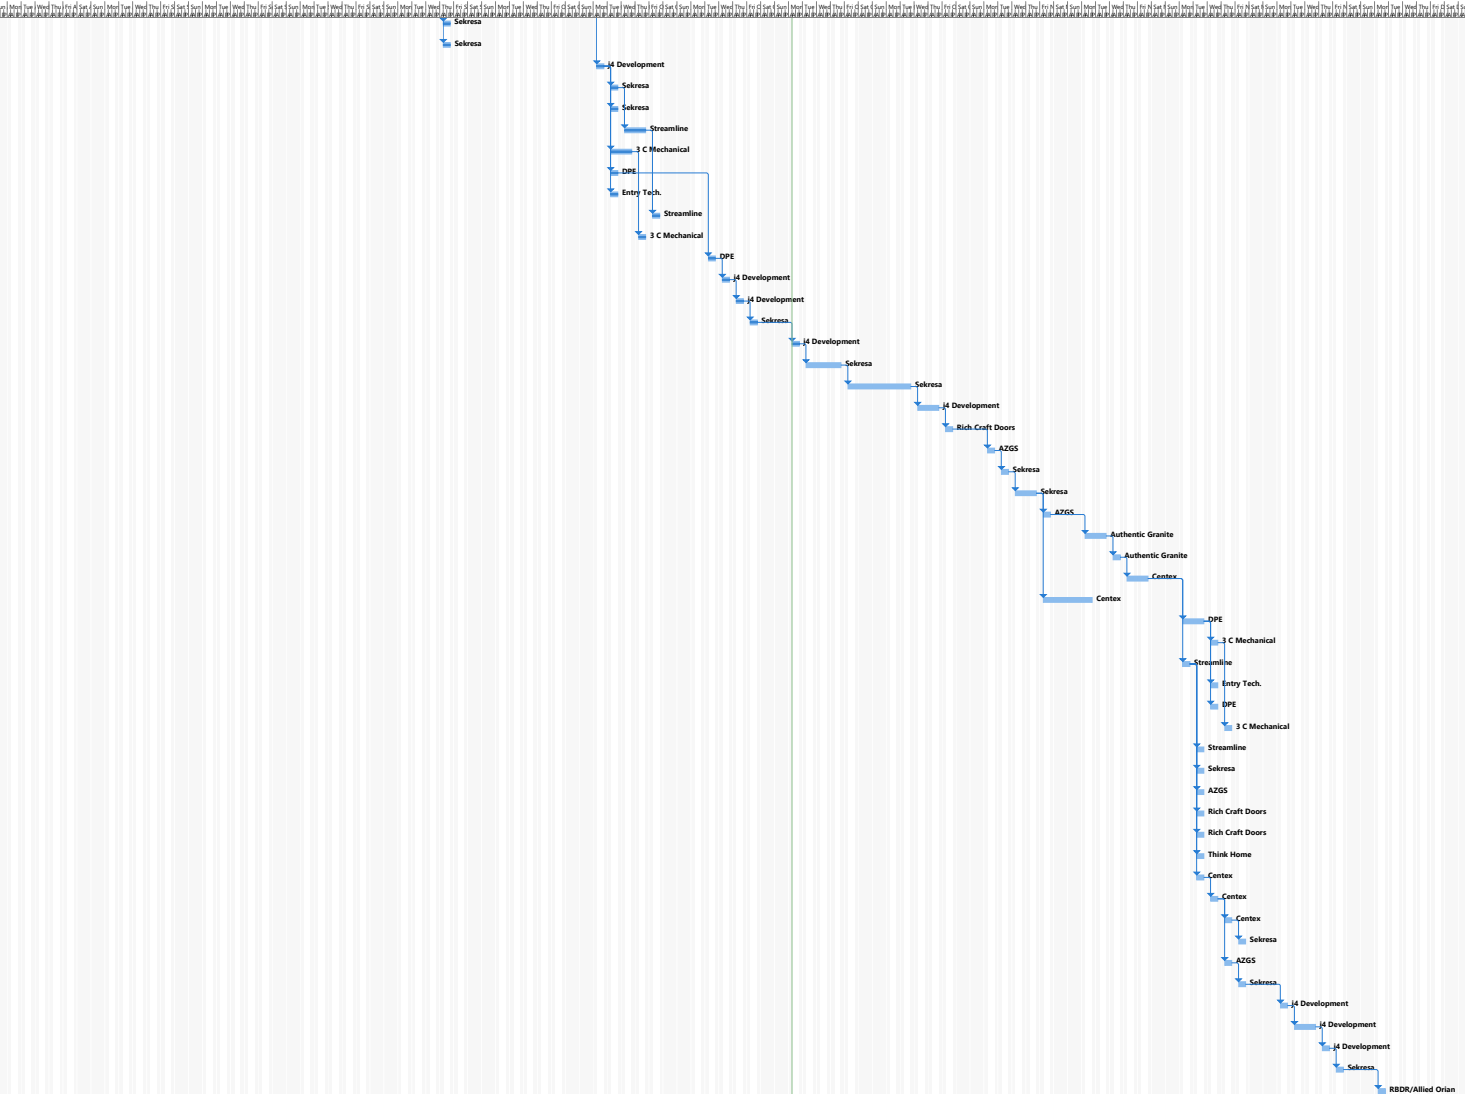

ID	Task	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
645	✓	Abatement	2 days	Mon 9/6/21	Tue 9/7/21	638	ARC	100%
646	✓	Air Test	1 day	Wed 9/8/21	Wed 9/8/21	645	Choice Consulting	100%
647	✓	Remaining Demo Walls & Ceilings	3 days	Thu 9/9/21	Mon 9/13/21	646	ARC	100%
648	✓	Point up Existing Brick	2 days	Mon 8/23/21	Tue 8/24/21	637	Alamo Masonry	100%
649	✓	Install Exterior Stone	3 days	Wed 8/25/21	Fri 8/27/21	648	Alamo Masonry	100%
650	✓	Install new front door with construction	1 day	Mon 8/30/21	Mon 8/30/21	649	Rich Craft Doors	100%
651	✓	Cedar Demo and/or building wrap install	2 days	Mon 8/30/21	Tue 8/31/21	649	Sherman	100%
652	✓	Building Wrap Inspection	1 day	Wed 9/1/21	Wed 9/1/21	651	J4 Development	100%
653	✓	Install Hardie Shake Siding	2 days	Thu 9/2/21	Fri 9/3/21	652	Sherman	100%
654	✓	Install Hardie Soffit Board	1 day	Mon 9/6/21	Mon 9/6/21	653	Sekresa	100%
655	✓	Prime Paint Building Exterior	1 day	Tue 9/7/21	Tue 9/7/21	654	Sekresa	100%
656	✓	Finish Paint Building Exterior	1 day	Wed 9/8/21	Wed 9/8/21	655	Sekresa	100%
657	✓	Pressure Wash Existing CMU	1 day	Fri 9/17/21	Fri 9/17/21	6475+3 days	Sekresa	100%
658	✓	Install Vapor Barrier	2 days	Mon 9/27/21	Tue 9/28/21	6575+5 days	Sekresa	100%
659	✓	Install Foam Insulation	1 day	Wed 9/29/21	Wed 9/29/21	658	Sekresa	100%
660	✓	Install Metal Strapping	1 day	Thu 9/30/21	Thu 9/30/21	659	Sekresa	100%
661	✓	Install Ceiling Hat Channel	1 day	Tue 9/14/21	Tue 9/14/21	647	Sekresa	100%
662	✓	Install Smoke Barrier	1 day	Tue 9/14/21	Tue 9/14/21	647	Sekresa	100%
663	✓	Install Interior Wall Framing	1 day	Fri 10/1/21	Fri 10/1/21	660	J4 Development	100%
664	✓	Install in Wall Blocking	1 day	Mon 10/4/21	Mon 10/4/21	663	Sekresa	100%
665	✓	J4 Frame Punch	1 day	Tue 10/5/21	Tue 10/5/21	664	Sekresa	100%
666	✓	Install Plumbing R/I	2 days	Mon 10/4/21	Tue 10/5/21	663	Streamline	100%
667	✓	Install HVAC R/I	2 days	Wed 9/15/21	Thu 9/16/21	661	3 C Mechanical	100%
668	✓	Install Electrical R/I	2 days	Mon 10/4/21	Tue 10/5/21	663	DPE	100%
669	✓	Install Data R/I	1 day	Mon 10/4/21	Mon 10/4/21	663	Entry Tech.	100%
670	✓	Plumbing R/I Inspection	1 day	Wed 10/6/21	Wed 10/6/21	666	Streamline	100%
671	✓	HVAC R/I Inspection	1 day	Fri 9/17/21	Fri 9/17/21	667	3 C Mechanical	100%
672	✓	Electrical R/I Inspection	1 day	Wed 10/13/21	Wed 10/13/21	668+5 days	DPE	100%
673	✗	Smoke Barrier Inspection	1 day	Wed 10/20/21	Wed 10/20/21	6725+4 days	J4 Development	0%
674	✗	Wall Framing Inspection	1 day	Thu 10/21/21	Thu 10/21/21	673	J4 Development	0%
675	✗	Install Batt Insulation	1 day	Fri 10/22/21	Fri 10/22/21	674	Sekresa	0%
676	✗	Insulation Inspection	1 day	Mon 10/25/21	Mon 10/25/21	675	J4 Development	0%
677	✗	Hang Drywall	3 days	Tue 10/26/21	Thu 10/28/21	676	Sekresa	0%
678	✗	Skim Coat and/or T&T	3 days	Fri 10/29/21	Tue 11/2/21	677	Sekresa	0%
679	✗	J4 Drywall Punch	2 days	Wed 11/3/21	Thu 11/4/21	678	J4 Development	0%
680	✗	Install Interior Doors	1 day	Wed 11/3/21	Wed 11/3/21	678	Rich Craft Doors	0%
681	✗	Install Closet Shelving	1 day	Wed 11/3/21	Wed 11/3/21	678	AZGS	0%
682	✗	Interior Prime Paint	1 day	Thu 11/4/21	Thu 11/4/21	681	Sekresa	0%
683	✗	Interior Finish Paint	2 days	Fri 11/5/21	Mon 11/8/21	682	Sekresa	0%
684	✗	Install Cabinets	1 day	Tue 11/9/21	Tue 11/9/21	683	AZGS	0%
685	✗	Field measure & cut Countertops	2 days	Wed 11/10/21	Thu 11/11/21	684	Authentic Granite	0%
686	✗	Install Countertop	1 day	Fri 11/12/21	Fri 11/12/21	685	Authentic Granite	0%
687	✗	Install Backsplash Tile	2 days	Mon 11/15/21	Tue 11/16/21	686	Centex	0%
688	✗	Install Bathroom Floor Tile	2 days	Tue 11/9/21	Wed 11/10/21	683	Centex	0%
689	✗	Trim out Electrical	2 days	Wed 11/17/21	Thu 11/18/21	687	DPE	0%
690	✗	Trim out HVAC	1 day	Fri 11/19/21	Fri 11/19/21	689	3 C Mechanical	0%
691	✗	Trim out Plumbing	1 day	Wed 11/17/21	Wed 11/17/21	687	Streamline	0%
692	✗	Trim out Data	1 day	Tue 11/9/21	Tue 11/9/21	683	Entry Tech.	0%
693	✗	Electrical Final Inspection	1 day	Fri 11/19/21	Fri 11/19/21	689	DPE	0%
694	✗	HVAC Final Inspection	1 day	Mon 11/22/21	Mon 11/22/21	690	3 C Mechanical	0%
695	✗	Plumbing Final Inspection	1 day	Thu 11/18/21	Thu 11/18/21	691	Streamline	0%
696	✗	Install Bath Acc.	1 day	Thu 11/18/21	Thu 11/18/21	691	Sekresa	0%
697	✗	Install Blinds	1 day	Thu 11/18/21	Thu 11/18/21	691	AZGS	0%
698	✗	Install Interior Door Hardware	1 day	Thu 11/18/21	Thu 11/18/21	691	Rich Craft Doors	0%
699	✗	Install Exterior Door Hardware	1 day	Thu 11/18/21	Thu 11/18/21	691	Rich Craft Doors	0%
700	✗	Blow Insulation in Attic	1 day	Thu 11/18/21	Thu 11/18/21	691	Think Home	0%
701	✗	Prep floors for LVT	2 days	Thu 11/18/21	Fri 11/19/21	691	Centex	0%
702	✗	Install LVT	2 days	Mon 11/22/21	Tue 11/23/21	701	Centex	0%
703	✗	Install Rubber Base	1 day	Wed 11/24/21	Wed 11/24/21	702	Centex	0%
704	✗	Install Door Stops	1 day	Thu 11/25/21	Thu 11/25/21	703	Sekresa	0%
705	✗	Install Appliances	1 day	Fri 11/26/21	Fri 11/26/21	704	AZGS	0%
706	✗	Construction Clean Unit	1 day	Mon 11/29/21	Mon 11/29/21	705	Sekresa	0%
707	✗	J4 Punch Walk	1 day	Tue 11/30/21	Tue 11/30/21	706	J4 Development	0%
708	✗	J4 Punch Unit	2 days	Wed 12/1/21	Thu 12/2/21	707	J4 Development	0%

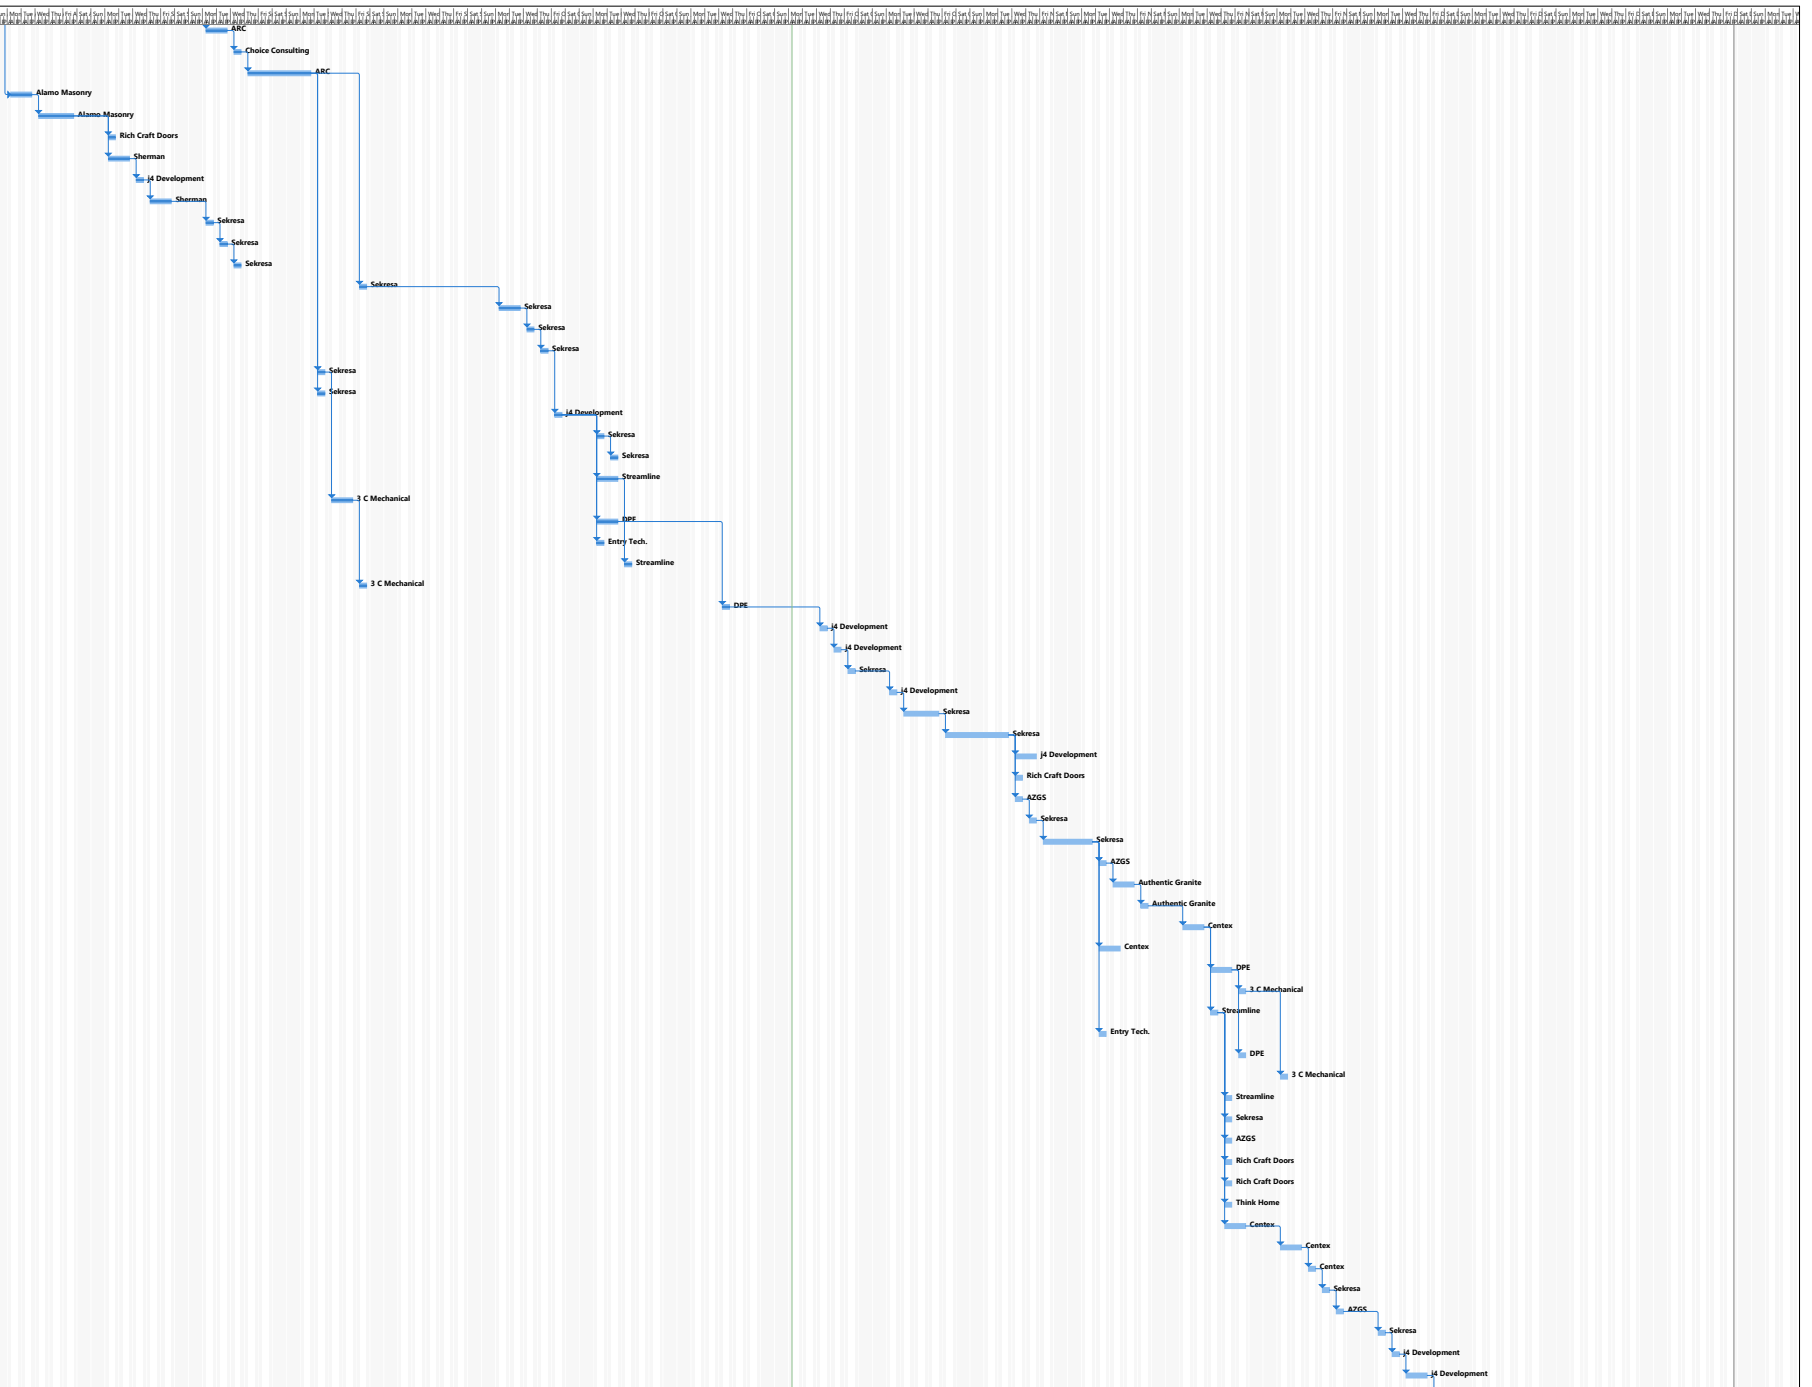

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
709	Building City Final Inspection	1 day	Fri 12/3/21	Fri 12/3/21	708	J4 Development	0%
710	Final Clean Unit	1 day	Mon 12/6/21	Mon 12/6/21	709	Sekresa	0%
711	Architect/Owner Turn Over Walk	1 day	Tue 12/7/21	Tue 12/7/21	710	RBDR/Allied Orion	0%
712							
713	Building 163	81 days	Mon 8/16/21	Mon 12/6/21			57%
714	121/123 Lyndon Type J	81 days	Mon 8/16/21	Mon 12/6/21			57%
715	Receive possession of Unit	81 days	Mon 8/16/21	Mon 12/6/21		J4 Development	57%
716	Walk unit to verify existing conditions & MEP systems are working	3 days	Mon 8/16/21	Wed 8/18/21		J4 Development	100%
717	Submit 10 day abatement notice	10 days	Mon 8/16/21	Fri 8/27/21		ARC	100%
718	Electrical Demo	1 day	Thu 8/19/21	Thu 8/19/21	716	DPE	100%
719	HVAC Demo	1 day	Thu 8/19/21	Thu 8/19/21	716	3 C Mechanical	100%
720	Plumbing Demo	1 day	Thu 8/19/21	Thu 8/19/21	716	Streamline	100%
721	Fascia Demo & Install New	2 days	Mon 8/16/21	Tue 8/17/21	716	Sekresa	100%
722	New Roof Demo & Install New	2 days	Wed 8/18/21	Thu 8/19/21	721	Texas Built Roofing	100%
723	Interior Soft Demo	1 day	Mon 8/16/21	Mon 8/16/21	716	ARC	100%
724	Abatement	2 days	Mon 8/30/21	Tue 8/31/21	717	ARC	100%
725	Air Test	1 day	Wed 9/1/21	Wed 9/1/21	724	Choice Consulting	100%
726	Remaining Demo Walls & Ceilings	3 days	Thu 9/2/21	Mon 9/6/21	725	ARC	100%
727	Paint out Existing Brick	2 days	Mon 8/16/21	Tue 8/17/21	716	Alamo Masonry	100%
728	Install Exterior Stone	3 days	Wed 8/18/21	Fri 8/20/21	727	Alamo Masonry	100%
729	Install new front door with construction	1 day	Mon 8/23/21	Mon 8/23/21	728	Rich Craft Doors	100%
730	Cedar Demo and/or building wrap install	2 days	Tue 8/24/21	Wed 8/25/21	729	Sherman	100%
731	Building Wrap Inspection	1 day	Thu 8/26/21	Thu 8/26/21	730	J4 Development	100%
732	Install Hardie Shake Siding	2 days	Fri 8/27/21	Mon 8/30/21	731	Sherman	100%
733	Install Hardie Soffit Board	1 day	Tue 8/31/21	Tue 8/31/21	732	Sekresa	100%
734	Prime Paint Building Exterior	1 day	Wed 9/1/21	Wed 9/1/21	733	Sekresa	100%
735	Finish Paint Building Exterior	1 day	Thu 9/2/21	Thu 9/2/21	734	Sekresa	100%
736	Pressure Wash Existing CMU	1 day	Tue 9/7/21	Tue 9/7/21	726	Sekresa	100%
737	Install Vapor Barrier	2 days	Mon 9/27/21	Tue 9/28/21	736	Sekresa	100%
738	Install Foam Insulation	1 day	Fri 10/1/21	Fri 10/1/21	737	Sekresa	100%
739	Install Metal Strapping	1 day	Wed 10/6/21	Wed 10/6/21	738	Sekresa	100%
740	Install Ceiling Hat Channel	1 day	Wed 9/8/21	Wed 9/8/21	736	Sekresa	100%
741	Install Smoke Barrier	1 day	Wed 9/8/21	Wed 9/8/21	736	Sekresa	100%
742	Install Interior Wall Framing	1 day	Thu 10/7/21	Thu 10/7/21	739	J4 Development	100%
743	Install in Wall Blocking	1 day	Fri 10/8/21	Fri 10/8/21	742	Sekresa	100%
744	J4 Frame Punch	1 day	Mon 10/11/21	Mon 10/11/21	743	Sekresa	100%
745	Install Plumbing R/I	2 days	Fri 10/8/21	Mon 10/11/21	742	Streamline	100%
746	Install HVAC R/I	2 days	Thu 9/9/21	Fri 9/10/21	740	3 C Mechanical	100%
747	Install Electrical R/I	2 days	Fri 10/8/21	Mon 10/11/21	742	DPE	100%
748	Install Data R/I	1 day	Fri 10/8/21	Fri 10/8/21	742	Entry Tech.	100%
749	Plumbing R/I Inspection	1 day	Tue 10/12/21	Tue 10/12/21	745	Streamline	100%
750	HVAC R/I Inspection	1 day	Mon 9/13/21	Mon 9/13/21	746	3 C Mechanical	100%
751	Electrical R/I Inspection	1 day	Tue 10/12/21	Tue 10/12/21	747	DPE	100%
752	Smoke Barrier Inspection	1 day	Wed 10/13/21	Wed 10/13/21	751	J4 Development	100%
753	Wall Framing Inspection	1 day	Thu 10/14/21	Thu 10/14/21	752	J4 Development	100%
754	Install Batt Insulation	1 day	Fri 10/15/21	Fri 10/15/21	753	Sekresa	100%
755	Insulation Inspection	1 day	Wed 10/20/21	Wed 10/20/21	754	J4 Development	0%
756	Hang Drywall	3 days	Thu 10/21/21	Mon 10/25/21	755	Sekresa	0%
757	Skim Coat and/or TBT	3 days	Tue 10/26/21	Thu 10/28/21	756	Sekresa	0%
758	J4 Drywall Punch	2 days	Fri 10/29/21	Mon 11/1/21	757	J4 Development	0%
759	Install Interior Doors	1 day	Tue 11/2/21	Tue 11/2/21	758	Rich Craft Doors	0%
760	Install Closet Shelving	1 day	Tue 11/2/21	Tue 11/2/21	758	AZGS	0%
761	Interior Prime Paint	1 day	Wed 11/3/21	Wed 11/3/21	759	Sekresa	0%
762	Interior Finish Paint	2 days	Thu 11/4/21	Fri 11/5/21	761	Sekresa	0%
763	Install Cabinets	1 day	Mon 11/8/21	Mon 11/8/21	762	AZGS	0%
764	Field measure & cut Countertops	2 days	Tue 11/9/21	Wed 11/10/21	763	Authentic Granite	0%
765	Install Countertop	1 day	Thu 11/11/21	Thu 11/11/21	764	Authentic Granite	0%
766	Install Backsplash Tile	2 days	Fri 11/12/21	Mon 11/15/21	765	Centex	0%
767	Install Bathroom Floor Tile	2 days	Mon 11/8/21	Tue 11/9/21	762	Centex	0%
768	Trim out Electrical	2 days	Tue 11/16/21	Wed 11/17/21	766	DPE	0%
769	Trim out HVAC	1 day	Thu 11/18/21	Thu 11/18/21	768	3 C Mechanical	0%
770	Trim out Plumbing	1 day	Tue 11/16/21	Tue 11/16/21	766	Streamline	0%
771	Trim out Data	1 day	Thu 11/18/21	Thu 11/18/21	768	Entry Tech.	0%

Project: 10.11.2021 South Terra
Date: Mon 10/18/21

■ Milestone
■ Inactive Milestone
■ Manual Task
■ Manual Summary Rollup
■ Manual Summary
■ Start-only
■ Finish-only
■ External Task
■ External Milestone
■ Deadline
■ Manual Progress
■ Progress

Page 11


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
772	Electrical Final Inspection	1 day	Thu 11/18/21	Thu 11/18/21	768	DPE	0%
773	HVAC Final Inspection	1 day	Fri 11/19/21	Fri 11/19/21	769	3 C Mechanical	0%
774	Plumbing Final Inspection	1 day	Wed 11/17/21	Wed 11/17/21	770	Streamline	0%
775	Install Bath Acc.	1 day	Wed 11/17/21	Wed 11/17/21	770	Sekresa	0%
776	Install Blinds	1 day	Wed 11/17/21	Wed 11/17/21	770	AZGS	0%
777	Install Interior Door Hardware	1 day	Wed 11/17/21	Wed 11/17/21	770	Rich Craft Doors	0%
778	Install Exterior Door Hardware	1 day	Wed 11/17/21	Wed 11/17/21	770	Rich Craft Doors	0%
779	Blow Insulation in Attic	1 day	Wed 11/17/21	Wed 11/17/21	770	Think Home	0%
780	Prep floors for LVT	2 days	Wed 11/17/21	Thu 11/18/21	770	Centex	0%
781	Install LVT	2 days	Fri 11/19/21	Mon 11/22/21	780	Centex	0%
782	Install Rubber Base	1 day	Tue 11/23/21	Tue 11/23/21	781	Centex	0%
783	Install Door Stops	1 day	Wed 11/24/21	Wed 11/24/21	782	Sekresa	0%
784	Install Appliances	1 day	Thu 11/25/21	Thu 11/25/21	783	AZGS	0%
785	Construction Clean Unit	1 day	Fri 11/26/21	Fri 11/26/21	784	Sekresa	0%
786	J4 Punch Walk	1 day	Mon 11/29/21	Mon 11/29/21	785	J4 Development	0%
787	J4 Punch Unit	2 days	Tue 11/30/21	Wed 12/1/21	786	J4 Development	0%
788	Building City Final Inspection	1 day	Thu 12/2/21	Thu 12/2/21	787	J4 Development	0%
789	Final Clean Unit	1 day	Fri 12/3/21	Fri 12/3/21	788	Sekresa	0%
790	Architect/Owner Turn Over Walk	1 day	Mon 12/6/21	Mon 12/6/21	789	RBDR/Allied Orion	0%
791							0%
792	Building 204	90 days	Mon 8/16/21	Fri 12/17/21			50%
793	1105/1107/1109/1111 Gurley Type G	90 days	Mon 8/16/21	Fri 12/17/21			50%
794	Receive possession of Unit	90 days	Mon 8/16/21	Fri 12/17/21		J4 Development	50%
795	Walk unit to verify existing conditions & MEP systems are working	3 days	Mon 8/16/21	Wed 8/18/21		J4 Development	100%
796	Submit 10 day abatement notice	10 days	Mon 8/16/21	Fri 8/27/21		ARC	100%
797	Electrical Demo	1 day	Thu 8/19/21	Thu 8/19/21	795	DPE	100%
798	HVAC Demo	1 day	Thu 8/19/21	Thu 8/19/21	795	3 C Mechanical	100%
799	Plumbing Demo	1 day	Thu 8/19/21	Thu 8/19/21	795	Streamline	100%
800	Fascia Demo & Install New	2 days	Mon 8/16/21	Tue 8/17/21	795	Sekresa	100%
801	New Roof Demo & Install New	2 days	Wed 8/18/21	Thu 8/19/21	800	Texas Built Roofing	100%
802	Interior Soft Demo	1 day	Mon 8/16/21	Mon 8/16/21	795	ARC	100%
803	Abatement	2 days	Mon 8/30/21	Tue 8/31/21	796	ARC	100%
804	Air Test	1 day	Wed 9/1/21	Wed 9/1/21	803	Choice Consulting	100%
805	Remaining Demo Walls & Ceilings	3 days	Thu 9/2/21	Mon 9/6/21	804	ARC	100%
806	Point up Existing Brick	2 days	Mon 8/16/21	Tue 8/17/21	795	Alamo Masonry	100%
807	Install Exterior Stone	3 days	Tue 9/7/21	Thu 9/9/21	805	Alamo Masonry	100%
808	Install new front door with construction	1 day	Fri 9/10/21	Fri 9/10/21	807	Rich Craft Doors	100%
809	Cedar Demo and/or building wrap install	2 days	Mon 9/13/21	Tue 9/14/21	808	Sherman	100%
810	Building Wrap Inspection	1 day	Wed 9/15/21	Wed 9/15/21	809	J4 Development	100%
811	Install Hardie Shake Siding	2 days	Thu 9/16/21	Fri 9/17/21	810	Sherman	100%
812	Install Hardie Soffit Board	1 day	Mon 9/20/21	Mon 9/20/21	811	Sekresa	100%
813	Prime Paint Building Exterior	1 day	Tue 9/21/21	Tue 9/21/21	812	Sekresa	100%
814	Finish Paint Building Exterior	1 day	Wed 9/22/21	Wed 9/22/21	813	Sekresa	100%
815	Pressure Wash Existing CMU	1 day	Tue 9/7/21	Tue 9/7/21	805	Sekresa	100%
816	Install Vapor Barrier	2 days	Tue 9/28/21	Wed 9/29/21	815	Sekresa	100%
817	Install Foam Insulation	2 days	Thu 9/30/21	Fri 10/1/21	816	Sekresa	100%
818	Install Metal Strapping	2 days	Mon 10/4/21	Tue 10/5/21	817	Sekresa	100%
819	Install Ceiling Hat Channel	2 days	Tue 9/7/21	Wed 9/8/21	805	Sekresa	100%
820	Install Smoke Barrier	1 day	Tue 9/7/21	Tue 9/7/21	805	Sekresa	100%
821	Install Interior Wall Framing	2 days	Wed 10/6/21	Thu 10/7/21	818	J4 Development	100%
822	Install in Wall Blocking	1 day	Fri 10/8/21	Fri 10/8/21	821	Sekresa	100%
823	J4 Frame Punch	1 day	Mon 10/11/21	Mon 10/11/21	822	Sekresa	100%
824	Install Plumbing R/	3 days	Fri 10/8/21	Tue 10/12/21	822	Streamline	100%
825	Install HVAC R/	3 days	Thu 9/9/21	Mon 9/13/21	819	3 C Mechanical	100%
826	Install Electrical R/	3 days	Fri 10/8/21	Tue 10/12/21	821	DPE	100%
827	Install Data R/	1 day	Fri 10/8/21	Fri 10/8/21	821	Entry Tech.	100%
828	Plumbing R/ Inspection	1 day	Wed 10/13/21	Wed 10/13/21	824	Streamline	100%
829	HVAC R/ Inspection	1 day	Tue 9/14/21	Tue 9/14/21	825	3 C Mechanical	100%
830	Electrical R/ Inspection	1 day	Fri 10/15/21	Fri 10/15/21	826	DPE	100%
831	Smoke Barrier Inspection	1 day	Tue 10/19/21	Tue 10/19/21	830	J4 Development	0%
832	Wall Framing Inspection	1 day	Wed 10/20/21	Wed 10/20/21	831	J4 Development	0%
833	Install Batt Insulation	1 day	Thu 10/21/21	Thu 10/21/21	832	Sekresa	0%
834	Insulation Inspection	1 day	Fri 10/22/21	Fri 10/22/21	833	J4 Development	0%

Project: 10.11.2021 South Terra Date: Mon 10/18/21

Legend: Milestone, Project Summary, Inactive Milestone, Manual Task, Manual Summary Rollup, Start-only, External Tasks, Deadline, Manual Progress

Page 12

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
835	Hang Drywall	4 days	Mon 10/25/21	Thu 10/28/21	834	Sekresa	0%
836	Skim Coat and/or T&T	4 days	Fri 10/29/21	Wed 11/3/21	835	Sekresa	0%
837	J4 Drywall Punch	2 days	Thu 11/4/21	Fri 11/5/21	836	J4 Development	0%
838	Install Interior Doors	2 days	Mon 11/8/21	Tue 11/9/21	837	Rich Craft Doors	0%
839	Install Closet Shelving	2 days	Mon 11/8/21	Tue 11/9/21	837	AZGS	0%
840	Interior Prime Paint	2 days	Wed 11/10/21	Thu 11/11/21	839	Sekresa	0%
841	Interior Finish Paint	3 days	Fri 11/12/21	Tue 11/16/21	840	Sekresa	0%
842	Install Cabinets	2 days	Wed 11/17/21	Thu 11/18/21	841	AZGS	0%
843	Field measure & cut Countertops	2 days	Fri 11/19/21	Mon 11/22/21	842	Authentic Granite	0%
844	Install Countertop	1 day	Tue 11/23/21	Tue 11/23/21	843	Authentic Granite	0%
845	Install Backsplash Tile	3 days	Wed 11/24/21	Fri 11/26/21	844	Centex	0%
846	Install Bathroom Floor Tile	3 days	Wed 11/24/21	Fri 11/26/21	841	Centex	0%
847	Trim out Electrical	3 days	Mon 11/29/21	Wed 12/1/21	845	DPE	0%
848	Trim out HVAC	2 days	Thu 12/2/21	Fri 12/3/21	847	3 C Mechanical	0%
849	Trim out Plumbing	2 days	Mon 12/29/21	Tue 11/30/21	845	Streamline	0%
850	Trim out Data	1 day	Thu 12/2/21	Thu 12/2/21	847	Entry Tech.	0%
851	Electrical Final Inspection	1 day	Thu 12/2/21	Thu 12/2/21	847	DPE	0%
852	HVAC Final Inspection	1 day	Mon 12/6/21	Mon 12/6/21	848	3 C Mechanical	0%
853	Plumbing Final Inspection	1 day	Wed 12/1/21	Wed 12/1/21	849	Streamline	0%
854	Install Bath Acc.	1 day	Thu 12/2/21	Thu 12/2/21	853	Sekresa	0%
855	Install Blinds	1 day	Thu 12/2/21	Thu 12/2/21	853	AZGS	0%
856	Install Interior Door Hardware	1 day	Thu 12/2/21	Thu 12/2/21	853	Rich Craft Doors	0%
857	Install Exterior Door Hardware	1 day	Thu 12/2/21	Thu 12/2/21	853	Rich Craft Doors	0%
858	Blow Insulation in Attic	1 day	Thu 12/2/21	Thu 12/2/21	853	Think Home	0%
859	Prep Floors for LVT	3 days	Wed 12/1/21	Fri 12/3/21	849	Centex	0%
860	Install LVT	3 days	Mon 12/6/21	Wed 12/8/21	859	Centex	0%
861	Install Rubber Base	2 days	Thu 12/9/21	Fri 12/10/21	860	Centex	0%
862	Install Door Steps	1 day	Mon 12/13/21	Mon 12/13/21	861	Sekresa	0%
863	Install Appliances	1 day	Thu 12/9/21	Thu 12/9/21	860	AZGS	0%
864	Construction Clean Unit	1 day	Thu 12/9/21	Thu 12/9/21	860	Sekresa	0%
865	J4 Punch Walk	1 day	Mon 12/13/21	Mon 12/13/21	861	J4 Development	0%
866	J4 Punch Unit	2 days	Tue 12/14/21	Wed 12/15/21	865	J4 Development	0%
867	Building City Final Inspection	1 day	Fri 12/10/21	Fri 12/10/21	863	J4 Development	0%
868	Final Clean Unit	1 day	Thu 12/16/21	Thu 12/16/21	866	Sekresa	0%
869	Architect/Owner Turn Over Walk	1 day	Fri 12/17/21	Fri 12/17/21	868	RBDR/Allied Orion	0%
870		81 days?	Mon 8/23/21	Mon 12/13/21			32%
871	Building 221	80 days	Mon 8/23/21	Fri 12/10/21			42%
872	Unit 117 Kennedy Type F	80 days	Mon 8/23/21	Fri 12/10/21			42%
873	Receive possession of Unit	80 days	Mon 8/23/21	Fri 12/10/21	J4 Development		42%
874	Walk unit to verify existing conditions & MEP systems are working	3 days	Mon 8/23/21	Wed 8/25/21	J4 Development		100%
875	Submit 10 day abatement notice	10 days	Mon 8/23/21	Fri 9/3/21	ARC		100%
876	Electrical Demo	1 day	Thu 8/26/21	Thu 8/26/21	874	DPE	100%
877	HVAC Demo	1 day	Thu 8/26/21	Thu 8/26/21	874	3 C Mechanical	100%
878	Plumbing Demo	1 day	Thu 8/26/21	Thu 8/26/21	874	Streamline	100%
879	Fascia Demo & Install New	2 days	Mon 8/23/21	Tue 8/24/21	874	Sekresa	100%
880	New Roof Demo & Install New	2 days	Wed 8/25/21	Thu 8/26/21	879	Texas Built Roofing	0%
881	Interior Soft Demo	1 day	Mon 8/23/21	Mon 8/23/21	874	ARC	100%
882	Abatement	2 days	Thu 8/26/21	Fri 8/27/21	874	ARC	100%
883	Air Test	1 day	Mon 8/30/21	Mon 8/30/21	882	Choice Consulting	100%
884	Remaining Demo Walls & Ceilings	3 days	Tue 8/31/21	Thu 9/2/21	883	ARC	100%
885	Point up Existing Brick	2 days	Mon 8/23/21	Tue 8/24/21	874	Alamo Masonry	100%
886	Install Exterior Stone	3 days	Wed 8/25/21	Fri 8/27/21	885	Alamo Masonry	100%
887	Install new front door with construction in	1 day	Mon 8/30/21	Mon 8/30/21	886	Rich Craft Doors	100%
888	Cedar Demo and/or building wrap install	2 days	Tue 8/31/21	Wed 9/1/21	887	Sherman	100%
889	Building Wrap Inspection	1 day	Thu 9/2/21	Thu 9/2/21	888	J4 Development	100%
890	Install Hardie Shake Siding	2 days	Fri 9/3/21	Mon 9/6/21	889	Sherman	100%
891	Install Hardie Soffit Board	1 day	Tue 9/7/21	Tue 9/7/21	890	Sekresa	100%
892	Prime Paint Building Exterior	1 day	Wed 9/8/21	Wed 9/8/21	891	Sekresa	100%
893	Finish Paint Building Exterior	1 day	Thu 9/9/21	Thu 9/9/21	892	Sekresa	100%
894	Pressure Wash Existing CMU	1 day	Thu 9/30/21	Thu 9/30/21	884	Sekresa	100%
895	Install Vapor Barrier	2 days	Fri 10/1/21	Mon 10/4/21	894	Sekresa	100%
896	Install Foam Insulation	1 day	Tue 10/5/21	Tue 10/5/21	895	Sekresa	100%
897	Install Metal Strapping	1 day	Wed 10/6/21	Wed 10/6/21	896	Sekresa	100%

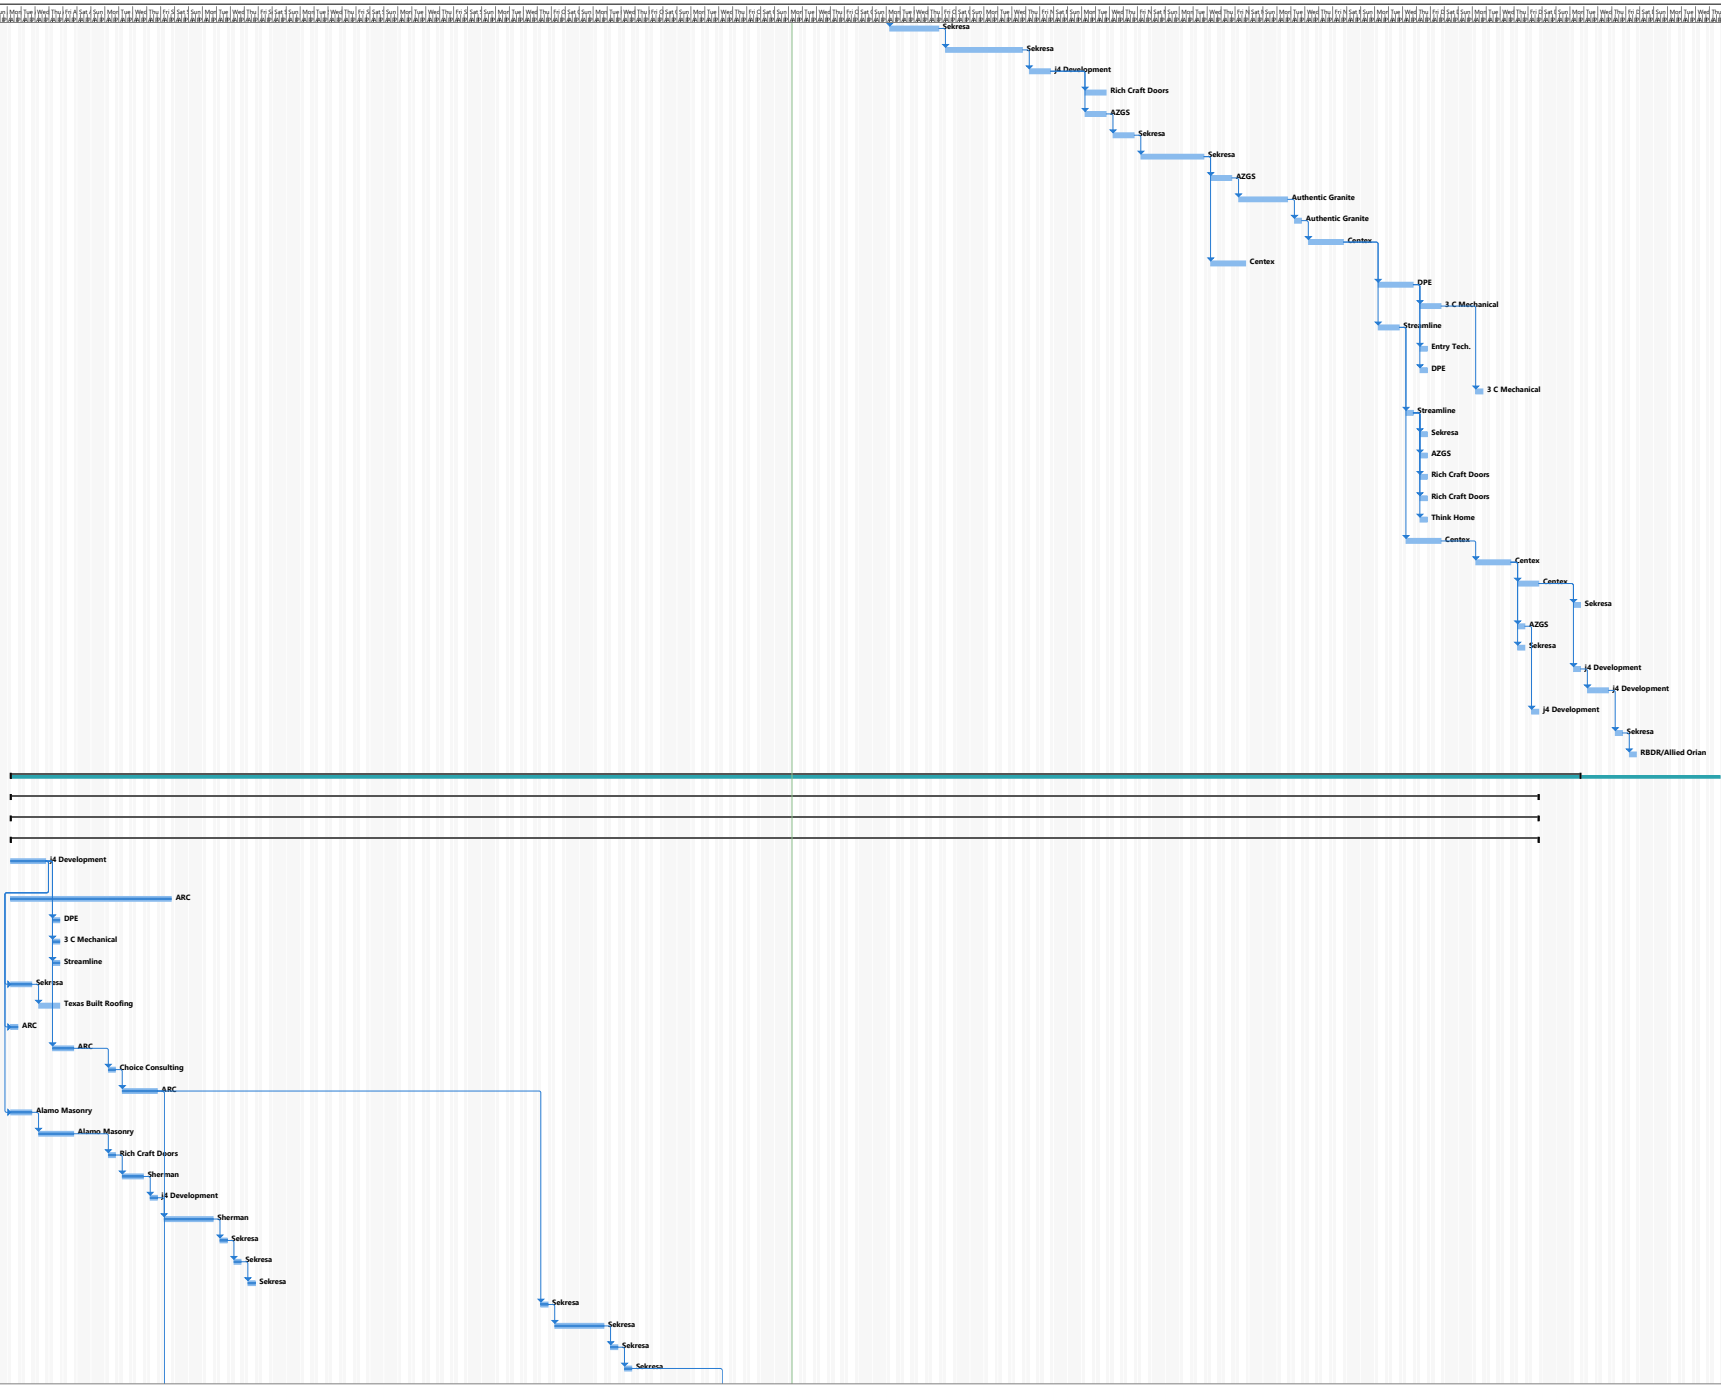


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
896	Install Ceiling Hat Channel	1 day	Fri 9/3/21	Fri 9/3/21	884	Sekresa	100%
899	Install Smoke Barrier	1 day	Fri 9/3/21	Fri 9/3/21	884	Sekresa	100%
900	Install Interior Wall Framing	2 days	Wed 10/13/21	Thu 10/14/21	897,95+4 days	J4 Development	100%
901	Install in Wall Blocking	1 day	Fri 10/15/21	Fri 10/15/21	900	Sekresa	100%
902	J4 Frame Punch	1 day	Mon 10/18/21	Mon 10/18/21	901	Sekresa	0%
903	Install Plumbing R/I	2 days	Mon 10/18/21	Tue 10/19/21	901	Streamline	0%
904	Install HVAC R/I	2 days	Wed 10/20/21	Thu 10/21/21	903	3 C Mechanical	0%
905	Install Electrical R/I	2 days	Wed 10/20/21	Thu 10/21/21	903	DPE	0%
906	Install Data R/I	1 day	Fri 10/22/21	Fri 10/22/21	905	Entry Tech.	0%
907	Plumbing R/I Inspection	1 day	Wed 10/20/21	Wed 10/20/21	903	Streamline	0%
908	HVAC R/I Inspection	1 day	Fri 10/22/21	Fri 10/22/21	904	3 C Mechanical	0%
909	Electrical R/I Inspection	1 day	Fri 10/22/21	Fri 10/22/21	905	DPE	0%
910	Smoke Barrier Inspection	1 day	Mon 10/25/21	Mon 10/25/21	909	J4 Development	0%
911	Wall Framing Inspection	1 day	Tue 10/26/21	Tue 10/26/21	910	J4 Development	0%
912	Install Batt Insulation	1 day	Wed 10/27/21	Wed 10/27/21	911	Sekresa	0%
913	Insulation Inspection	1 day	Thu 10/28/21	Thu 10/28/21	912	J4 Development	0%
914	Hang Drywall	3 days	Fri 10/29/21	Tue 11/2/21	913	Sekresa	0%
915	Skim Coat and/or T&T	3 days	Wed 11/3/21	Fri 11/5/21	914	Sekresa	0%
916	J4 Drywall Punch	2 days	Mon 11/8/21	Tue 11/9/21	915	J4 Development	0%
917	Install Interior Doors	1 day	Wed 11/10/21	Wed 11/10/21	916	Rich Craft Doors	0%
918	Install Closet Shelving	1 day	Wed 11/10/21	Wed 11/10/21	916	AZGS	0%
919	Interior Prime Paint	2 days	Thu 11/11/21	Fri 11/12/21	917	Sekresa	0%
920	Interior Finish Paint	3 days	Mon 11/15/21	Wed 11/17/21	919	Sekresa	0%
921	Install Cabinets	1 day	Thu 11/18/21	Thu 11/18/21	920	AZGS	0%
922	Field measure & cut Countertops	2 days	Fri 11/19/21	Mon 11/22/21	921	Authentic Granite	0%
923	Install Countertop	1 day	Tue 11/23/21	Tue 11/23/21	922	Authentic Granite	0%
924	Install Backsplash Tile	2 days	Wed 11/24/21	Thu 11/25/21	923	Centex	0%
925	Install Bathroom Floor Tile	2 days	Thu 11/18/21	Fri 11/19/21	920	Centex	0%
926	Trim out Electrical	2 days	Fri 11/26/21	Mon 11/29/21	924	DPE	0%
927	Trim out HVAC	1 day	Tue 11/30/21	Tue 11/30/21	926	3 C Mechanical	0%
928	Trim out Plumbing	1 day	Fri 11/26/21	Fri 11/26/21	924	Streamline	0%
929	Trim out Data	1 day	Tue 11/30/21	Tue 11/30/21	926	Entry Tech.	0%
930	Electrical Final Inspection	1 day	Tue 11/30/21	Tue 11/30/21	926	DPE	0%
931	HVAC Final Inspection	1 day	Wed 12/1/21	Wed 12/1/21	927	3 C Mechanical	0%
932	Plumbing Final Inspection	1 day	Mon 11/29/21	Mon 11/29/21	928	Streamline	0%
933	Install Bath Acc.	1 day	Mon 11/29/21	Mon 11/29/21	928	Sekresa	0%
934	Install Blinds	1 day	Mon 11/29/21	Mon 11/29/21	928	AZGS	0%
935	Install Interior Door Hardware	1 day	Mon 11/29/21	Mon 11/29/21	928	Rich Craft Doors	0%
936	Install Exterior Door Hardware	1 day	Mon 11/29/21	Mon 11/29/21	928	Rich Craft Doors	0%
937	Blow Insulation in Attic	1 day	Mon 11/29/21	Mon 11/29/21	928	Think Home	0%
938	Prep floors for LVT	2 days	Mon 11/29/21	Tue 11/30/21	928	Centex	0%
939	Install LVT	2 days	Wed 12/1/21	Thu 12/2/21	938	Centex	0%
940	Install Rubber Base	1 day	Fri 12/3/21	Fri 12/3/21	939	Centex	0%
941	Install Door Stops	1 day	Mon 12/6/21	Mon 12/6/21	940	Sekresa	0%
942	Install Appliances	1 day	Mon 12/6/21	Mon 12/6/21	940	AZGS	0%
943	Construction Clean Unit	1 day	Tue 12/7/21	Tue 12/7/21	942	Sekresa	0%
944	J4 Punch Walk	1 day	Tue 12/7/21	Tue 12/7/21	942	J4 Development	0%
945	J4 Punch Unit	2 days	Wed 12/8/21	Thu 12/9/21	944	J4 Development	0%
946	Building City Final Inspection	1 day	Wed 12/8/21	Wed 12/8/21	944	J4 Development	0%
947	Final Clean Unit	1 day	Thu 12/9/21	Thu 12/9/21	946	Sekresa	0%
948	Architect/Owner Turn Over Walk	1 day	Fri 12/10/21	Fri 12/10/21	947	RBR/Allied Orion	0%
949							0%
950	Building 181	59 days	Mon 10/4/21	Thu 12/23/21			42%
951	2713/2715 S. 12th St. Type 1	59 days	Mon 10/4/21	Thu 12/23/21			42%
952	Receive possession of Unit	59 days	Mon 10/4/21	Thu 12/23/21		J4 Development	42%
953	Walk unit to verify existing conditions & MEP systems are working	3 days	Mon 10/4/21	Wed 10/6/21		J4 Development	100%
954	Submit 10 day abatement notice	10 days	Mon 10/4/21	Fri 10/15/21		ARC	100%
955	Electrical Demo	1 day	Thu 10/7/21	Thu 10/7/21		DPE	100%
956	HVAC Demo	1 day	Thu 10/7/21	Thu 10/7/21		3 C Mechanical	100%
957	Plumbing Demo	1 day	Thu 10/7/21	Thu 10/7/21		Streamline	100%
958	Fascia Demo & Install New	2 days	Mon 10/4/21	Tue 10/5/21		Sekresa	100%
959	New Roof Demo & Install New	2 days	Wed 10/6/21	Thu 10/7/21		Texas Built Roofing	100%
960	Interior Soft Demo	2 days	Mon 10/4/21	Tue 10/5/21		ARC	100%


Project: 10.11.2021 South Terra Date: Mon 10/18/21

Legend: Task (blue bar), Milestone (diamond), Project Summary (black bar), Inactive Milestone (grey bar), Manual Task (green bar), Manual Summary Rollup (teal bar), Start-only (black bar), External Tasks (grey bar), External Milestone (grey diamond), Deadline (grey bar), Manual Progress (blue bar).


Page 14

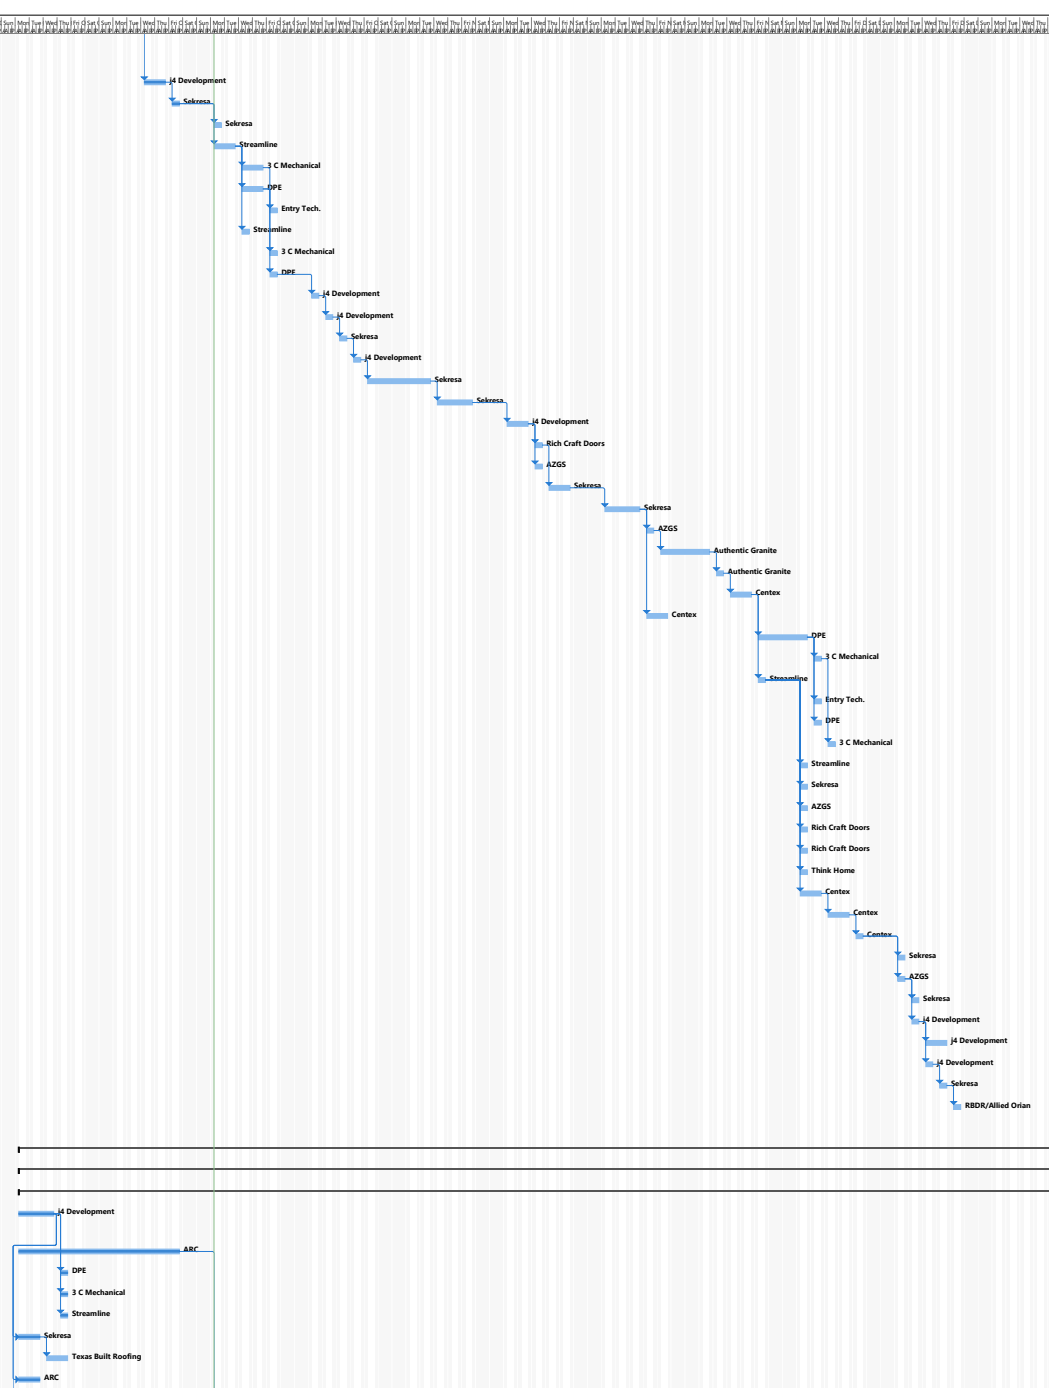


ID	Task	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
961	✓	Abatement	2 days	Mon 10/18/21	Tue 10/20/21	954	ARC	100%
962	✓	Air Test	1 day	Wed 10/20/21	Wed 10/20/21	961	Choice Consulting	100%
963	✓	Remaining Demo Walls & Ceilings	3 days	Thu 10/21/21	Mon 10/25/21	962	ARC	100%
964	✓	Paint up Existing Brick	2 days	Mon 10/4/21	Tue 10/5/21	953	Alamo Masonry	100%
965	✓	Install Exterior Stone	3 days	Wed 10/6/21	Fri 10/8/21	964	Alamo Masonry	100%
966	✓	Install new front door with construction	1 day	Mon 10/11/21	Mon 10/11/21	965	Rich Craft Doors	100%
967	✓	Cedar Demo and/or building wrap install	2 days	Tue 10/12/21	Wed 10/13/21	966	Sherman	100%
968	✓	Building Wrap Inspection	1 day	Thu 10/14/21	Thu 10/14/21	967	J4 Development	100%
969	✓	Install Hardie Shake Siding	2 days	Fri 10/15/21	Mon 10/18/21	968	Sherman	100%
970	✓	Install Hardie Soffit Board	1 day	Tue 10/19/21	Tue 10/19/21	969	Sekresa	100%
971	✓	Prime Paint Building Exterior	1 day	Wed 10/20/21	Wed 10/20/21	970	Sekresa	100%
972	✓	Finish Paint Building Exterior	1 day	Thu 10/21/21	Thu 10/21/21	971	Sekresa	100%
973	✓	Pressure Wash Existing CMU	1 day	Tue 10/26/21	Tue 10/26/21	963	Sekresa	100%
974	✗	PCO 79 2713/2715 Structural Issues	10 days	Wed 10/6/21	Tue 10/19/21	964	Brinshore	0%
975	✗	Structural Issue Repair Work	5 days	Wed 10/20/21	Tue 10/26/21	974	Alamo Masonry	0%
976	✗	Install Vapor Barrier	2 days	Wed 10/27/21	Thu 10/28/21	975	Sekresa	0%
977	✗	Install Foam Insulation	1 day	Fri 10/29/21	Fri 10/29/21	976	Sekresa	0%
978	✗	Install Metal Strapping	1 day	Mon 11/1/21	Mon 11/1/21	977	Sekresa	0%
979	✓	Install Ceiling Hat Channel	1 day	Thu 10/28/21	Thu 10/28/21	975	Sekresa	100%
980	✓	Install Smoke Barrier	1 day	Thu 10/28/21	Thu 10/28/21	975	Sekresa	100%
981	✓	Install Interior Wall Framing	1 day	Wed 11/3/21	Wed 11/3/21	978	Sekresa	100%
982	✓	Install in Wall Blocking	1 day	Thu 11/4/21	Thu 11/4/21	981	Sekresa	100%
983	✓	J4 Frame Punch	1 day	Fri 11/5/21	Fri 11/5/21	982	J4 Development	100%
984	✓	Install Plumbing R/I	2 days	Mon 11/8/21	Tue 11/9/21	983	Streamline	100%
985	✓	Install HVAC R/I	1 day	Fri 10/29/21	Fri 10/29/21	979	3 C Mechanical	100%
986	✓	Install Electrical R/I	1 day	Mon 11/8/21	Mon 11/8/21	983	DPE	100%
987	✓	Install Data R/I	1 day	Mon 11/8/21	Mon 11/8/21	983	Entry Tech.	100%
988	✓	Plumbing R/I Inspection	1 day	Wed 11/10/21	Wed 11/10/21	984	Streamline	100%
989	✓	HVAC R/I Inspection	1 day	Mon 11/1/21	Mon 11/1/21	985	3 C Mechanical	100%
990	✓	Electrical R/I Inspection	1 day	Tue 11/9/21	Tue 11/9/21	986	DPE	100%
991	✗	Smoke Barrier Inspection	1 day	Tue 11/9/21	Tue 11/9/21	987	J4 Development	0%
992	✗	Wall Framing Inspection	1 day	Wed 11/10/21	Wed 11/10/21	991	J4 Development	0%
993	✗	Install Batt Insulation	1 day	Thu 11/11/21	Thu 11/11/21	992	Sekresa	0%
994	✗	Insulation Inspection	3 days	Fri 11/12/21	Tue 11/16/21	993	J4 Development	0%
995	✗	Hang Drywall	3 days	Wed 11/17/21	Fri 11/19/21	994	Sekresa	0%
996	✗	Skim Coat and/or T&T	2 days	Mon 11/22/21	Tue 11/23/21	995	Sekresa	0%
997	✗	J4 Drywall Punch	1 day	Wed 11/24/21	Wed 11/24/21	996	J4 Development	0%
998	✗	Install Interior Doors	1 day	Thu 11/25/21	Thu 11/25/21	997	Rich Craft Doors	0%
999	✗	Install Closet Shelving	1 day	Thu 11/25/21	Thu 11/25/21	997	AZGS	0%
1000	✗	Interior Prime Paint	3 days	Fri 11/26/21	Tue 11/30/21	998	Sekresa	0%
1001	✗	Interior Finish Paint	1 day	Wed 12/1/21	Wed 12/1/21	1000	Sekresa	0%
1002	✗	Install Cabinets	1 day	Thu 12/2/21	Thu 12/2/21	1001	AZGS	0%
1003	✗	Field measure & cut Countertops	2 days	Fri 12/3/21	Mon 12/6/21	1002	Authentic Granite	0%
1004	✗	Install Countertop	1 day	Tue 12/7/21	Tue 12/7/21	1003	Authentic Granite	0%
1005	✗	Install Backsplash Tile	2 days	Wed 12/8/21	Thu 12/9/21	1004	Centex	0%
1006	✗	Install Bathroom Floor Tile	3 days	Thu 12/2/21	Mon 12/6/21	1001	Centex	0%
1007	✗	Trim out Electrical	2 days	Fri 12/10/21	Mon 12/13/21	1005	DPE	0%
1008	✗	Trim out HVAC	1 day	Thu 12/2/21	Thu 12/2/21	1001	3 C Mechanical	0%
1009	✗	Trim out Plumbing	1 day	Tue 12/7/21	Tue 12/7/21	1006	DPE	0%
1010	✗	Trim out Data	1 day	Thu 12/2/21	Thu 12/2/21	1001	Entry Tech.	0%
1011	✗	Electrical Final Inspection	1 day	Tue 12/14/21	Tue 12/14/21	1007	DPE	0%
1012	✗	HVAC Final Inspection	1 day	Fri 12/3/21	Fri 12/3/21	1008	3 C Mechanical	0%
1013	✗	Plumbing Final Inspection	1 day	Wed 12/8/21	Wed 12/8/21	1009	Streamline	0%
1014	✗	Install Bath Acc.	1 day	Thu 12/2/21	Thu 12/2/21	1001	Sekresa	0%
1015	✗	Install Blinds	1 day	Thu 12/2/21	Thu 12/2/21	1001	AZGS	0%
1016	✗	Install Interior Door Hardware	1 day	Thu 12/2/21	Thu 12/2/21	1001	Rich Craft Doors	0%
1017	✗	Install Exterior Door Hardware	1 day	Thu 12/2/21	Thu 12/2/21	1001	Rich Craft Doors	0%
1018	✗	Blow Insulation in Attic	1 day	Wed 12/8/21	Wed 12/8/21	1009	Think Home	0%
1019	✗	Prep floors for LVT	1 day	Wed 12/8/21	Wed 12/8/21	1009	Centex	0%
1020	✗	Install LVT	2 days	Thu 12/9/21	Fri 12/10/21	1019	Centex	0%
1021	✗	Install Rubber Base	1 day	Mon 12/13/21	Mon 12/13/21	1020	Centex	0%
1022	✗	Install Door Stops	1 day	Tue 12/14/21	Tue 12/14/21	1021	Sekresa	0%
1023	✗	Install Appliances	1 day	Tue 12/14/21	Tue 12/14/21	1021	AZGS	0%
1024	✗	Construction Clean Unit	1 day	Wed 12/15/21	Wed 12/15/21	1023	Sekresa	0%

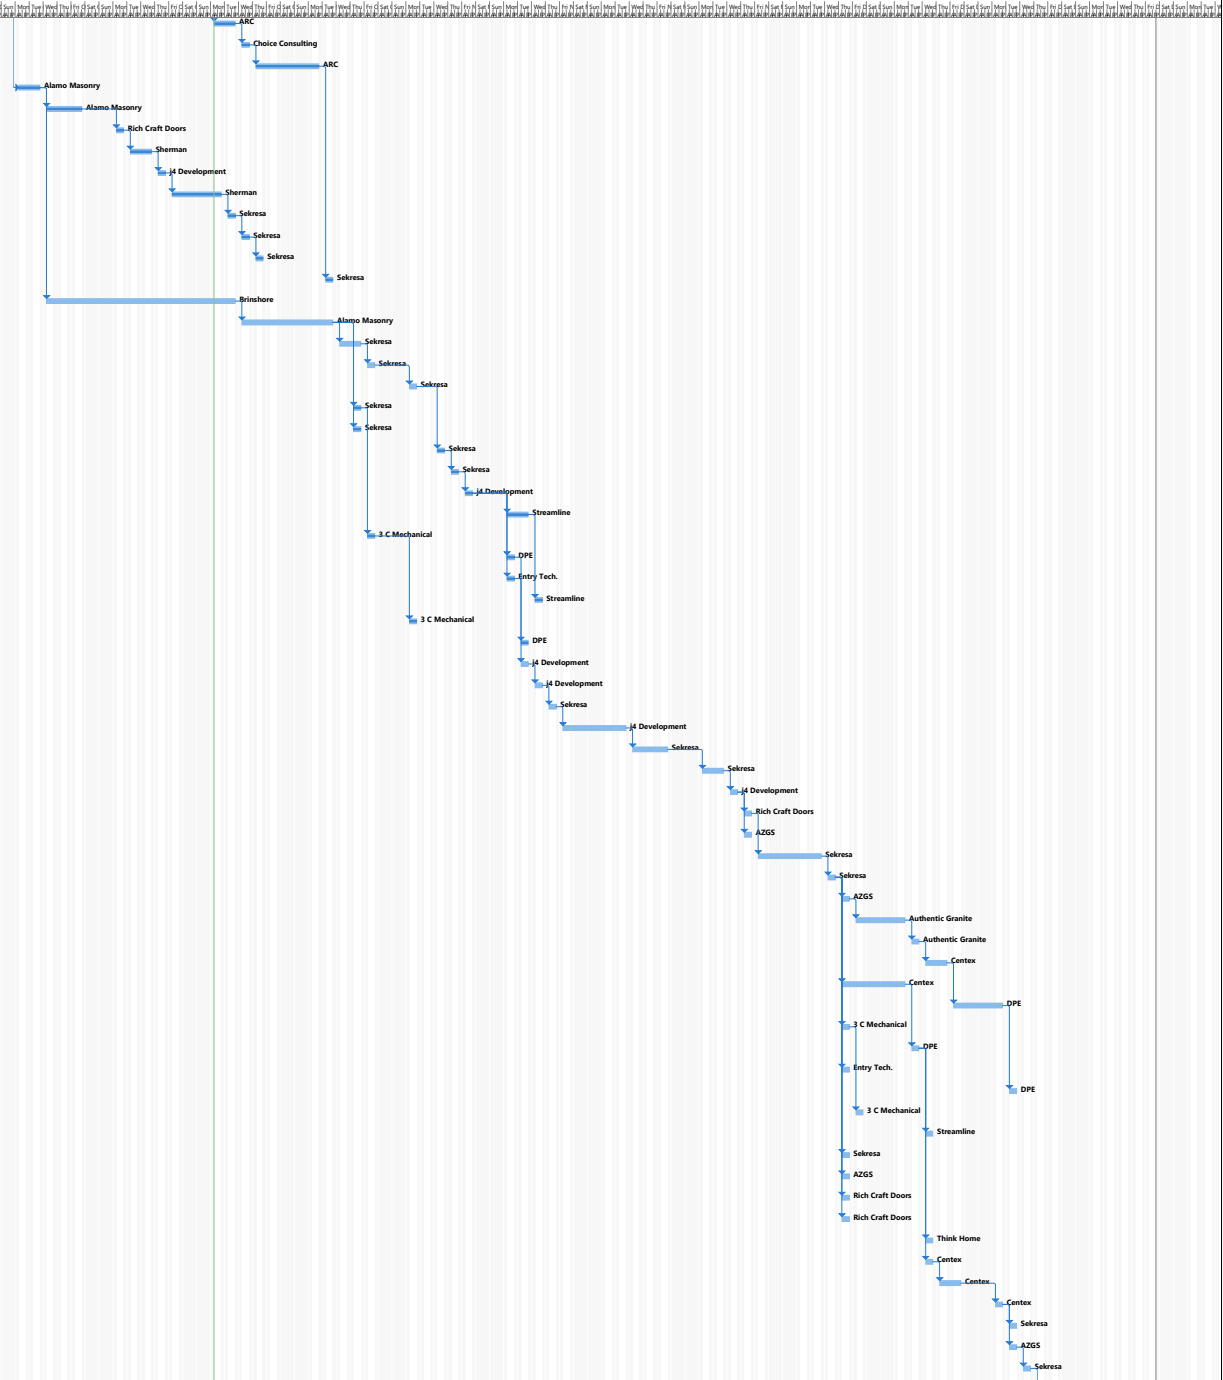



ID	Task	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
1023	1023	J4 Punch Walk	1 day	Thu 12/16/21	Thu 12/16/21	1024	J4 Development	0%
1024	1024	J4 Punch Unit	2 days	Fri 12/17/21	Mon 12/20/21	1025	J4 Development	0%
1027	1027	Building City Final Inspection	1 day	Tue 12/21/21	Tue 12/21/21	1026	J4 Development	0%
1028	1028	Final Clean Unit	1 day	Wed 12/22/21	Wed 12/22/21	1027	Sekresa	0%
1029	1029	Architect/Owner Turn Over Walk	1 day	Thu 12/23/21	Thu 12/23/21	1028	RBOR/Allied Orion	0%
1030	1030							0%
1031	1031	Building 154	58 days	Tue 9/28/21	Thu 12/16/21			20%
1032	1032	2700/2702 S. 14th St Type A	58 days	Tue 9/28/21	Thu 12/16/21			20%
1033	1033	Receive possession of Unit	58 days	Tue 9/28/21	Thu 12/16/21		J4 Development	20%
1034	1034	Walk unit to verify existing conditions & MEP systems are working	3 days	Tue 9/28/21	Thu 9/30/21		J4 Development	100%
1035	1035	Submit 10 day abatement notice	10 days	Tue 9/28/21	Mon 10/11/21		ARC	100%
1036	1036	Electrical Demo	1 day	Fri 10/1/21	Fri 10/1/21	1034	DPE	100%
1037	1037	HVAC Demo	1 day	Fri 10/1/21	Fri 10/1/21	1034	3 C Mechanical	100%
1038	1038	Plumbing Demo	1 day	Fri 10/1/21	Fri 10/1/21	1034	Streamline	100%
1039	1039	Fascia Demo & Install New	2 days	Tue 9/28/21	Wed 9/29/21	1034	Sekresa	100%
1040	1040	New Roof Demo & Install New	2 days	Thu 9/30/21	Fri 10/1/21	1039	Texas Built Roofing	0%
1041	1041	Interior Soft Demo	2 days	Tue 9/28/21	Wed 9/29/21	1034	ARC	100%
1042	1042	Abatement	2 days	Tue 10/12/21	Wed 10/13/21	1035	ARC	100%
1043	1043	Air Test	1 day	Thu 10/14/21	Thu 10/14/21	1042	Choice Consulting	100%
1044	1044	Remaining Demo Walls & Ceilings	1 day	Fri 10/15/21	Fri 10/15/21	1043	ARC	100%
1045	1045	Point up Existing Brick	2 days	Tue 9/28/21	Wed 9/29/21	1034	Alamo Masonry	100%
1046	1046	Install Exterior Stone	3 days	Thu 9/30/21	Mon 10/4/21	1045	Alamo Masonry	100%
1047	1047	RFI 90 Add Siding at Rear of Building	10 days	Fri 10/1/21	Thu 10/14/21	1046's 2 days	Birishore	0%
1048	1048	Install new front door with construction	1 day	Fri 10/15/21	Fri 10/15/21	1047	Rich Craft Doors	100%
1049	1049	Cedar Demo and/or building wrap install	2 days	Mon 10/18/21	Tue 10/19/21	1048	Sherman	0%
1050	1050	Building Wrap Inspection	1 day	Wed 10/20/21	Wed 10/20/21	1049	J4 Development	0%
1051	1051	Install Hardie Shake Siding	2 days	Thu 10/21/21	Fri 10/22/21	1050	Sherman	0%
1052	1052	Install Hardie Soffit Board	1 day	Mon 10/25/21	Mon 10/25/21	1051	Sekresa	0%
1053	1053	Prime Paint Building Exterior	1 day	Tue 10/26/21	Tue 10/26/21	1052	Sekresa	0%
1054	1054	Finish Paint Building Exterior	1 day	Wed 10/27/21	Wed 10/27/21	1053	Sekresa	0%
1055	1055	Install Smoke Barrier	1 day	Mon 10/18/21	Mon 10/18/21	1044	Sekresa	0%
1056	1056	Install Interior Wall Framing	1 day	Tue 10/19/21	Tue 10/19/21	1055	Sekresa	0%
1057	1057	Install in Wall Blocking	1 day	Wed 10/20/21	Wed 10/20/21	1056	Sekresa	0%
1058	1058	J4 Frame Punch	1 day	Thu 10/21/21	Thu 10/21/21	1057	J4 Development	0%
1059	1059	Install Plumbing R/I	2 days	Fri 10/22/21	Mon 10/25/21	1058	Streamline	0%
1060	1060	Install HVAC R/I	2 days	Tue 10/26/21	Wed 10/27/21	1059	3 C Mechanical	0%
1061	1061	Install Electrical R/I	2 days	Thu 10/28/21	Fri 10/29/21	1060	DPE	0%
1062	1062	Install Data R/I	1 day	Mon 11/1/21	Mon 11/1/21	1061	Entry Tech.	0%
1063	1063	Plumbing R/I Inspection	1 day	Tue 10/26/21	Tue 10/26/21	1059	Streamline	0%
1064	1064	HVAC R/I Inspection	1 day	Thu 10/28/21	Thu 10/28/21	1060	3 C Mechanical	0%
1065	1065	Electrical R/I Inspection	1 day	Mon 11/1/21	Mon 11/1/21	1061	DPE	0%
1066	1066	Smoke Barrier Inspection	1 day	Tue 11/2/21	Tue 11/2/21	1065	J4 Development	0%
1067	1067	Wall Framing Inspection	1 day	Wed 11/3/21	Wed 11/3/21	1066	J4 Development	0%
1068	1068	Install Batt Insulation	1 day	Thu 11/4/21	Thu 11/4/21	1067	Sekresa	0%
1069	1069	Insulation Inspection	1 day	Fri 11/5/21	Fri 11/5/21	1068	J4 Development	0%
1070	1070	Hang Drywall	1 day	Mon 11/8/21	Mon 11/8/21	1069	Sekresa	0%
1071	1071	Skim Coat and/or TBT	3 days	Tue 11/9/21	Thu 11/11/21	1070	Sekresa	0%
1072	1072	J4 Drywall Punch	1 day	Fri 11/12/21	Fri 11/12/21	1071	J4 Development	0%
1073	1073	Install Interior Doors	1 day	Mon 11/15/21	Mon 11/15/21	1072	Rich Craft Doors	0%
1074	1074	Install Closet Shelving	1 day	Mon 11/15/21	Mon 11/15/21	1072	AZGS	0%
1075	1075	Interior Prime Paint	2 days	Tue 11/16/21	Wed 11/17/21	1073	Sekresa	0%
1076	1076	Interior Finish Paint	3 days	Thu 11/18/21	Mon 11/22/21	1075	Sekresa	0%
1077	1077	Install Cabinets	1 day	Tue 11/23/21	Tue 11/23/21	1076	AZGS	0%
1078	1078	Field measure & cut Countertops	2 days	Wed 11/24/21	Thu 11/25/21	1077	Authentic Granite	0%
1079	1079	Install Countertop	1 day	Fri 11/26/21	Fri 11/26/21	1078	Authentic Granite	0%
1080	1080	Install Backsplash Tile	2 days	Mon 11/29/21	Tue 11/30/21	1079	Centex	0%
1081	1081	Install Bathroom Floor Tile	2 days	Wed 12/1/21	Thu 12/2/21	1080	Centex	0%
1082	1082	Trim out Electrical	2 days	Wed 12/1/21	Thu 12/2/21	1080	DPE	0%
1083	1083	Trim out HVAC	2 days	Fri 12/3/21	Mon 12/6/21	1082	3 C Mechanical	0%
1084	1084	Trim out Plumbing	2 days	Wed 12/1/21	Thu 12/2/21	1080	Streamline	0%
1085	1085	Trim out Data	1 day	Fri 12/3/21	Fri 12/3/21	1082	Entry Tech.	0%
1086	1086	Electrical Final Inspection	1 day	Fri 12/3/21	Fri 12/3/21	1082	DPE	0%
1087	1087	HVAC Final Inspection	1 day	Tue 12/7/21	Tue 12/7/21	1083	3 C Mechanical	0%

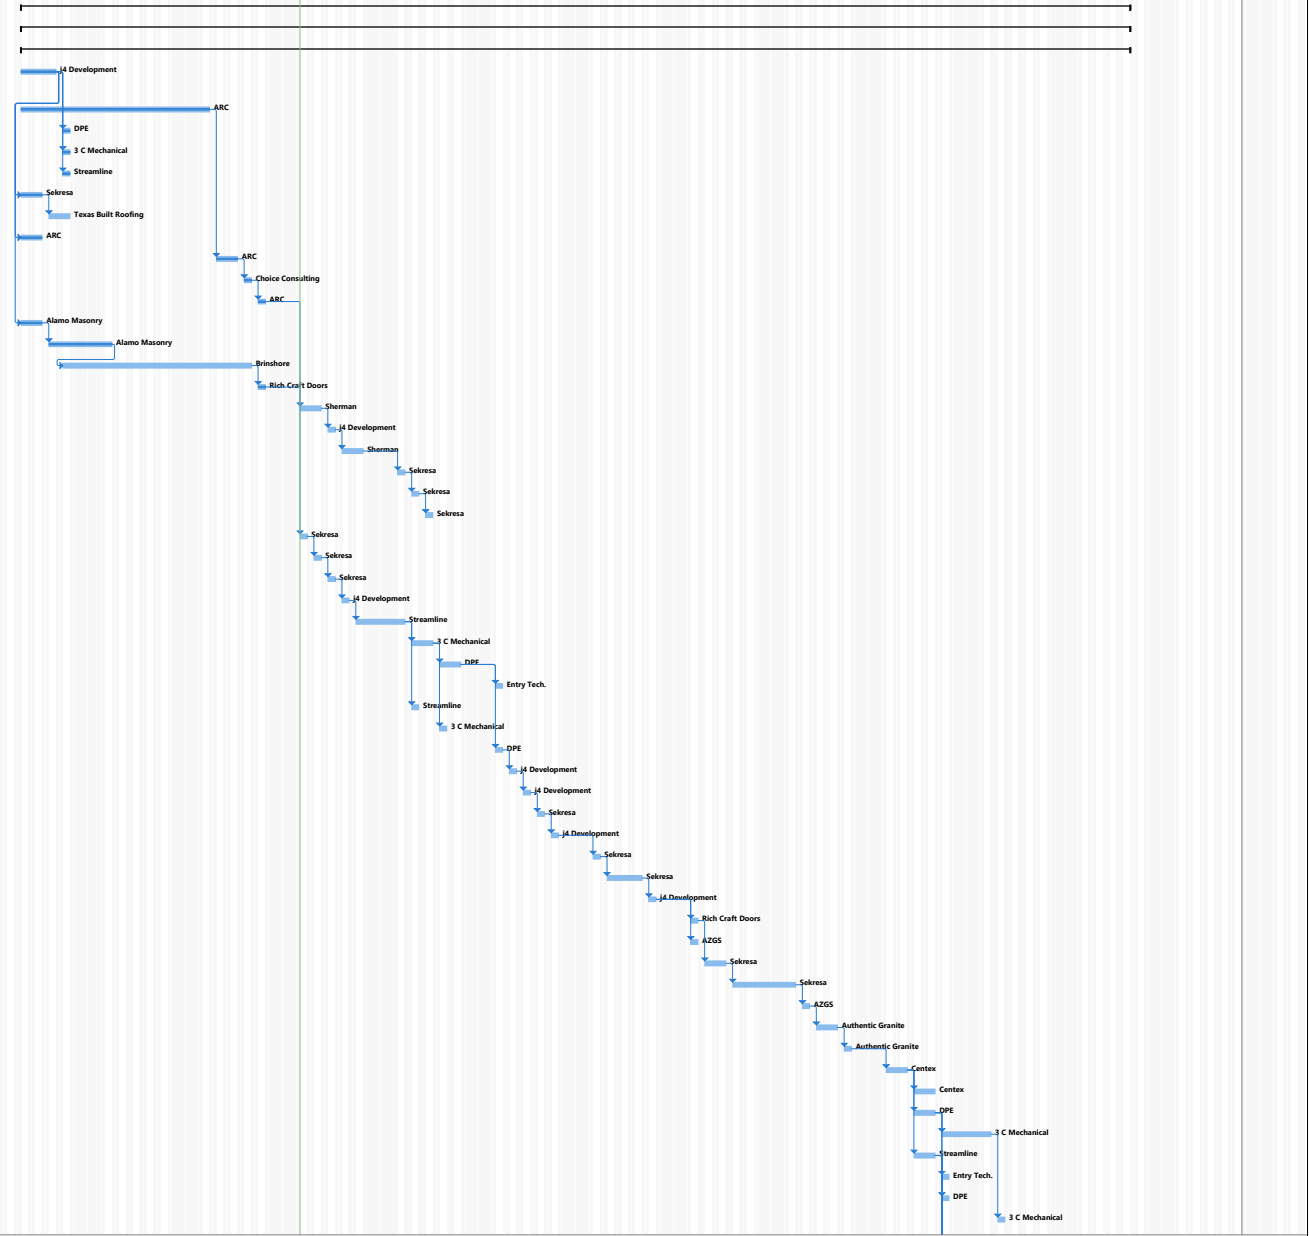


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
1088	Plumbing Final Inspection	1 day	Fri 12/3/21	Fri 12/3/21	1084	Streamline	0%
1089	Install Bath Acc.	1 day	Fri 12/3/21	Fri 12/3/21	1084	Sekresa	0%
1090	Install Blinds	1 day	Fri 12/3/21	Fri 12/3/21	1084	AZGS	0%
1091	Install Interior Door Hardware	1 day	Fri 12/3/21	Fri 12/3/21	1084	Rich Craft Doors	0%
1092	Install Exterior Door Hardware	1 day	Fri 12/3/21	Fri 12/3/21	1084	Rich Craft Doors	0%
1093	Blow Insulation in Attic	1 day	Fri 12/3/21	Fri 12/3/21	1084	Think Home	0%
1094	Prep Floors for LVT	1 day	Fri 12/3/21	Fri 12/3/21	1084	Centex	0%
1095	Install LVT	1 day	Mon 12/6/21	Mon 12/6/21	1094	Centex	0%
1096	Install Rubber Base	1 day	Tue 12/7/21	Tue 12/7/21	1095	Centex	0%
1097	Install Door Steps	1 day	Wed 12/8/21	Wed 12/8/21	1096	Sekresa	0%
1098	Install Appliances	1 day	Wed 12/8/21	Wed 12/8/21	1096	AZGS	0%
1099	Construction Clean Unit	1 day	Thu 12/9/21	Thu 12/9/21	1097	Sekresa	0%
1100	J4 Punch Walk	2 days	Thu 12/9/21	Fri 12/10/21	1098	J4 Development	0%
1101	J4 Punch Unit	1 day	Mon 12/13/21	Mon 12/13/21	1100	J4 Development	0%
1102	Building City Final Inspection	1 day	Tue 12/14/21	Tue 12/14/21	1101	J4 Development	0%
1103	Final Clean Unit	1 day	Wed 12/15/21	Wed 12/15/21	1102	Sekresa	0%
1104	Architect/Owner Turn Over Walk	1 day	Thu 12/16/21	Thu 12/16/21	1103	RBDR/Allied Orion	0%
1105							
1106	Building 109	62 days	Tue 9/28/21	Wed 12/22/21			26%
1107	2634/2636 S. 14th St Type B	62 days	Tue 9/28/21	Wed 12/22/21			26%
1108	Receive possession of Unit	62 days	Tue 9/28/21	Wed 12/22/21		J4 Development	26%
1109	Walk unit to verify existing conditions & MEP systems are working	3 days	Tue 9/28/21	Thu 9/30/21		J4 Development	100%
1110	Submit 10 day abatement notice	10 days	Tue 9/28/21	Mon 10/11/21		ARC	100%
1111	Electrical Demo	1 day	Fri 10/1/21	Fri 10/1/21	1109	DPE	100%
1112	HVAC Demo	1 day	Fri 10/1/21	Fri 10/1/21	1109	3 C Mechanical	100%
1113	Plumbing Demo	1 day	Fri 10/1/21	Fri 10/1/21	1109	Streamline	100%
1114	Fascia Demo & Install New	2 days	Tue 9/28/21	Wed 9/29/21	1109	Sekresa	100%
1115	New Roof Demo & Install New	2 days	Thu 9/30/21	Fri 10/1/21	1114	Texas Built Roofing	0%
1116	Interior Soft Demo	2 days	Tue 9/28/21	Wed 9/29/21	1109	ARC	100%
1117	Abatement	2 days	Tue 10/12/21	Wed 10/13/21	1110	ARC	100%
1118	Air Test	1 day	Thu 10/14/21	Thu 10/14/21	1117	Choice Consulting	100%
1119	Remaining Demo Walls & Ceilings	1 day	Fri 10/15/21	Fri 10/15/21	1118	ARC	100%
1120	Point up Existing Brick	2 days	Tue 9/28/21	Wed 9/29/21	1109	Alamo Masonry	100%
1121	Install Exterior Stone	3 days	Thu 9/30/21	Mon 10/4/21	1120	Alamo Masonry	100%
1122	RFI #7 Rotted Cedar at Gables	10 days	Wed 10/6/21	Tue 10/19/21	1120P5+4 days	Brinshore	0%
1123	Install new front door with construction lo	1 day	Fri 10/15/21	Fri 10/15/21	1123P5+3 days	Rich Craft Doors	100%
1124	Cedar Demo and/or building wrap install	2 days	Mon 10/18/21	Tue 10/19/21	1123	Sherman	0%
1125	Building Wrap Inspection	1 day	Wed 10/20/21	Wed 10/20/21	1124	J4 Development	0%
1126	Install Hardie Shake Siding	2 days	Thu 10/21/21	Fri 10/22/21	1125	Sherman	0%
1127	Install Hardie Soffit Board	1 day	Mon 10/25/21	Mon 10/25/21	1126	Sekresa	0%
1128	Prime Paint Building Exterior	1 day	Tue 10/26/21	Tue 10/26/21	1127	Sekresa	0%
1129	Finish Paint Building Exterior	1 day	Wed 10/27/21	Wed 10/27/21	1128	Sekresa	0%
1130	Install Smoke Barrier	1 day	Mon 10/18/21	Mon 10/18/21	1119	Sekresa	0%
1131	Install Interior Wall Framing	1 day	Tue 10/19/21	Tue 10/19/21	1130	Sekresa	0%
1132	Install in Wall Blocking	1 day	Wed 10/20/21	Wed 10/20/21	1131	Sekresa	0%
1133	J4 Frame Punch	1 day	Thu 10/21/21	Thu 10/21/21	1132	J4 Development	0%
1134	Install Plumbing R/	2 days	Fri 10/22/21	Mon 10/25/21	1133	Streamline	0%
1135	Install HVAC R/	2 days	Fri 10/22/21	Mon 10/25/21	1133	3 C Mechanical	0%
1136	Install Electrical R/	2 days	Tue 10/26/21	Wed 10/27/21	1135	DPE	0%
1137	Install Data R/	1 day	Fri 10/22/21	Fri 10/22/21	1133	Entry Tech.	0%
1138	Plumbing R/ Inspection	1 day	Tue 10/26/21	Tue 10/26/21	1134	Streamline	0%
1139	HVAC R/ Inspection	1 day	Tue 10/26/21	Tue 10/26/21	1135	3 C Mechanical	0%
1140	Electrical R/ Inspection	1 day	Thu 10/28/21	Thu 10/28/21	1136	DPE	0%
1141	Smoke Barrier Inspection	1 day	Fri 10/29/21	Fri 10/29/21	1140	J4 Development	0%
1142	Wall Framing Inspection	1 day	Mon 11/1/21	Mon 11/1/21	1141	J4 Development	0%
1143	Install Batt Insulation	1 day	Tue 11/2/21	Tue 11/2/21	1142	Sekresa	0%
1144	Insulation Inspection	1 day	Wed 11/3/21	Wed 11/3/21	1143	J4 Development	0%
1145	Hang Drywall	1 day	Thu 11/4/21	Thu 11/4/21	1144	Sekresa	0%
1146	Skim Coat and/or T&T	3 days	Fri 11/5/21	Tue 11/9/21	1145	Sekresa	0%
1147	J4 Drywall Punch	1 day	Wed 11/10/21	Wed 11/10/21	1146	J4 Development	0%
1148	Install Interior Doors	1 day	Thu 11/11/21	Thu 11/11/21	1147	Rich Craft Doors	0%
1149	Install Closet Shelving	1 day	Thu 11/11/21	Thu 11/11/21	1147	AZGS	0%
1150	Interior Prime Paint	2 days	Fri 11/12/21	Mon 11/15/21	1148	Sekresa	0%

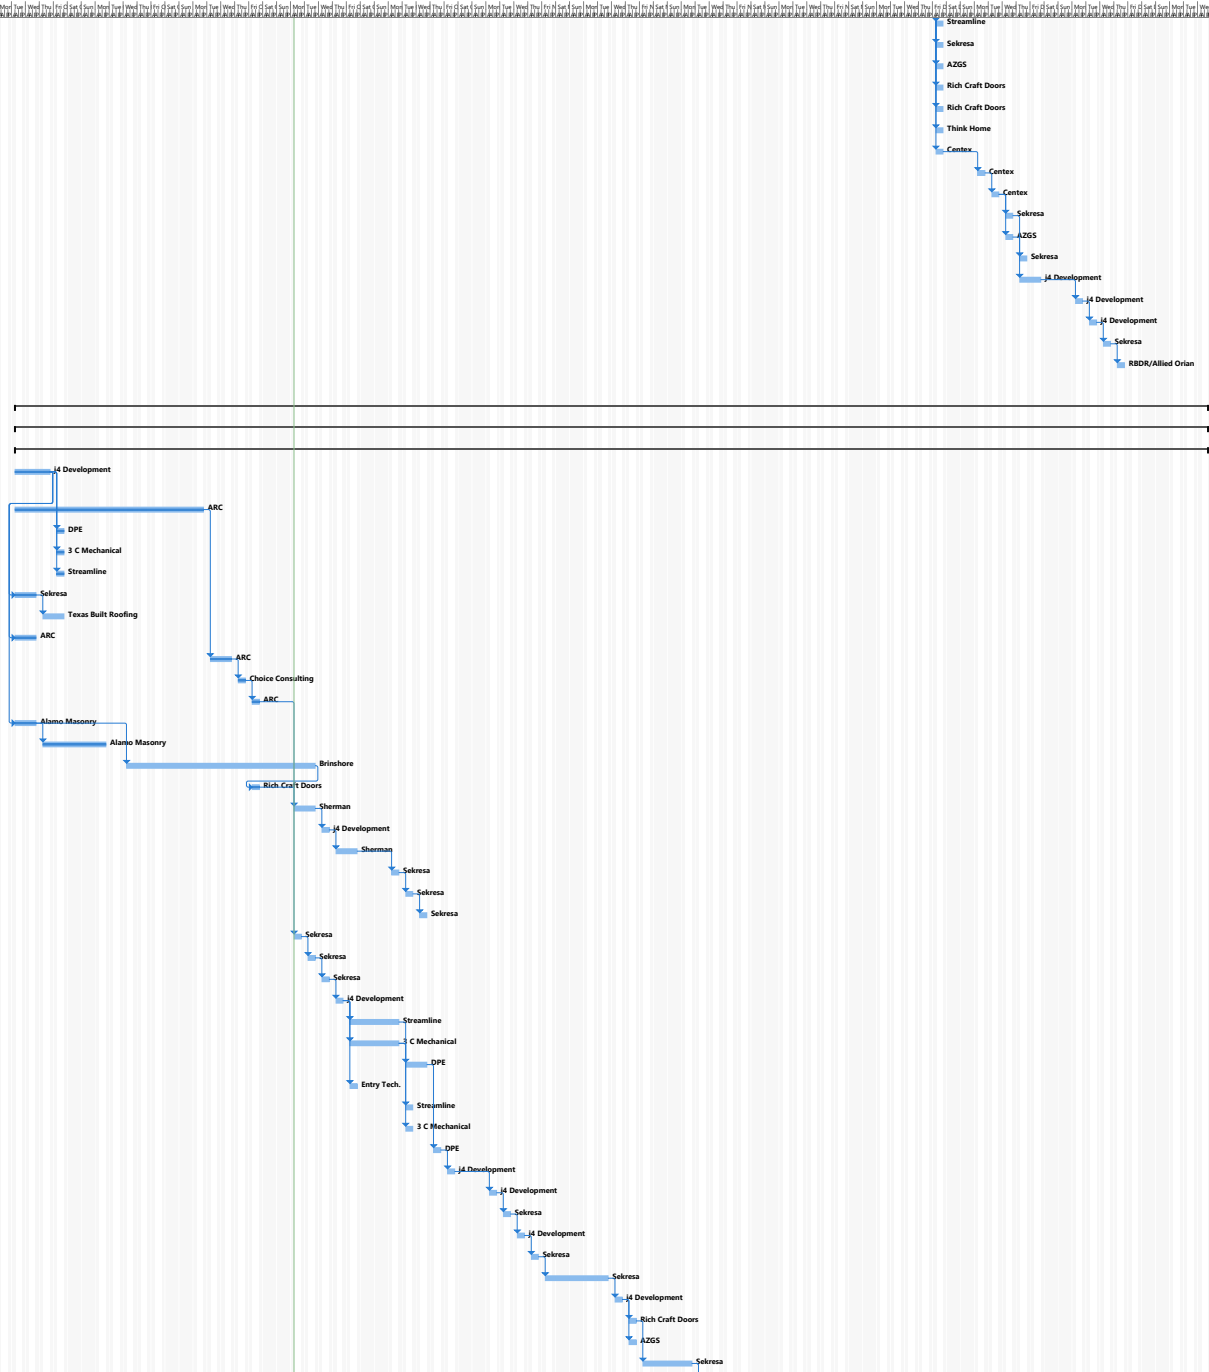

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
1151	Interior Finish Paint	3 days	Tue 11/16/21	Thu 11/18/21	1150	Sekresa	0%
1152	Install Cabinets	1 day	Fri 11/19/21	Fri 11/19/21	1151	AZGS	0%
1153	Field measure & cut Countertops	2 days	Mon 11/22/21	Tue 11/23/21	1152	Authentic Granite	0%
1154	Install Countertop	1 day	Wed 11/24/21	Wed 11/24/21	1153	Authentic Granite	0%
1155	Install Backsplash Tile	2 days	Thu 11/25/21	Fri 11/26/21	1154	Centex	0%
1156	Install Bathroom Floor Tile	2 days	Tue 11/16/21	Wed 11/17/21	1150	Centex	0%
1157	Trim out Electrical	2 days	Mon 11/29/21	Tue 11/30/21	1155	DPE	0%
1158	Trim out HVAC	2 days	Wed 12/1/21	Thu 12/2/21	1157	3 C Mechanical	0%
1159	Trim out Plumbing	2 days	Mon 11/29/21	Tue 11/30/21	1155	Streamline	0%
1160	Trim out Data	1 day	Wed 12/1/21	Wed 12/1/21	1157	Entry Tech.	0%
1161	Electrical Final Inspection	1 day	Wed 12/1/21	Wed 12/1/21	1157	DPE	0%
1162	HVAC Final Inspection	1 day	Fri 12/3/21	Fri 12/3/21	1158	3 C Mechanical	0%
1163	Plumbing Final Inspection	1 day	Wed 12/1/21	Wed 12/1/21	1159	Streamline	0%
1164	Install Bath Acc.	1 day	Wed 12/1/21	Wed 12/1/21	1159	Sekresa	0%
1165	Install Blinds	1 day	Wed 12/1/21	Wed 12/1/21	1159	AZGS	0%
1166	Install Interior Door Hardware	1 day	Wed 12/1/21	Wed 12/1/21	1159	Rich Craft Doors	0%
1167	Install Exterior Door Hardware	1 day	Wed 12/1/21	Wed 12/1/21	1159	Rich Craft Doors	0%
1168	Blow Insulation in Attic	1 day	Thu 12/2/21	Thu 12/2/21	1163	Think Home	0%
1169	Prep floors for LVT	2 days	Fri 12/3/21	Mon 12/6/21	1168	Centex	0%
1170	Install LVT	2 days	Tue 12/7/21	Wed 12/8/21	1169	Centex	0%
1171	Install Rubber Base	1 day	Thu 12/9/21	Thu 12/9/21	1170	Centex	0%
1172	Install Door Steps	1 day	Fri 12/10/21	Fri 12/10/21	1171	Sekresa	0%
1173	Install Appliances	1 day	Mon 12/13/21	Mon 12/13/21	1172	AZGS	0%
1174	Construction Clean Unit	1 day	Tue 12/14/21	Tue 12/14/21	1173	Sekresa	0%
1175	J4 Punch Walk	2 days	Wed 12/15/21	Thu 12/16/21	1174	J4 Development	0%
1176	J4 Punch Unit	1 day	Fri 12/17/21	Fri 12/17/21	1175	J4 Development	0%
1177	Building City Final Inspection	1 day	Mon 12/20/21	Mon 12/20/21	1176	J4 Development	0%
1178	Final Clean Unit	1 day	Tue 12/21/21	Tue 12/21/21	1177	Sekresa	0%
1179	Architect/Owner Turn Over Walk	1 day	Wed 12/22/21	Wed 12/22/21	1178	RBD/Allied Orion	0%
1180							
1181	Building 125	62 days	Tue 9/28/21	Wed 12/22/21			27%
1182	2612/2614 S. 14th St Type C	62 days	Tue 9/28/21	Wed 12/22/21			27%
1183	Receive possession of Unit	62 days	Tue 9/28/21	Wed 12/22/21	J4 Development		27%
1184	Walk unit to verify existing conditions & MEP systems are working	3 days	Tue 9/28/21	Thu 9/30/21	J4 Development		100%
1185	Submit 10 day abatement notice	10 days	Tue 9/28/21	Mon 10/11/21	ARC		100%
1186	Electrical Demo	1 day	Fri 10/1/21	Fri 10/1/21	1184	DPE	100%
1187	HVAC Demo	1 day	Fri 10/1/21	Fri 10/1/21	1184	3 C Mechanical	100%
1188	Plumbing Demo	1 day	Fri 10/1/21	Fri 10/1/21	1184	Streamline	100%
1189	Fascia Demo & Install New	2 days	Tue 9/28/21	Wed 9/29/21	1184	Sekresa	100%
1190	New Roof Demo & Install New	2 days	Thu 9/30/21	Fri 10/1/21	1189	Texas Built Roofing	0%
1191	Interior Soft Demo	2 days	Tue 9/28/21	Wed 9/29/21	1184	ARC	100%
1192	Abatement	2 days	Tue 10/12/21	Wed 10/13/21	1185	ARC	100%
1193	Air Test	1 day	Thu 10/14/21	Thu 10/14/21	1192	Choice Consulting	100%
1194	Remaining Demo Walls & Ceilings	1 day	Fri 10/15/21	Fri 10/15/21	1193	ARC	100%
1195	Point up Existing Brick	2 days	Tue 9/28/21	Wed 9/29/21	1184	Alamo Masonry	100%
1196	Install Exterior Stone	3 days	Thu 9/30/21	Mon 10/4/21	1195	Alamo Masonry	100%
1197	RFI #3 Rotted Cedar at Gables	10 days	Thu 10/7/21	Wed 10/20/21	1196/5+2 days	Brimshore	0%
1198	Install new front door with construction to	1 day	Fri 10/15/21	Fri 10/15/21	1197	Rich Craft Doors	100%
1199	Cedar Demo and/or building wrap install	2 days	Mon 10/18/21	Tue 10/19/21	1198	Sherman	0%
1200	Building Wrap Inspection	1 day	Wed 10/20/21	Wed 10/20/21	1199	J4 Development	0%
1201	Install Hardie Shake Siding	2 days	Thu 10/21/21	Fri 10/22/21	1200	Sherman	0%
1202	Install Hardie Soffit Board	1 day	Mon 10/25/21	Mon 10/25/21	1201	Sekresa	0%
1203	Prime Paint Building Exterior	1 day	Tue 10/26/21	Tue 10/26/21	1202	Sekresa	0%
1204	Finish Paint Building Exterior	1 day	Wed 10/27/21	Wed 10/27/21	1203	Sekresa	0%
1205	Install Smoke Barrier	1 day	Fri 10/22/21	Fri 10/22/21	1194/5+4 days	Sekresa	0%
1206	Install Interior Wall Framing	1 day	Mon 10/25/21	Mon 10/25/21	1205	Sekresa	0%
1207	Install in Wall Blocking	1 day	Tue 10/26/21	Tue 10/26/21	1206	Sekresa	0%
1208	J4 Frame Punch	1 day	Wed 10/27/21	Wed 10/27/21	1207	J4 Development	0%
1209	Install Plumbing R/	2 days	Thu 10/28/21	Fri 10/29/21	1208	Streamline	0%
1210	Install HVAC R/	2 days	Mon 11/1/21	Tue 11/2/21	1209	3 C Mechanical	0%
1211	Install Electrical R/	2 days	Wed 11/3/21	Thu 11/4/21	1210	DPE	0%
1212	Install Data R/	1 day	Fri 11/5/21	Fri 11/5/21	1211	Entry Tech.	0%
1213	Plumbing R/ Inspection	1 day	Mon 11/1/21	Mon 11/1/21	1209	Streamline	0%

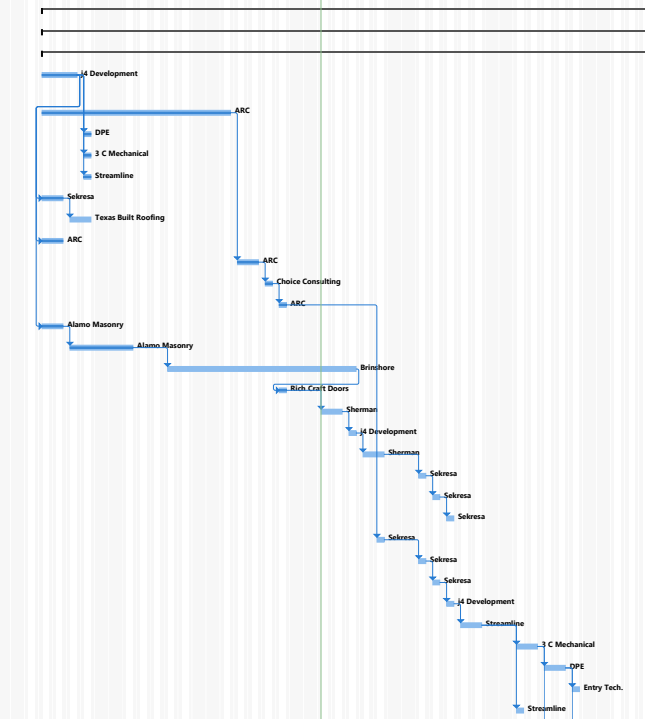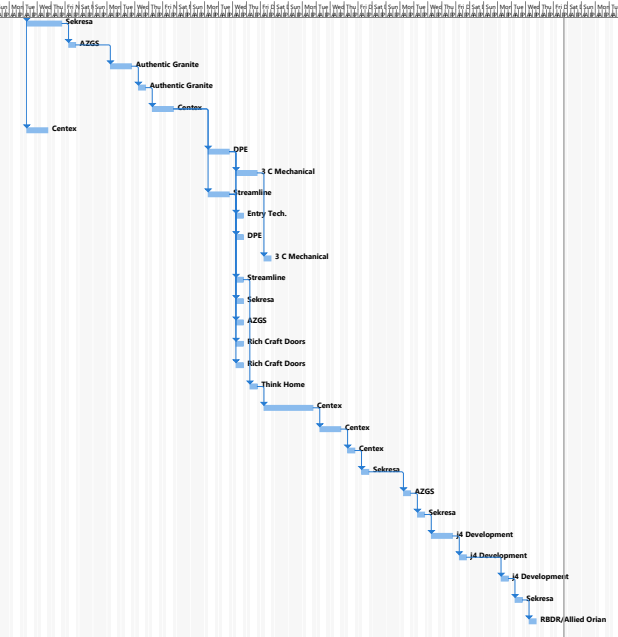

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
1214	HVAC R/I Inspection	1 day	Wed 11/3/21	Wed 11/3/21	1210	3 C Mechanical	0%
1215	Electrical R/I Inspection	1 day	Fri 11/5/21	Fri 11/5/21	1211	DPE	0%
1216	Smoke Barrier Inspection	1 day	Mon 11/8/21	Mon 11/8/21	1215	J4 Development	0%
1217	Wall Framing Inspection	1 day	Tue 11/9/21	Tue 11/9/21	1216	J4 Development	0%
1218	Install Batt Insulation	1 day	Wed 11/10/21	Wed 11/10/21	1217	Sekresa	0%
1219	Insulation Inspection	1 day	Thu 11/11/21	Thu 11/11/21	1218	J4 Development	0%
1220	Hang Drywall	1 day	Fri 11/12/21	Fri 11/12/21	1219	Sekresa	0%
1221	Skim Coat and/or TBT	3 days	Mon 11/15/21	Wed 11/17/21	1220	Sekresa	0%
1222	J4 Drywall Punch	1 day	Thu 11/18/21	Thu 11/18/21	1221	J4 Development	0%
1223	Install Interior Doors	1 day	Fri 11/19/21	Fri 11/19/21	1222	Rich Craft Doors	0%
1224	Install Closet Shelving	1 day	Mon 11/22/21	Mon 11/22/21	1223	AZGS	0%
1225	Interior Prime Paint	1 day	Tue 11/23/21	Tue 11/23/21	1224	Sekresa	0%
1226	Interior Finish Paint	2 days	Wed 11/24/21	Thu 11/25/21	1225	Sekresa	0%
1227	Install Cabinets	1 day	Fri 11/26/21	Fri 11/26/21	1226	AZGS	0%
1228	Field measure & cut Countertops	2 days	Mon 11/29/21	Tue 11/30/21	1227	Authentic Granite	0%
1229	Install Countertop	1 day	Wed 12/1/21	Wed 12/1/21	1228	Authentic Granite	0%
1230	Install Backsplash Tile	2 days	Thu 12/2/21	Fri 12/3/21	1229	Centex	0%
1231	Install Bathroom Floor Tile	2 days	Mon 12/6/21	Tue 12/7/21	1230	Centex	0%
1232	Trim out Electrical	2 days	Wed 12/8/21	Thu 12/9/21	1231	DPE	0%
1233	Trim out HVAC	2 days	Fri 12/10/21	Mon 12/13/21	1232	3 C Mechanical	0%
1234	Trim out Plumbing	2 days	Mon 12/6/21	Tue 12/7/21	1230	Streamline	0%
1235	Trim out Data	1 day	Fri 12/10/21	Fri 12/10/21	1232	Entry Tech.	0%
1236	Electrical Final Inspection	1 day	Fri 12/10/21	Fri 12/10/21	1232	DPE	0%
1237	HVAC Final Inspection	1 day	Tue 12/14/21	Tue 12/14/21	1233	3 C Mechanical	0%
1238	Plumbing Final Inspection	1 day	Wed 12/8/21	Wed 12/8/21	1234	Streamline	0%
1239	Install Bath Acc.	1 day	Wed 12/8/21	Wed 12/8/21	1234	Sekresa	0%
1240	Install Blinds	1 day	Wed 12/8/21	Wed 12/8/21	1234	AZGS	0%
1241	Install Interior Door Hardware	1 day	Wed 12/8/21	Wed 12/8/21	1234	Rich Craft Doors	0%
1242	Install Exterior Door Hardware	1 day	Wed 12/8/21	Wed 12/8/21	1234	Rich Craft Doors	0%
1243	Blow insulation in Attic	1 day	Wed 12/8/21	Wed 12/8/21	1234	Think Home	0%
1244	Prep floors for LVT	1 day	Mon 12/13/21	Mon 12/13/21	1235	Centex	0%
1245	Install LVT	1 day	Tue 12/14/21	Tue 12/14/21	1244	Centex	0%
1246	Install Rubber Base	1 day	Wed 12/15/21	Wed 12/15/21	1245	Centex	0%
1247	Install Door Stops	1 day	Thu 12/16/21	Thu 12/16/21	1246	Sekresa	0%
1248	Install Appliances	1 day	Thu 12/16/21	Thu 12/16/21	1246	AZGS	0%
1249	Construction Clean Unit	1 day	Fri 12/17/21	Fri 12/17/21	1247	Sekresa	0%
1250	J4 Punch Walk	2 days	Fri 12/17/21	Mon 12/20/21	1247	J4 Development	0%
1251	J4 Punch Lint	1 day	Tue 12/21/21	Tue 12/21/21	1250	J4 Development	0%
1252	Building City Final Inspection	1 day	Fri 12/17/21	Fri 12/17/21	1248	J4 Development	0%
1253	Final Clean Unit	1 day	Tue 12/21/21	Tue 12/21/21	1250	Sekresa	0%
1254	Architect/Owner Turn Over Walk	1 day	Wed 12/22/21	Wed 12/22/21	1253	RBD/Allied Orion	0%
1255							
1256	Building 194	69 days	Tue 9/14/21	Fri 12/17/21			26%
1257	204/205 Kennedy Type H	69 days	Tue 9/14/21	Fri 12/17/21			26%
1258	Receive possession of Unit	69 days	Tue 9/14/21	Fri 12/17/21		J4 Development	26%
1259	Walk unit to verify existing conditions & MEP systems are working	3 days	Tue 9/14/21	Thu 9/16/21		J4 Development	100%
1260	Submit 10 day abatement notice	10 days	Tue 9/14/21	Mon 9/27/21		ARC	100%
1261	Electrical Demo	1 day	Fri 9/17/21	Fri 9/17/21	1259	DPE	100%
1262	HVAC Demo	1 day	Fri 9/17/21	Fri 9/17/21	1259	3 C Mechanical	100%
1263	Plumbing Demo	1 day	Fri 9/17/21	Fri 9/17/21	1259	Streamline	100%
1264	Fascia Demo & Install New	2 days	Tue 9/14/21	Wed 9/15/21	1259	Sekresa	100%
1265	New Roof Demo & Install New	2 days	Thu 9/16/21	Fri 9/17/21	1264	Texas Built Roofing	0%
1266	Interior Soft Demo	2 days	Tue 9/14/21	Wed 9/15/21	1259	ARC	100%
1267	Abatement	2 days	Tue 9/28/21	Wed 9/29/21	1260	ARC	100%
1268	Air Test	1 day	Thu 9/30/21	Thu 9/30/21	1267	Choice Consulting	100%
1269	Remaining Demo Walls & Ceilings	3 days	Fri 10/1/21	Tue 10/5/21	1268	ARC	100%
1270	Paint up Existing Brick	2 days	Wed 10/13/21	Thu 10/14/21	1264	Alamo Masonry	100%
1271	Install Exterior Stone	3 days	Fri 10/15/21	Tue 10/19/21	1270	Alamo Masonry	100%
1272	Install new front door with construction in	1 day	Wed 10/20/21	Wed 10/20/21	1271	Rich Craft Doors	0%
1273	Cedar Demo and/or building wrap install	2 days	Thu 10/21/21	Fri 10/22/21	1272	Sherman	0%
1274	Building Wrap Inspection	1 day	Mon 10/25/21	Mon 10/25/21	1273	J4 Development	0%
1275	Install Hardie Shake Siding	2 days	Tue 10/26/21	Wed 10/27/21	1274	Sherman	0%
1276	Install Hardie Soffit Board	1 day	Thu 10/28/21	Thu 10/28/21	1275	Sekresa	0%

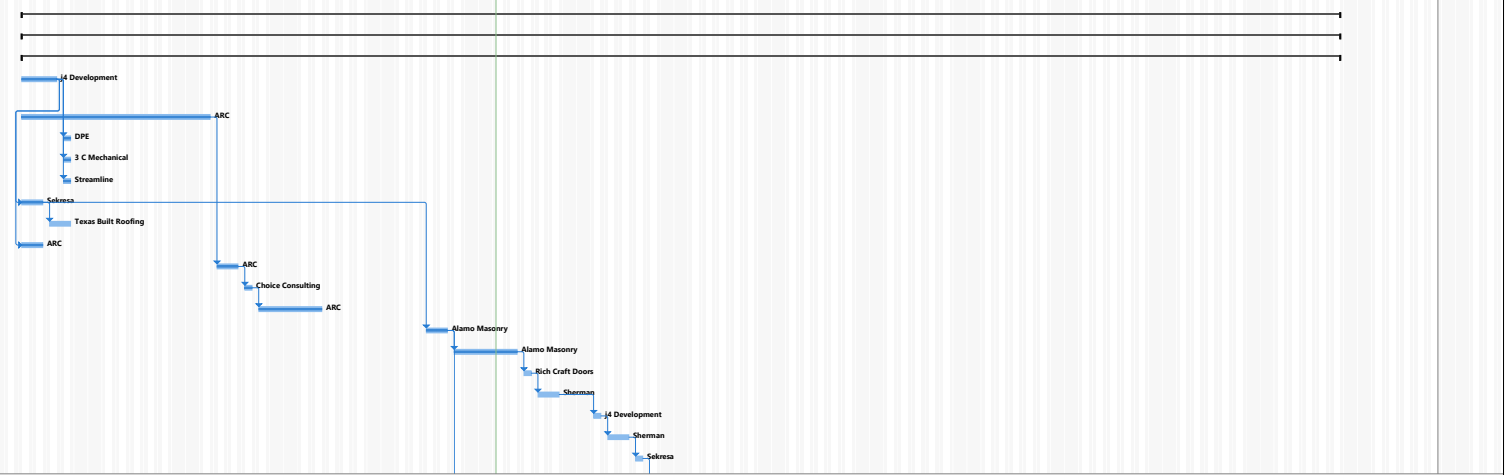

ID	Task	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
1277	Prime Paint Building Exterior	1 day	Fri 10/29/21	Fri 10/29/21	1276	Sekresa	0%	
1278	Finish Paint Building Exterior	1 day	Mon 11/1/21	Mon 11/1/21	1277	Sekresa	0%	
1279	Pressure Wash Existing CMU	1 day	Fri 10/15/21	Fri 10/15/21	1270	Sekresa	0%	
1280	Install Vapor Barrier	2 days	Mon 10/18/21	Tue 10/19/21	1279	Sekresa	0%	
1281	Install Foam Insulation	1 day	Wed 10/20/21	Wed 10/20/21	1280	Sekresa	0%	
1282	Install Metal Strapping	1 day	Thu 10/21/21	Thu 10/21/21	1281	Sekresa	0%	
1283	Install Ceiling Hat Channel	1 day	Fri 10/22/21	Fri 10/22/21	1282	Sekresa	0%	
1284	Install Smoke Barrier	1 day	Fri 10/15/21	Fri 10/15/21	1270	Sekresa	0%	
1285	Install Interior Wall Framing	1 day	Fri 10/22/21	Fri 10/22/21	1282	J4 Development	0%	
1286	Install in Wall Blocking	1 day	Mon 10/25/21	Mon 10/25/21	1285	Sekresa	0%	
1287	J4 Frame Punch	1 day	Tue 10/26/21	Tue 10/26/21	1286	Sekresa	0%	
1288	Install Plumbing R/I	2 days	Wed 10/27/21	Thu 10/28/21	1287	Streamline	0%	
1289	Install HVAC R/I	2 days	Fri 10/29/21	Mon 11/1/21	1288	3 C Mechanical	0%	
1290	Install Electrical R/I	2 days	Tue 11/2/21	Wed 11/3/21	1289	DPE	0%	
1291	Install Data R/I	1 day	Thu 11/4/21	Thu 11/4/21	1290	Entry Tech.	0%	
1292	Plumbing R/I Inspection	1 day	Fri 10/29/21	Fri 10/29/21	1288	Streamline	0%	
1293	HVAC R/I Inspection	1 day	Mon 11/1/21	Mon 11/1/21	1289	3 C Mechanical	0%	
1294	Electrical R/I Inspection	1 day	Tue 11/2/21	Tue 11/2/21	1293	DPE	0%	
1295	Smoke Barrier Inspection	1 day	Wed 11/3/21	Wed 11/3/21	1294	J4 Development	0%	
1296	Wall Framing Inspection	1 day	Thu 11/4/21	Thu 11/4/21	1295	J4 Development	0%	
1297	Install Batt Insulation	1 day	Fri 11/5/21	Fri 11/5/21	1296	Sekresa	0%	
1298	Insulation Inspection	3 days	Mon 11/8/21	Wed 11/10/21	1297	J4 Development	0%	
1299	Hang Drywall	3 days	Thu 11/11/21	Mon 11/15/21	1298	Sekresa	0%	
1300	Skim Coat and/or T&T	2 days	Tue 11/16/21	Wed 11/17/21	1299	Sekresa	0%	
1301	J4 Drywall Punch	1 day	Thu 11/18/21	Thu 11/18/21	1300	J4 Development	0%	
1302	Install Interior Doors	1 day	Fri 11/19/21	Fri 11/19/21	1301	Rich Craft Doors	0%	
1303	Install Closet Shelving	1 day	Mon 11/22/21	Mon 11/22/21	1302	AZGS	0%	
1304	Interior Prime Paint	3 days	Tue 11/23/21	Thu 11/25/21	1303	Sekresa	0%	
1305	Interior Finish Paint	1 day	Fri 11/26/21	Fri 11/26/21	1304	Sekresa	0%	
1306	Install Cabinets	1 day	Mon 11/29/21	Mon 11/29/21	1305	AZGS	0%	
1307	Field measure & cut Countertops	2 days	Mon 11/29/21	Tue 11/30/21	1305	Authentic Granite	0%	
1308	Install Countertop	1 day	Tue 11/30/21	Tue 11/30/21	1306	Authentic Granite	0%	
1309	Install Backsplash Tile	2 days	Wed 12/1/21	Thu 12/2/21	1307	Centex	0%	
1310	Install Bathroom Floor Tile	3 days	Wed 12/1/21	Fri 12/3/21	1308	Centex	0%	
1311	Trim out Electrical	2 days	Fri 12/3/21	Mon 12/6/21	1309	DPE	0%	
1312	Trim out HVAC	2 days	Tue 12/7/21	Wed 12/8/21	1311	3 C Mechanical	0%	
1313	Trim out Plumbing	2 days	Mon 12/6/21	Tue 12/7/21	1310	Streamline	0%	
1314	Trim out Data	1 day	Tue 12/7/21	Tue 12/7/21	1311	Entry Tech.	0%	
1315	Electrical Final Inspection	1 day	Tue 12/7/21	Tue 12/7/21	1311	DPE	0%	
1316	HVAC Final Inspection	1 day	Thu 12/9/21	Thu 12/9/21	1312	3 C Mechanical	0%	
1317	Plumbing Final Inspection	1 day	Wed 12/8/21	Wed 12/8/21	1313	Streamline	0%	
1318	Install Bath Acc.	1 day	Wed 12/8/21	Wed 12/8/21	1313	Sekresa	0%	
1319	Install Blinds	1 day	Wed 12/8/21	Wed 12/8/21	1313	AZGS	0%	
1320	Install Interior Door Hardware	1 day	Wed 12/8/21	Wed 12/8/21	1313	Rich Craft Doors	0%	
1321	Install Exterior Door Hardware	1 day	Wed 12/8/21	Wed 12/8/21	1313	Rich Craft Doors	0%	
1322	Blow Insulation in Attic	1 day	Wed 12/8/21	Wed 12/8/21	1313	Think Home	0%	
1323	Prep floors for LVT	1 day	Wed 12/8/21	Wed 12/8/21	1313	Centex	0%	
1324	Install LVT	2 days	Thu 12/9/21	Fri 12/10/21	1323	Centex	0%	
1325	Install Rubber Base	1 day	Mon 12/13/21	Mon 12/13/21	1324	Centex	0%	
1326	Install Door Stops	1 day	Tue 12/14/21	Tue 12/14/21	1325	Sekresa	0%	
1327	Install Appliances	1 day	Tue 12/14/21	Tue 12/14/21	1325	AZGS	0%	
1328	Construction Clean Unit	1 day	Wed 12/15/21	Wed 12/15/21	1327	Sekresa	0%	
1329	J4 Punch Walk	1 day	Wed 12/15/21	Wed 12/15/21	1327	J4 Development	0%	
1330	J4 Punch Unit	2 days	Thu 12/16/21	Fri 12/17/21	1329	J4 Development	0%	
1331	Building City Final Inspection	1 day	Wed 12/15/21	Wed 12/15/21	1327	J4 Development	0%	
1332	Final Clean Unit	1 day	Thu 12/16/21	Thu 12/16/21	1329	Sekresa	0%	
1333	Architect/Owner Turn Over Walk	1 day	Fri 12/17/21	Fri 12/17/21	1332	RBD/Allied Orion	0%	

